



CONTRACT DOCUMENTS

VOLUME I

PWC2324064

FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

ISSUED FOR BID

March 4, 2024

Fayetteville Public Works Commission Administrative Building 955 Old Wilmington Road Fayetteville, NC 28301

WK Dickson & Co, Inc. 720 Corporate Center Drive Raleigh, NC 27607 (910) 256-5651 NC License F-0374

TABLE OF CONTENTS

SECTION A - PROJECT SPECIFICS

General

Advertisement for Bids

00100 - Instructions to Bidders

Bid Submittal Documents

Bid Schedule - Performance and Delivery

Bid Checklist

00300 – Bid Pricing Form

Technical Evaluation Criteria Form

Bid Supplemental Forms and Attachments

Minority, Women, Disadvantaged Business Enterprise (MWDBE) Program

MWDBE Program Forms

SLS/MWDBE Disclosure Form

SECTION B - CONTRACT EXECUTION DOCUMENTS

Notice of Award

Acceptance of Award

Construction Agreement

PWC General Conditions

Contract Supplemental Forms and Attachments

Notice to Proceed

SECTION C - ADMINISTRATIVE PROVISIONS

DIVISION 1 – GENERAL REQUIREMENTS

01000 - Supplementary Conditions

01025 – Measurement and Payment

01300 – Submittals

01310 - Construction Schedule

01400 - Quality Control

01700 - Project Closeout

SECTION D - TECHNICAL SPECIFICATIONS

DIVISION 2 – SITE WORK

02000 - Special Provisions

02110 - Site Clearing

02211 - Grading, Utilities

02222 - Excavation and Backfilling for Utility Systems rev 1.1.16

02272 - Erosion Control - General Provisions

02273 - Temporary Silt Fence

02274 - Gravel Construction Entrance/Exit

02275 - Block and Gravel Inlet Protection rev 7.1.10

02301 - Boring and Jacking

02302 - HDD rev 8.5.15

02350 - Steel H Piles

02500 - Traffic Control

02505 - Adjustment of Existing Structures rev 1.1.17

02573 - Permanent Pavement Patch rev 1.1.17

02574 - Temporary Pavement Patch (Type I-19.0C)


02575 - Driveway Replacement


02584 - Roadway and Parking Lot Marking

- 02660 Water Distribution rev 12.10.19
- 02662 Fire Hydrant Painting
- 02730 Sanitary Sewer System rev 1.1.16
- 02732 Sewage Force Mains rev 6.1.18
- 02737 DIP for HDD rev 8.5.15
- 02831 Chain Link Fencing
- 02931 Lawns and Grasses (Sodding)
- 02933 Lawns and Grasses (Seeding)
- 02934 Seeding Wetlands
- 03301 Concrete Construction (Utility)
- 09801 Anti-Microbial Additive rev 1.1.17
- 09802 Special Coatings (Ceramic Epoxy)
- 09804 Special Coatings (Epoxy Lining Ductile Iron Pipe and Fittings rev 3.31.15

APPENDICES

- Appendix A Aqua America Specifications -
- Appendix B Lateral Relocation Release Form -
- Appendix C Claims Form
- Appendix D Structural Survey
- Appendix E Letter of Approval, Erosion & SC Narrative
- Appendix F Geotechnical Report
- Appendix G Easement Special Requirements

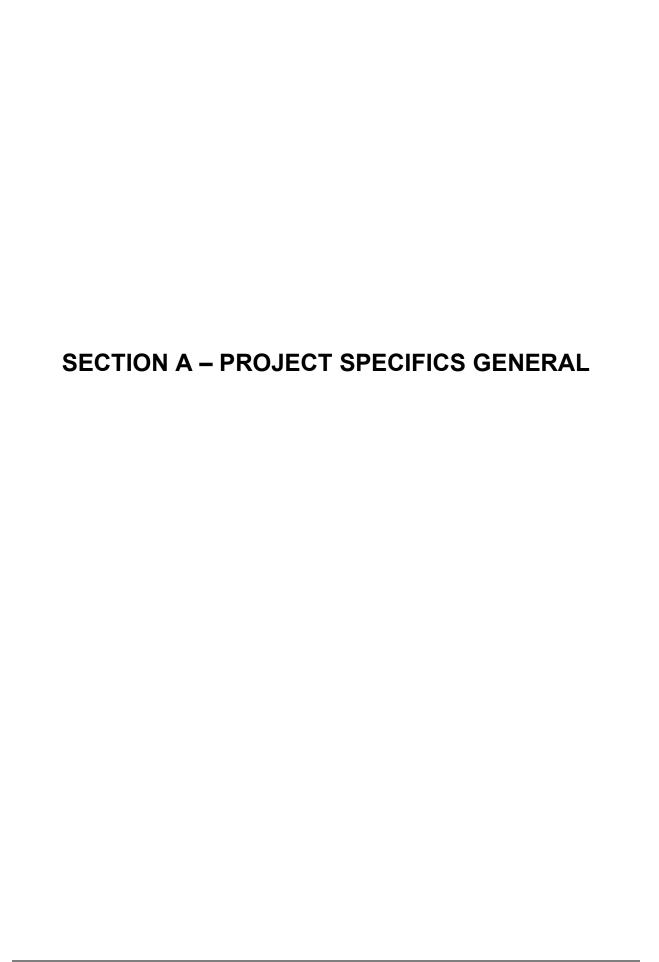

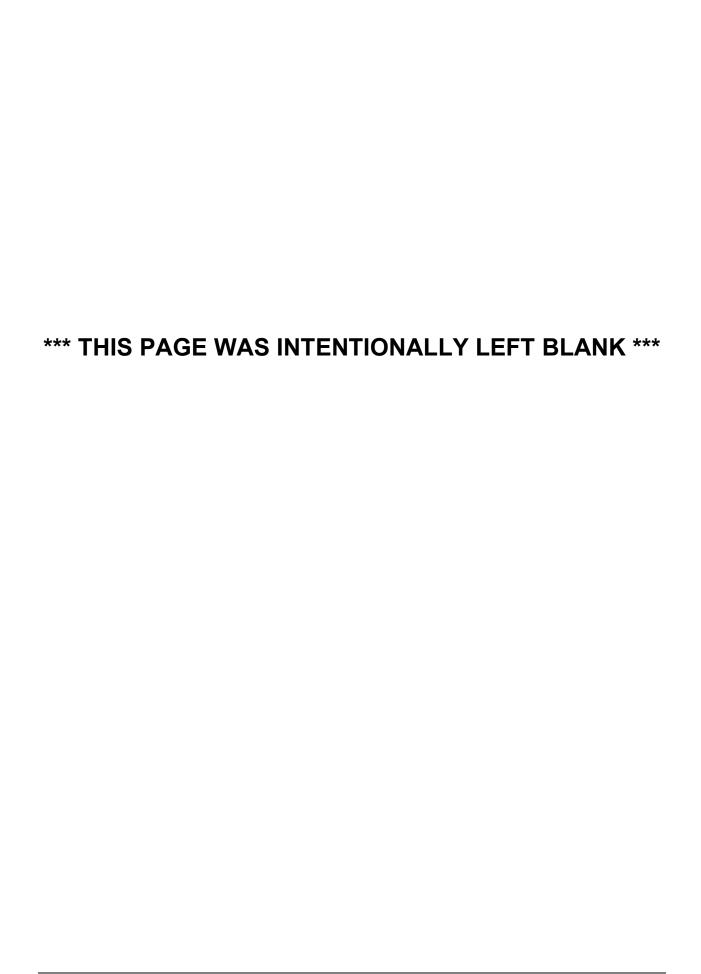

ADVERTISEMENT FOR BID FAYETTEVILLE PUBLIC WORKS COMMISSION FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

Cumberland County North Carolina

Pursuant to N.C.G.S 143-129, sealed bids are solicited and will be received at Fayetteville Public Works Commission, Administration Building, Conference Room 107, 955 Old Wilmington Road, Fayetteville, NC 28301, until **2:00 p.m., EST Thursday, March 28, 2024**, at which time they will be publicly opened and read.

The project will consist of installing approximately 77 manholes, 225 sanitary sewer laterals, 14,657 linear feet of 8-inch gravity sewer, and approximately 370 linear feet of bore/jack and 110 linear feet of aerial crossings. This project requires stream crossings, stream bank stabilization, trenchless construction, aerial crossings, post-inspection of the completed gravity sewer and all other items necessary to provide a complete project.

The foregoing description shall not be construed as a complete description of all work required. All work shall be done in accordance with PWC technical specifications and standard contract terms.

A MANDATORY pre-bid meeting will be held at 11:00 a.m., EST Tuesday, March 12, 2024, via web conference. All potential bidders must email Tanya Hazlett, Procurement Advisor at procurement@faypwc.com of their intent to attend, and to be added to the meeting ID: 296 580 015 006. Potential bidders will have the ability to join the virtual meeting via phone at: (910) 302-6113 with Phone Conference ID 261 453 490# and/or via Microsoft Teams. It is encouraged to utilize Microsoft Teams as this pre-bid meeting may contain a presentation of plans and an agenda. Should you need assistance accessing Microsoft Teams via web, smart phone, or tablet, please contact Tanya Hazlett via email at the email address listed above.

Questions will be fielded at the pre-bid meeting and all prospective bidders are required to attend the meeting. Individual telephone inquiries are prohibited. PWC assumes no responsibility to fully inform absentees of clarifications not issued by addendum.

Bids must be enclosed in a sealed envelope addressed to Tanya Hazlett, Procurement Advisor, Fayetteville Public Works Commission, 955 Old Wilmington Road, Fayetteville, North Carolina 28301. The outside of the envelope must be marked **SEALED BID: FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST** and shall indicate the name, address and state license number of the bidder. Bids shall be submitted on the printed forms, or exact copies thereof, contained in the Contract Documents.

Each bid shall be accompanied by a bid bond of five percent (5%) of the bid executed by a surety company licensed under the laws of North Carolina to execute the Contract in accordance with the bid bond and upon failure to forthwith make payment, the surety shall pay the obligee an amount equal to the amount of said bond. Said deposit shall be retained by the Owner as liquidated damages in event of failure of the successful bidder to execute the Contract within ten (10) days after the Notice of Award or give satisfactory surety as required by law.

Performance and Payment Bonds are required in the amount of 100% of the Contract amount and shall be furnished by the Contractor.

All Contractors are notified that North Carolina Statutory provisions as to licensing of Contractors will be followed as applicable in receiving and evaluating bids and in reading and awarding the Contract (Chapter 87 of the North Carolina General Statutes).

The license classification shall be:

Part 1: Public Utilities (Water and Sewer) - Unlimited
Unclassified - Unlimited

Plans and Specifications including Contract Documents will be available online for viewing and downloading on or about Friday, March, 1, 2024 on the PWC Procurement website at https://www.faypwc.com/purchasing. In addition, the documents will be available from the Fayetteville State University Construction Resource Office (FSU CRO) https://www.uncfsu.edu/academics/colleges-schools-and-departments/broadwell-college-ofbusiness-and-economics/outreach-centers/construction-resource-office. In collaboration with the North Carolina Institute of Minority Economic Development, the FSU CRO offers services and support to help small, minority, veteran, and women-owned businesses identify and compete for construction-related projects.

At the FSU CRO, potential bidders may:

- Research, view and print project drawings to scale free of charge;
- · Use available software to prepare their bid; and
- Receive certification and pre-qualification assistance.

Please email the FSU CRO to make an appointment: fsucro@uncfsu.edu

Plans and Specifications are also being furnished to ISQFT (www.isqft.com) for online posting. Purchase of the documents is not required to bid.

Fayetteville Public Works Commission reserves the right to reject any or all bids for any reason determined by PWC to be in its best interest, or to award the bid to the lowest responsible bidder or bidders, taking into consideration quality, performance, and the time specified in the bids for the performance of the contract.

The bidder to whom the contract may be awarded must comply fully with the requirements of North Carolina General Statutes Section 143-129, as amended.

No bids may be withdrawn after the scheduled Bid Opening for a period of ninety (90) calendar days.

FAYETTEVILLE PUBLIC WORKS COMMISSION Victoria McAllister Procurement Manager

00100 - INSTRUCTIONS TO BIDDERS FAYETTEVILLE PUBLIC WORKS COMMISSION FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

A. DEFINED TERMS

Terms used in these Instructions to Bidders are defined in the Definitions and Terminology sections of PWC General Conditions.

B. COPIES OF BIDDING DOCUMENTS

- 1. Complete sets of the Bidding Documents as stated in the Invitation to Bidders, may be obtained from the PWC Procurement Department.
- Complete sets of Bidding Documents shall be used in preparing Bids. PWC assumes no responsibility for errors or misinterpretations resulting from the use of incomplete sets of Bidding Documents.

C. EXAMINATION OF CONTRACT DOCUMENTS, OTHER RELATED DATA, AND PROJECT SITE

- 1. Before submitting a Bid, each Bidder shall (a) examine the Contract Documents thoroughly, (b) visit the site and become familiar with the site and any local conditions that may in any manner affect the cost, progress, or performance of the Work, (c) be familiar with federal, state and local laws, ordinances, rules and regulations that may in any manner affect cost, progress or performance of the Work, and (d) study and carefully correlate Bidder's observations with the Contract Documents, and (e) give the PWC Procurement Advisor written notice of all conflicts, errors ordiscrepancies in the Contract Documents.
- 2. Bidders should consult the Specifications for the identification of those reports of investigations and tests of subsurface and latent physical conditions at the site or reports that otherwise may affect cost, progress, or performance of the Work which may have been utilized in the preparation of the Drawings and Specifications. PWC will make copies of such reports if available at the cost (non-refundable) of reproduction to any Bidder requesting them. These reports are not intended to constitute any explicit or implicit representation as to the nature of the subsurface and latent physical conditions, which may be encountered at the site or to constitute explicit or implicit representations as to any other matter, contained in any report. Such reports are not guaranteed as to accuracy or completeness and are not part of the Contract Documents. Before submitting a Bid, each Bidder will, at its own expense, make such investigations and tests as the Bidder may deem necessary to determine his Bid for the performance of the Work in accordance with the Contract Documents.
- On request (minimum 48 hours advance notice), PWC will provide each Bidder access to the site to conduct such investigations and tests, as each Bidder deems necessary for submission of its Bid.
- 4. The lands upon which the Work is to be performed, right-of-way for access thereto, and other lands available for use by the Contractor in performing the Work are identified in the

Contract Documents.

5. The submission of a Bid constitutes an incontrovertible representation by the Bidder that it has complied with every requirement of this Section and that the Contract Documents are sufficient in scope and detail to indicate and convey an understanding of all terms and conditions for the performance of the Work.

D. INTERPRETATIONS AND ADDENDA

1. All questions about the meaning or intent of the bid or Contract Documents shall be submitted in writing to Tanya Hazlett, Procurement Advisor, by email to procurement@faypwc.com. In order to receive consideration, questions must be received by Friday, March, 15, 2024 and time 5:00 p.m. Any interpretations of questions so raised, which in the opinion of the Project Engineer require interpretations, will be issued by Addenda via email or posted online by the Owner and/or Project Engineer. An Addendum extending the Bid Opening date may be issued up to five (5) business days before the Bid Opening date. An Addendum withdrawing the Invitation for Bid may be issued any time prior to the Bid Opening date. The Owner and Project Engineer will not be responsible for oral interpretations or clarifications, which anyone presumes to make on their behalf.

Bidders are expressly prohibited from contacting any PWC official or employee associated with this project, except as noted above. Violation of this prohibition is grounds for the immediate disqualification of the bidder.

- PWC may issue such additional Addenda as may be necessary to clarify, correct, or change the Contract Documents. Such Addenda, if any, will be issued in the manner and within the time stated in Paragraph 1 of this Section.
- 3. Each Bidder shall be responsible for determining that all Addenda issued by PWC have been received before submitting a Bid for the Work.
- 4. Each Bidder shall acknowledge the receipt of each Addendum on the Bid Form.

E. SUBSTITUTE MATERIAL AND EQUIPMENT

The Contract, if awarded, will be on the basis of material and equipment described in the Drawings orrequired in the Specifications without consideration of possible substitute or "orequal" items. The procedure for submittal of substitute or "or-equal" items for consideration is set forth in the PWC General Conditions.

F. CONTRACTOR'S LICENSE

- 1. No General Contractor shall engage in contracting work in the State of North Carolina unless it has been licensed under in accordance with North Carolina law.
- 2. Bidders are prohibited from contracting for, or bidding upon, the construction, removal, repair or improvements to or upon real property owned, controlled or leased by Fayetteville Public Works Commission without a North Carolina Contractor's License.
- 3. Each bidder shall indicate its North Carolina Contractor's License number on the bid envelope and the Bid Form.
- 4. License Classification shall be:

Public Utilities Water and Sewer: UnlimitedUnclassified: Unlimited

G. SUBCONTRACTORS

1. Contractor shall subcontract no more than 49 percent (49%) of the value of the Contract.

- 2. Each Bidder shall submit to PWC with its bid the List of Subcontractors, Suppliers, other persons, and organizations proposed for those portions of the Work for which such identification is required. If PWC, after due investigation has reasonable objection to any proposed Subcontractor, Supplier, other person or organization, PWC may, before Notice of Award is given, request apparent Successful Bidder to submit an acceptable substitute without an increase in the Bid.
- 3. If the apparent Successful Bidder declines to make such a substitution, PWC may award the Contract to the next lowest responsive, responsible Bidder that proposes to use acceptable Subcontractors, Suppliers, and other persons, and organizations. The declining to make requested substitutions will not constitute grounds for sacrificing the bid security of any Bidder. If PWC does not make written objection to a Bidder's list of Subcontractors, Suppliers, other persons, or organizations prior to giving Notice of Award, the list will be considered acceptable, subject to revocation as provided in the PWC General Conditions.

H. MINORITY, WOMEN, DISADVANTAGED BUSINESS ENTERPRISE (MWDBE) PROGRAM / SMALL LOCAL SUPPLIER (SLS) PROGRAM

- 1. PWC is committed to promoting the utilization of Minority, Women, and Disadvantaged Businesses in PWC's geographical statistical area (GSA) by providing equal opportunity for participating in all aspects of PWC's contracting and procurement programs. The GSA consists of NCDOT division areas 3-8, and 10. PWC is also committed to promoting the utilization of small, local businesses in the Fayetteville Metropolitan Statistical Area (MSA) by increasing opportunities for those businesses to participate in PWC procurements. The MSA consists of Cumberland County, Hoke County, and Harnett County.
- 2. PWC requires Bidders to report efforts to utilize Minority, Women, and Disadvantaged Business Enterprises (MWDBEs) and Historically Underutilized Businesses (HUBs) for specific projects and requires all Bidders to report all such efforts for MWDBEs, HUBs, and Small Local Suppliers regardless of the requirements of a specific project. Bidders shall document any good-faith efforts and utilization in the MWDBE forms provided within the Contract Documents.
- 3. NCDOT Disadvantaged Business Enterprise (DBE) and NC Department of Administration (DOA) Historically Underutilized Business (HUB) firms with current certifications are acceptable for listing in the bidder's submittal of MWDBE participation and will be considered to meet any necessary contract goal. Firms that are certified through NCDOT are listed in the "Vendor Directory" which can be accessed through the following: https://www.ebs.nc.gov/VendorDirectory/default.html. Firms that are certified through NC DOA are listed at the "Vendor Search" which can be accessed through the following link: https://evp.nc.gov/vendors/vendorsearchadvanceform/?id=d98aa5d6-0d57-ee11-be6e-

001dd804e775.

4. Bidders shall submit, with their bid, the MWDBE documentation required in the Contract Documents. The Bidder is strongly recommended to attend the Pre-Bid Meeting, as important information will be reviewed.

I. SUBMISSION OF BIDS

- 1. All Bidders shall use the enclosed Bid Forms, or exact copies thereof, in submitting their bid prices. PWC will not accept oral Bids or Bids received by telephone, email, or telecopier (FAX machine) for this Bid.
- 2. All prices must be F.O.B. delivered to the point as indicated by this Bid. PWC will grant no allowance for boxing, crating, or delivery unless specifically provided for in this Bid.
- 3. The Bid Form must be completed in black ink. Black or blue pen ink is acceptable if handwritten. Discrepancies between amounts shown in words and amounts shown in figures will be resolved in favor of the amounts shown in words. Discrepancies in the multiplication of units of Work and the unit prices will be resolved in favor of the correct multiplication of the unit prices. Discrepancies between the indicated sum of any column of figures and the correct sum thereof will be resolved in favor of the correct sum.
- 4. Bid submittals sent by mail should be registered mail. The sealed Bid, marked as indicated above, should be enclosed in an additional sealed envelope similarly marked and addressed to:

Fayetteville Public Works Commission Attn: Tanya Hazlett, Procurement Advisor 955 Old Wilmington Road Fayetteville, North Carolina 28301

- 5. Mark the envelope in the lower left-hand corner with the project title, hour and due date of Bid, and the Bidder's North Carolina contractor registration number.
- 6. Bids sent by mail and arriving after the time for the opening of Bids shall not be considered valid Bids. In such instances, the Bidders shall have no claim against PWC.
- 7. All items contained in the Bid Checklist shall be completely filled out and submitted with the bid. Failure to submit any of the items requested with the Bid Form may be just cause for rejection of the Bid by PWC.
- 8. All erasures, insertions, additions, and other changes made by the Bidder to the Bid Form shall be signed or initialed by the Bidder. Bids containing any conditions, omissions, erasures, alterations, or items not called for in the Bid, may be rejected by PWC as being incomplete or nonresponsive.
- 9. The Bid Form must be signed in order to be considered. If the Bidder is a corporation, the Bid must be submitted in the name of the corporation, not simply the corporation's trade name. In addition, the Bidder must indicate the corporate title of the individual signing the Bid.

- 10. The Bid Form, the Bid security, if any, and any other documents required, shall be enclosed in a sealed opaque envelope. Any notation or notations on the exterior of the envelope purporting to alter, amend, modify, or revise the bid contained within the envelope shall be of no effect and shall be disregarded.
- 11. All Bids received in the Procurement Department by the deadline indicated will be kept sealed until the time and date of the Bid Opening.
- 12. All late Bids shall be returned unopened to the sender.

J. BID BOND

- 1. Each Bid shall be accompanied by an acceptable Bid bond in the amount of five percent (5%) of the Bid amount, and made payable to Fayetteville Public Works Commission, North Carolina.
- 2. The Bid bond is a guarantee that if the contract is awarded by PWC to the Bidder, the Bidder shall enter into the contract with PWC for the work mentioned in this Bid or forfeit the Bid bond to PWC, not as a penalty, but as liquidated damages.
- 3. No forfeiture under a Bid bond shall exceed the lesser of (a) the difference between the Bid forwhich the Bid bond was written and the next low Bid of another Bidder, or (b) the face amount of the Bid bond.
- 4. All bonds shall be executed by a surety company selected by the Bidder, which is legally authorized to do business in the State of North Carolina (NCGS §44 A-26), and the bond shall be the same in both form as well as substance as AIA Document A310, Bid Bond.
- 5. The Bidder shall require the attorney-in-fact, who executed the required bond on behalf of the surety company, to affix thereto a certified and current copy of the power of attorney.
- 6. The bond premium shall be paid by the Bidder and the cost shall be included in the Bid price.
- 7. Any inspection of procurement transaction records shall be subject to reasonable restrictions to ensure the security and integrity of the records.

K. OPENING OF BIDS

- 1. Bids will be opened publicly and read aloud on the date and time set for the Bid Opening in the Notice to Bidders.
- 2. Any Bidder, upon request, shall be afforded the opportunity to inspect Bid records within a reasonable time after the opening of all Bids but prior to award, except in the event that PWC decides not to accept any of the Bids and to reopen the contract. Otherwise, bid records shall be open to public inspection only after the award of the Contract.
- 3. Any inspection of procurement transaction records shall be subject to reasonable restrictions to ensure the security and integrity of the records.

L. MODIFICATION OF BIDS

1. A Bid may be modified or withdrawn by the Bidder at any time prior to the time and date

- set for the Bid Opening. The Bidder shall notify the PWC Procurement Department in writing of its intentions.
- 2. Modified and withdrawn Bids may be resubmitted to the PWC Procurement Department up to the time and date set for the Bid Opening.

M. WITHDRAWAL OF BID DUE TO ERROR

 If the Bidder desires to withdraw its Bid, the Bidder must do so before the time fixed for the opening, without prejudice, by communicating its purpose in writing to PWC. After bids are open, bids may only be withdrawn in strict accordance with N.C.G.S. Section 143-129-1

N. BIDS TO REMAIN OPEN

1. All Bids shall remain open for ninety (90) calendar days after the day of the Bid Opening.

O. ESTIMATED QUANTITIES

- 1. The estimated quantities contained herein in certain items in the Bid are for the purpose of comparing bids, and while they are believed to be close approximations, they are not guaranteed, and settlement will be made on the basis of the work as actually executed at the unit prices in the Bid as accepted. PWC further reserves the right to delete any single line item or combination of items from the bid and cannot guarantee that all quantities listed in the Contract Documents will be utilized.
- 2. The Contractor should verify quantities before submitting a bid. Due to conditions that may be found under pavement such as the accurate location of existing water lines, sewer lines, gas lines, and structure services of all types, quantities are subject to change during construction, but this contingency shall not be used for a claim to change unit prices submitted in the Bid.

P. AWARD OF CONTRACT

- PWC reserves the right to reject any and all Bids, to waive any and all informalities, and
 to disregard all nonconforming, nonresponsive, or conditional Bids. PWC reserves the
 right to request additional information from any or all bidders for evaluation purposes.
 Failure or refusal to furnish additional information as requested may result in the rejection
 of the bid.
- 2. In case of a tie Bid, the tie shall be decided by lot.
- 3. It is the intent of PWC to recommend the award of this contract to the lowest responsive, responsible Bidder provided the Bid has been submitted in accordance with the requirements of the Bidding Documents and does not exceed the funds available. In determining the lowest responsible Bidder, PWC may consider, among other criteria, the Bidder's past performance conduct on other contracts, and other information provided by the Bidder as noted below.
- 4. In determining the lowest responsive Bidder, PWC will evaluate the Bidder's proposed Bid price and the completeness of the submitted bid in accordance with the requirements of the Contract Documents.

- 5. PWC may consider the operating costs, maintenance considerations, performance date, and guarantees of materials and equipment.
- 6. PWC may conduct such investigations as deemed necessary to assist in the evaluation of any Bid and to establish the responsibility, qualifications and financial ability of the Bidders, as well as other considerations, to include but not limited to resources available to the Bidder to perform the work effectively, proposed Subcontractors and other persons and organizations to do the workin accordance with the Contract Documents to PWC's satisfaction within the prescribed time.
- 7. PWC reserves the right to reject the Bid of any Bidder who does not pass any such evaluation to PWC's satisfaction.
- 8. If the Contract is to be awarded, PWC will give the Successful Bidder a Notice of Award within ninety (90) days after the day of the Bid Opening.
- 9. The Bidder to whom the contract is awarded shall, within ten (10) days after prescribed documents are presented for signature, execute and deliver the Contract Documents and any otherforms or bonds required by the Bid to PWC.
- 10. The Bidder is required to complete the attached forms that will allow PWC to verify that the Bidder is qualified to perform the Work described in these Contract Documents. All forms shall be completed and submitted with the Bid. Failure to submit all the required forms shall be considered grounds for PWC to reject the bid.
 - PWC will review all of the bids and qualification data to determine the lowest responsive, responsible Bidder. PWC reserves the right to not award the Contract to the lowest bidder if the information provided is not complete, does not meet the satisfaction of PWC, or has been falsified. PWC will not request any additional information in order to allow the Contractor to complete bid.
- 11. During the evaluation phase, bid submittals will be reviewed to ascertain which bids technically and otherwise address all the requirements of these Contract Documents. Bid submittals determined to be technically non-responsive or not sufficiently responsive may be disqualified.
 - The Bidder shall address each of the Evaluation Criteria as requested in the Technical Evaluation Criteria Form located within Section A Project Specifics Bid Submittal Documents. To be considered substantive, the information must respond to all requirements.
- 12. PWC may conduct such investigations/verifications as deemed necessary to establish the responsibility, qualification and financial ability of the Bidder. Should PWC find that the apparent low bidder is not the lowest responsive, responsible bidder by integrity of the information furnished, said apparent low bidder will be so notified and its bid bond shall be returned without prejudice. Failure or refusal to furnish any items of information requested by PWC shall be considered as non-responsive and therefore basis for rejection of the bid.

Q. TAXES

- The Successful Bidder shall pay all county, city, state and federal taxes required by laws in effect at the time Bids are received and resulting from the Work or traceable thereto, under whatever name levied.
- 2. Said taxes shall not be in addition to the contract price between PWC and the Successful Bidder. The taxes shall be an obligation of the Successful Bidder and not of PWC. PWC shall be held harmless from same by the Successful Bidder.

R. PERFORMANCE AND OTHER BONDS

1. The PWC General Conditions set forth PWC's requirements as to Performance and other Bonds.

S. E-VERIFY REQUIREMENTS

- 1. Contractor hereby acknowledges that "E-Verify" is the federal E-Verify program operated by the US Department of Homeland Security and other federal agencies which is used to verify the work authorization of newly hired employees pursuant to federal law and in accordance with Article 2, Chapter 64 of the North Carolina General Statutes.
- 2. Contractor further acknowledges that all employers, as defined by Article 2, Chapter 64 of the North Carolina General Statutes, must use E-Verify and after hiring an employee to work in the United States, shall verify the work authorization of the employee through E-Verify in accordance with NCGS §64-26(a).
- 3. Contractor hereby pledges, attests and warrants through execution of this Agreement that Contractor complies with the requirements of Article 2, Chapter 64 of the North Carolina General Statutes and further pledges, attests and warrants that any subcontractors currently employed byor subsequently hired by Contractor shall comply with any and all E-Verify requirements. Failure to comply with the above requirements shall be considered a breach of this Agreement.

T. IRAN DIVESTMENT ACT

1. As mandated by N.C.G.S. 147-86.59(a), the Contractor hereby certifies that it is not listed on the Final Divestment List created by the North Carolina State Treasurer pursuant to N.C.G.S. 147-86.58. Contractor further certifies that in accordance with N.C.G.S. 146-86.58(b) that it shall not utilize any subcontractor found on the State Treasurer's Final Divestment List. Contractor certifies that the signatory to this Purchase Order authorized by the Contractor to make the foregoing statement.

*** END OF SECTION ***

SECTION A – PROJECT SPECIFICS BID SUBMITTAL DOCUMENTS

BID SCHEDULE – PERFORMANCE AND DELIVERY FAYETTEVILLE PUBLIC WORKS COMMISSION FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

Virtual Pre-Bid Meeting: 11:00 am, Tuesday, March 12, 2024

(MANDATORY) Via Microsoft Teams

Click here to join the meeting Meeting ID: 296 580 015 006

Passcode: yLskxB Or call in (audio only)

910-302-6113 # 261 453 490#

Deadline for Questions from

Bidders¹

5:00 pm, Friday, March 15, 2024

Deadline for Addenda issued by PWC Procurement Department and

Project Engineer²

5:00 pm, Wednesday, March 20, 2024

Bid Opening (Submittal Deadline) 2:00 pm, Thursday, March 28, 2024

Fayetteville Public Works Commission

Administrative Building Conference Room 107 955 Old Wilmington Road Fayetteville, NC 28301

Contract Time: 350

Liquidated Damages: Insert amount \$1,000.00 per day for each

day beyond the Final Completion Date

Bid Acceptance Period Within ninety (90) Calendar Days unless

otherwise noted

1. Questions regarding this bid must be submitted in writing to the attention of Tanya Hazlett, Procurement Advisor, by email to procurement@faypwc.com.


Bidders are expressly prohibited from contacting any FPWC official or employee associated with this Invitation to Bid, except as noted above. Violation of this prohibition is grounds for the immediate disqualification of the bidder.

2. Any addenda to these Contract Documents will be issued by the Project Engineer no later than the date and time stated above.

BID SUBMITTAL CHECKLIST

| 1. | Enter Contractor's License Number where called for in the Bid Form and on the outside of the sealed envelope containing the Bid. |
|----|---|
| 2. | Photocopy of Contractor's License. |
| 3. | Bid Bond |
| 4. | Bid Forms Section 00300. |
| 5. | Provide the responsible North Carolina Registered Agent for Insurance Claims. Include contact information. |
| 6. | Provide the proposed responsible Bonding Company name. Include contact information. |
| 7. | List of proposed Subcontractors and material suppliers exceeding 5% of the Contract Value. |
| 8. | Non-Collusive Affidavit. |
| 9. | Nondiscrimination Clause. |
| 10 | . Affidavit of Organization and Authority and Sworn Statement. |
| 11 | . Equal Employment Opportunity Acknowledgment. |
| 12 | . Certification regarding Debarment, Proposed Debarment, and other Responsible Matters. |
| 13 | . FTA Certification Regarding Lobbying. |
| 14 | . Affidavit A – Listing of Good Faith Efforts, et al. |
| 15 | . Affidavit B – (Only if the Contractor will perform <u>ALL ELEMENTS OF THE WORK</u> on this project with their own forces <u>AND</u> will complete <u>ALL ELEMENTS OF THIS PROJECT</u> <u>WITHOUT THE USE OF SUBCONTRACTORS, MATERIAL SUPPLIERS, OR PROVIDERS OF PROFESSIONAL SERVICES</u> . |
| 16 | . Affidavit E - Identification of Minority Business Participation Form. |
| 17 | . SLS / MWDBE Disclosure Form. |
| 18 | . The Completed Technical Evaluation Criteria Form. |

FAILURE TO SUBMIT THE ABOVE FORMS WITH THE BID FORM MAY BE JUST CAUSE FOR REJECTION OF THE BID BY THE OWNER

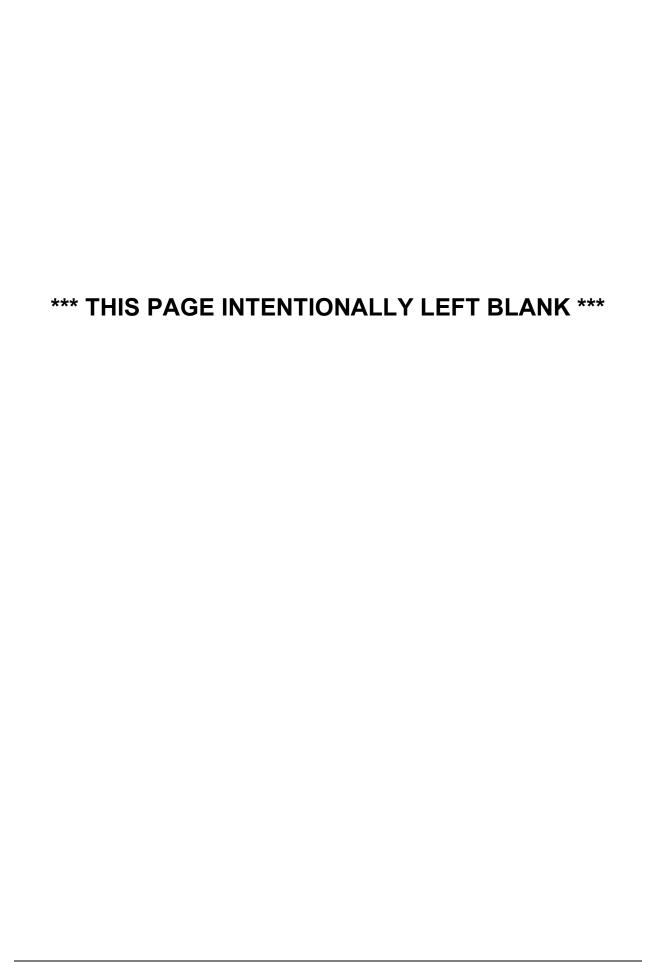

00300 - BID FORM

| TO: | Attn: Tanya Hazl 955 Old Wilming | ett, Procurement Advisor ton Road ch Carolina 28301 | |
|----------|-------------------------------------|---|-----|
| PROJECT: | | ANNEXATION PHASE V, PROJECT XII, CONSTRUCT FDALE FOREST | ION |
| FROM: | BIDDER | | |
| | ADDRESS | | |
| | | | |
| | DATE OF BID | . 20 |) |

- A. The undersigned BIDDER proposes and agrees, if this Bid is accepted, to enter into a Contract with OWNER in the form included in the Contract Documents to perform and furnish all Work (as that term is defined in the Construction Agreement) specified or indicated in the Contract Documents for the Contract Price and within the Contract Time indicated in this Bid and in accordance with the Contract Documents.
- B. BIDDER accepts all of the terms and conditions of the Instructions to Bidders, including, without limitation, those dealing with the disposition of payment and performance bonds, and insurance certificates. This bid will remain open for ninety (90) calendar days after the day of Bid opening. BIDDER will sign the Contract and submit the Contract Security and other documents required by the Contract Documents within ten (10) days after the date of receipt by the BIDDER.
- C. In submitting this Bid, Bidder represents, as more fully set forth in the Contract, that:
 - 1. BIDDER has examined copies of all the Contract Documents and of the following addenda, receipt of all which is acknowledged on the bid summary page:
 - BIDDER has examined the site and locality where the Work is to be performed, the legal requirements (federal, state, and local laws, ordinances, rules and regulations) and the conditions affecting cost, progress of performance of the work and has made such independent investigations as BIDDER deems necessary.
 - 3. BIDDER acknowledges that OWNER does not assume responsibility for the accuracy of dimensions or completeness of information and data shown or indicated in the Bidding Documents with respect to existing facilities.
 - 4. BIDDER has carefully studied all reports of explorations and tests of subsurface conditions at or contiguous to the site of the Work (expect underground facilities)

and all drawings of physical conditions in or relating to existing surface or subsurface structures, pipelines, and utilities at or contiguous to the site are provided within these Contract Documents. Geotechnical Reports and other information regarding subsurface conditions are identified in the attached appendices and detailed in Article V of the PWC General Conditions. BIDDER acknowledges that the OWNER does not assume responsibility for the accuracy or completeness of information and data shown or indicated in the Bidding Documents with respect to underground facilities at or contiguous to the site of Work. BIDDER had obtained and carefully studied (or assumes responsibility for have done so) all such additional or supplementary examinations investigations, explorations, tests, studies, and data that are necessary to identify and understand conditions (surface, subsurface, and underground facilities) at or contiguous to the site of Work or otherwise which may affect cost, progress, performance, or furnishing the Work or which relate to any aspect of means, methods, techniques, sequences, and procedures of construction to be employed by Bidder and safety precautions and programs incident thereto. BIDDER waives all rights to claim that any additional examinations, investigations, explorations, tests, studies, or data are necessary for the proper submission of the Bid for the performance and furnishing of the Work in accordance with the Contract Time, Contract Price, and other terms and conditions of the Contract Documents.

- 5. BIDDER hereby certifies that, if awarded the Contract for construction of the Project, it will take all possible actions to minimize costs to the OWNER which are related to any disruptions in any part of the Work resulting from unforeseeable conditions which may be encountered and work changes or additions which may be made.
- 6. BIDDER has correlated the information known to BIDDER, information and observations obtained from visits to the site, reports and drawings identified in the Contract Documents, and all additional examinations, investigations, exploration, tests, studies, and data with the Contract Documents.
- 7. BIDDER has given OWNER written notice of all conflicts, errors, ambiguities, or discrepancies that BIDDER has discovered in the Contract Documents and the written resolution thereof by OWNER is acceptable to BIDDER, and the Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performing and furnishing the Work for which this Bid is submitted.
- 8. By bidding in response to this invitation, the BIDDER represents that in the preparation and submission of this Bid, said BIDDER did not, either directly or indirectly, enter into any combination or arrangement with any person, firm or corporation or enter into any agreement, participate in any collusion, or otherwise take any action in the restraint of free, competitive bidding in violation of the Sherman Act (15 U.S.C. Section 1).
- 9. Bid form must be completed in blue or black ink or by typewriter. The Bid price of

each item on the form must be stated in both words and numerals. In case of a conflict, words shall take precedence. Discrepancies in the multiplication of units of work and unit prices will be resolved in favor of the correct multiplication of the unit prices. Discrepancies between the indicated sum of any column of figures and the correct sum thereof will be resolved in favor of the correct sum.

- 10. BIDDER understands that the award of contract will be made on the basis of the total Bid amount which will be determined as the sum of the unit price and lump sum Bid Items.
- 11. BIDDER understands that quantities are estimated and are not guaranteed; they are solely for comparing Bids and establishing the total Bid amount. The Price will be modified by Change Order, and final payment will be based on the quantities of work actually furnished and installed by the successful BIDDER.
- 12. BIDDER shall complete the Work for the prices indicated on the next page.

ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM tem | Estimated | Unit | Un

| Item No. | Ref. No. | Item | Estimated Quantities | Unit | Unit Price | Cost Extension |
|-------------|-------------|--|-------------------------|------|------------|----------------|
| | | PART "A" STREET CONSTRUCTION - "BASE BID" | | | | |
| A-1 | G-1 | Mobilization and Demobilization | 1 | ST | | |
| A-2 | G-2 | Traffic Control and Traffic Plan | - | ST | | |
| A-3 | A-1 | 2-inches min., SF9.5A for Permanent Pavement Patch (No Overage Allowed, NOA) @square yard | 17,553 | SΥ | | |
| A-4 | A-4 | 2-inches min., SF9.5A Permanent Pavement Patch Failed Areas - PWC (NOA) @square yard | 280 | SY | | |
| A-5 | A-4 | 2-inches min., SF9.5A Permanent Pavement Patch Failed Areas - COF (NOA) @square yard | 2,800 | SY | | |
| 9-V | A-1 | 2-inches min., SF9.5A with 8-inch Stone Base Course for Street Reconstruction (Lisa Avenue and Sanchez Drive) - PWC (NOA) @ | 3,178 | SY | | |
| 7-A | A-1 | 2-inches min., SF9.5A with 8-inch Stone Base Course for Steet Reconstruction (Lisa Avenue and Sanchez Drive) - COF (NOA) | 3,178 | SY | | |
| A-8 | A-6 | Undercut Excavation in Asphalt Subgrade (NOA) @ | 2,019 | СУ | | |
| A-9 | A-7 | Incidental Stone @per ton | 649 | NL | | |
| A-10 | A-13 | Maintenance Stone (NOA) | 1,404 | SY | | |
| | | | | | | |
| | | TOTAL PART "A" STREET CONSTRUCTION - "BASE BID" | | | | |

FAYETTEVILLE PUBLIC WORKS COMMISSION ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM

| Item | Ref. | 777 | | Estimated | 71-11 | I mit Duine | | _ |
|------|-----------------------------|--|-----------------|------------|-------|-------------|----------------|---|
| | No. | Item | | Quantities | משנ | Onit Price | Cost Extension | |
| | | PART "C" AQUA WATER CONSTRUCTION - "BASE BID" | SID" | | | | | _ |
| | G-7 Soc (AQUA) @_ | d (Aqua Water Service) (No Overage Allowed) | per square yard | 150 | λS | | | |
| İ | G-8 Ter (AQUA) @_ | nporary Seeding (No Overage Allowed) | per acre | 0.03 | AC | | | |
| Ì | C-10 Re (AQUA) @_ | placement of Existing 3/4" Aqua America Water Service | per each | 10 | EA | | | |
| | C-11 3/4 (AQUA) @_ | " Water Service Relocation Aqua America | per each | 2 | EA | | | |
| | C-21 Rei (AQUA) <u>@</u> | C-21 Remove and Replace Existing 6" Water Main with DIP Aqua America AQUA) @ | ica Ir foot | 20 | J) | | | |
| | | | | | | | | |
| | | TOTAL PART "C" AQUA WATER CONSTRUCTION - "BASE BID" | "BASE BID" | | | | | |

FAYETTEVILLE PUBLIC WORKS COMMISSION ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM

| Item No. | Ref. No. | | Estimated Quantities | Unit | Unit Price | Cost Extension |
|-------------|-------------|---|-------------------------|------|------------|----------------|
| | | PART "D" SANITARY SEWER UTILITIES - "BASE BID" | | | | |
| D-1 | 6-1 | Mobilization and Demobilization $@_$ lump sum $@_$ | 1 | ST | | |
| D-2 | G-2 | Traffic Control and Traffic Plan Jump sum | 1 | ST | | |
| D-3 | G-3 | Erosion and Sediment control @lump sum | 1 | ST | | |
| D-4 | G-5 | Clearing and Grubbing, Permanent Easements @ per acre | 0.34 | AC | | |
| D-5 | 9-9 | Clearing and Grubbing, Temporary Easements $@$ per acre $@$ | 0.25 | AC | | |
| D-6 | C-5 | Sod (No Overage Allowed) @ | 5,309 | SY | | |
| D-7 | C-5 | Sod (Sanitary Sewer Laterals) (No Overage Allowed) @ per square yard | 2,250 | SY | | |
| D-8 | g-9 | Temporary Seeding (No Overage Allowed) @ per acre | 1.56 | AC | | |
| 6-Q | g-9 | Wetland Seeding (No Overage Allowed) @ per acre | 0.16 | AC | | |
| D-10 | D-1 | 8" SDR26 PVC Sanitary Sewer 0'-6' Depth @ | 22 | LF | | |
| D-11 | D-1 | 8" SDR26 PVC Sanitary Sewer 6'-8' Depth @ | 8,010 | LF | | |
| D-12 | D-1 | 8" SDR26 PVC Sanitary Sewer 8'-10' Depth @ | 3,424 | -LF | | |
| D-13 | D-1 | 8" SDR26 PVC Sanitary Sewer 10'-12' Depth @per linear foot | 1,622 | LF | | |
| D-14 | D-1 | 8" SDR26 PVC Sanitary Sewer 12'-14' Depth @ | 282 | LF | | |
| D-15 | D-1 | 8" SDR26 PVC Sanitary Sewer 14'-16' Depth | 100 | 님 | | |

EAYETTEVILLE PUBLIC WORKS COMMISSION ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM

| 느 | 느 | Ľ | 当 | 占 | 打 | ㅂ | ㅂ | 打 | 当 | £1 | 打 | EA | EA | EA | EA |
|---|---|--|---|--|---|--|---|--|---|--|---|---|---|---|---|
| 164 | 276 | 209 | 44 | 58 | 20 | 298 | 63 | 38 | 26 | 370 | 110 | 4 | - | _ | 1 |
| 8" CL 50 DI Sanitary Sewer 0'-6' Depth @ | 50 DI Sanitary Sewer 6'-8' Depth per linear foot | 50 DI Sanitary Sewer 8'-10' Depth per linear foot | 8" CL 50 DI Sanitary Sewer 10'-12' Depth @ | 8" CL 50 Restrained DI Sanitary Sewer 0'-6' Depth @ | CL 50 Restrained DI Sanitary Sewer 6'-8' Depth per linear foot | 53 Restrained DI Sanitary Sewer 0'-6' Depth per linear foot | CL 53 Restrained DI Sanitary Sewer 6'-8' Depth per linear foot | 8" CL 53 Restrained DI Sanitary Sewer 8'-10' Depth @per linear foot | 8" CL 53 Restrained DI Sanitary Sewer 10'-12' Depth @per linear foot | Guided Bore & Jack (24" Steel Encasement, 0.375" thick, w/ 8" Restrained DIP Carrier Pipe) (Typical Launch Pit) @per linear foot | Furnish and Install Aerial 8-inch Class 53 RJDIP Crossing (Including Piers) | Sanitary Sewer Manhole 5' Dia 10'-12' Depth @ per each | Sanitary Sewer Manhole 5' Dia 12'-14' Depth @ per each | Sanitary Sewer Manhole 5' Dia 14'-16' Depth @ per each | Sanitary Sewer Manhole 4' Dia 0'-6' Depth @ per each |
| 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 | 8" CL 5 @ | 8" CL 5 | Guided w/8"R _' | Furnish | Sanitary @ | Sanitary @ | Sanitary @ | Sanitary @ |
| D-2 | D-2 | D-2 | D-2 | D-2 | D-2 | D-2 | D-2 | D-2 | D-2 | D-27 | D-33 | D-5 | D-5 | D-5 | D-5 |
| D-16 | D-17 | D-18 | D-19 | D-20 | D-21 | D-22 | D-23 | D-24 | D-25 | D-26 | D-27 | D-28 | D-29 | D-30 | D-31 |

EAYETTEVILLE PUBLIC WORKS COMMISSION ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM

| EA | EA | EA | EA | EA | EA | EA | EA | EA | EA | EA | EA | EA | EA | ≿ | 님 | 느 |
|--|--|---|---|--|--|--|--|---------------------------------------|---------------------------------------|--|--|---|----------------------|------------------------|-------------------------|------------------------------|
| 37 | 21 | 5 | - | - | Е | _ | - | 12 | 10 | 211 | 41 | 8 | 2 | 1,051 | 14,602 | 536 |
| Sanitary Sewer Manhole 4' Dia 6'-8' Depth per each | Sanitary Sewer Manhole 4' Dia 8'-10' Depth @ per each | Sanitary Sewer Manhole 4' Dia 10'-12' Depth @ per each | Sanitary Sewer Doghouse Manhole 4' Dia 0'-6' Depth @ | Sanitary Sewer Doghouse Manhole 4' Dia 8'-10' Depth @ per each | Sanitary Sewer Doghouse Manhole 5' Dia 10'-12' Depth @ per each | Sanitary Sewer Doghouse Manhole 5' Dia 12'-14' Depth @ per each | Sanitary Sewer Doghouse Manhole 5' Dia 14'-16' Depth @ per each | 4" Interior Drop Structure @ per each | 8" Interior Drop Structure @ per each | 4" PVC Sanitary Sewer Lateral @ per each | 4" DIP Sanitary Sewer Lateral @ per each | 8" Connection to Existing Structure @ per each | Anti-Seep Collars @ | Undercut Excavation @ | Testing Ber linear foot | Hydrostatic Pressure Testing |
| D-5 | D-5 | D-5 | 9-0 | 9-0 | 9-0 | 9-0 | 9-0 | 2-Q | D-7 | 8-0 | 6-0 | D-13 | D-14 | D-16 | D-17 | D-32 |
| D-32 | D-33 | D-34 | D-35 | D-36 | D-37 | D-38 | D-39 | D-40 | D-41 | D-42 | D-43 | D-44 | D-45 | D-46 | D-47 | D-48 |

FAYETTEVILLE PUBLIC WORKS COMMISSION ANNEXATION PHASE V, PROJECT XII CONSTRUCTION AREA 27 FAYETTEVILLE, NORTH CAROLINA BID FORM

| CY | -F | -F | 4 | LF | λS | EA | EA | EA | -F | - LF | |
|--|--|---|----------------------|---|--|--|--|--|--|---------------------------------------|--|
| G-4 Borrow Excavation per cubic yard 420 | Remove and Replace with new pipe 24" CL IV RCP 0'-6' Depth B-8 (No Overage Allowed) @ | Remove and Replace with new pipe 18" CL IV RCP 0'-6' Depth B-8 (No Overage Allowed) @ | B-8 @per linear foot | Remove and Replace with new elliptical pipe 19"x30"" CL IV RCP 0'-6' Depth B-8 (No Overage Allowed) @ | B-6 Install Class I RipRap per square yard 101 | Install 3.5' Chain Link Double Gates Across Easements O | N/A Install 6' Chain Link Double Gates Across Easements 6. | N/A Install 6' Wood Double Gates Across Easements 3 @ per each 3 | N/A Install 3.5' Chain Link Fencing 13.6' Chai | N/A Install 6' Chain Link Fencing 741 | TOTAL PART "D" SANITARY SEWER UTILITIES - "BASE BID" |
| D-49 | D-50 | D-51 | D-52 | D-53 | D-54 | D-55 | D-56 | D-57 | D-58 | D-59 | |

TOTAL PART "A" STREET CONSTRUCTION - "BASE BID"
TOTAL PART "C" AQUA WATER CONSTRUCTION - "BASE BID"
TOTAL PART "D" SANITARY SEWER UTILITIES - "BASE BID"

TOTAL BASE BID

- BID SUMMARY-

| TOTAL PART "A" STREET CONSTRUCTION | \$ |
|--|--|
| TOTAL PART "C" WATER (AQUA) | \$ |
| TOTAL PART "D" SANITARY SEWER | \$ |
| TOTAL BASE BID | \$ |
| The BIDDER has received, acknowledged, and ublid. (Initial and Date as appropriate). | used the following addenda in completing the |
| Addendum No. 1 | Date |
| Addendum No. 2 | Date |
| Addendum No. 3 | Date |
| Addendum No. 4 | Date |
| Addendum No. 5 | Date |
| Addendum No. 6 | Date |
| Addendum No. 7 | Date |
| The undersigned BIDDER | (Contractor Name) certifies that they are |
| licensed as a Contractor under N.C.G.S § 87, an | d that their license number |
| is (License Number) | |

The undersigned BIDDER hereby agrees to accept an award of the Contract based on the Total Contract Amount as accepted by the OWNER and as indicated on the Notice of Award.

- A. BIDDER agrees that Work shall be completed within the time frame indicated in the Agreement as follow:
 - 1. All work described herein to be complete, including restoration and all punch list items from 350 days from the Notice to Proceed.
 - 2. The BIDDER acknowledges that time is of the essence in this Contract and that the OWNER will suffer financial loss if the Work is not complete within the time specified in Paragraph D.1 above plus any extensions thereof allowed in accordance with these Contract Documents. BIDDER also recognizes the delays, expense and difficulties involved in proving in a legal proceeding the actual loss suffered by the OWNER if the Work is not complete on time. The Bidder agrees to diligently pursue all available work and complete all work in an expeditious manner.
- B. The following documents are attached to and made part of this bid:

Required Bid Security in the form of either a cashier's check or certified check or Bid Bond in the amount of 5% of maximum Bid price.

| C. | Address and Telephone Number) | be addressed to: (CONTRACTOR's Name, |
|----|---|---|
| | | |
| D. | PWC General Conditions or as otherwise s | I in Definitions and Terminology Section of the pecifically defined in the Contract Documents in, which are incorporated by reference as if forth herein. |
| E. | proprietorship, partnership and corporation | arnish his social security number and sole on are required to furnish their employer lic Works Commission. Please indicate this |
| | Social Security Number: | |
| | Federal Employer Identification Number: | |
| | SUBMITTED ONday of | _20 <u>24</u> |

AN INDIVIDUAL

| BY: | (SEAL) |
|--|---------------|
| (Individual's Name and Signature) | |
| Doing Business as: | |
| North Carolina Contractor Registration Number: | |
| Business Address: | |
| Phone Number: | |
| Subscribed and sworn to before me thisday of | _20 <u>24</u> |
| NOTARY PUBLIC | |
| My Commission Expires: | |
| A PARTNERSHIP | |
| BY: | (SEAL) |
| (Firm Name) | |
| (General Partner and Signature) | |
| North Carolina Contractor Registration Number: | |
| Phone Number: | |
| Subscribed and sworn to before me thisday of | _20 <u>24</u> |
| NOTARY PUBLIC | |
| My Commission Expires: | |
| A CORPORATION | |
| BY: | |

(Corporation Name)

(State of Incorporation)

| BY: | | (SEAL) |
|--|------------|--------------|
| (Name and Title of Person Authoriz | | |
| | | |
| ATTEST: | | |
| (Secretary or Assistant Secretary and Sign | ature) | |
| North Carolina Contractor Registration Nur | mber: | |
| Business Address: | | |
| Phone Number: | | |
| Subscribed and sworn to before me this | day of | 20 <u>24</u> |
| | | |
| | | |
| NOTARY PUBLIC | | |
| My Commission Expires: | | |
| | | |
| | | |
| A JOINT VENTURE | | |
| | | |
| BY: | | |
| (Name and | Signature) | |
| Doing Business as: | | |
| North Carolina Contractor Registration Nur | nber: | |
| Business Address: | | |
| Phone Number: | | |
| Subscribed and sworn to before me this | day of | 20 <u>24</u> |
| | | |
| | | |
| NOTARY PUBLIC | | |
| My Commission Expires: | | |

(Each joint venturer must sign. The name of signing for each individual, partnership, and corporation that is a party to the joint venture should be in the manner indicated above.)

TECHNICAL EVALUATION FORM

| ************************************** | | | | | |
|--|-------------------|--------|--|--|--|
| TECHNICAL EVALUATION CRITERIA FORM | | | | | |
| PROJE | ECT DOCUMENTATION | | | | |
| (1) Permanent Name of Business: | | | | | |
| (2) Permanent address: | | | | | |
| (3) Length of Time in Business: | | | | | |
| (4) Has the organization operated under any other name? | | | | | |
| (5) State the names and/or companies financially interested in the proposal: | | | | | |
| (6) Within the last five (5) years, has any officer or principal of the organization ever been an officer or principal of another organization when it failed to complete a construction contract? If yes, list name(s), and responsibility. | | | | | |
| UTILITY RETROFIT EXPERIENCE/WATER AND SEWER MAIN EXPERIENCE | | | | | |
| (1) List not less than three (3) completed retrofit projects of similar size, scope, nature, and cost, to include the dates of such projects. Please provide all requested information for each listed project. Each project should be from separate references. List only those projects completed as Prime Contractor. | | | | | |
| Project 1A: | | Cost: | | | |
| Location: | Dates: | Size: | | | |
| Scope: | Client: | Phone: | | | |
| D : 41D | | | | | |
| Project 1B: | | Cost: | | | |
| Location: | Dates: | Size: | | | |
| Scope: | Client: | Phone: | | | |

| Project 1C: | | Cost: | | |
|--|---------|--------|--|--|
| Location: | Dates: | Size: | | |
| Scope: | Client: | Phone: | | |
| | | | | |
| (2) A listing of three (3) water and/or sewer main projects of similar size, scope and cost. (Provide reference information as stated in #1.) | | | | |
| Project 2A: | | Cost: | | |
| Location: | Dates: | Size: | | |
| Scope: | Client: | Phone: | | |
| | | | | |
| Project 2B: | | Cost: | | |
| Location: | Dates: | Size: | | |
| Scope: | Client: | Phone: | | |
| | | | | |
| Project 2C: | | Cost: | | |
| Location: | Dates: | Size: | | |
| Scope: | Client: | Phone: | | |
| | | | | |
| (3) List any subcontracting experience on retrofit projects with specifics to the type of work performed for this project. Please provide all requested information. | | | | |
| Project: | | Cost: | | |

| Location: | Dates: | | Size: | | | |
|--|--------|---------------------------|-------|--|--|--|
| | | | | | | |
| Work | | | | | | |
| Performed: | | | | | | |
| | | | | | | |
| | | | | | | |
| | | | | | | |
| Project: | | | Cost: | | | |
| | | | | | | |
| Location: | Date | s: | Size: | | | |
| | | | | | | |
| | | | | | | |
| Work | | | | | | |
| Performed: | | | | | | |
| | | | | | | |
| | | | | | | |
| | T | | | | | |
| Project: | | | Cost: | | | |
| | | | | | | |
| Location: | Date | s: | Size: | | | |
| | | | | | | |
| W 1 | | | | | | |
| Work Performed: | | | | | | |
| | | | | | | |
| | | | | | | |
| | | | | | | |
| | | | | | | |
| (4) List of projects in progress. Please | provid | de all requested informat | 1 | | | |
| Project: | | Cost: | | | | |
| | | | | | | |
| Owner: | | | | | | |
| | | | | | | |
| Percentage Complete: | | Scheduled Completion | Date: | | | |
| | | 1 | | | | |
| Project: | | | Cost: | | | |
| | | | | | | |
| Owner: | | | | | | |
| | | | | | | |
| Paraantaga Camplata | | Schadulad Completion | Data | | | |
| Percentage Complete: | | Scheduled Completion | Date. | | | |
| | | | | | | |

| Project: | | Cost: | | | |
|---|-----------------------|----------------------|-------|--|--|
| Owner: | | | | | |
| Percentage Complete: | | Scheduled Completion | Date: | | |
| | | | | | |
| Project: | | | Cost: | | |
| Owner: | | | | | |
| Percentage Complete: | | Scheduled Completion | Date: | | |
| | | | | | |
| Project: | | | Cost: | | |
| Owner: | | | | | |
| Percentage Complete: | | Scheduled Completion | Date: | | |
| | | | | | |
| Project: | | | Cost: | | |
| Owner: | | | | | |
| Percentage Complete: | | Scheduled Completion | Date: | | |
| PROJECT PERSONNEL AND EXPERIENCE | | | | | |
| (1) The number of crews qualified and available to perform the work stated in this proposal: | | | | | |
| (2) The names of Bidder superintendents and crew leaders/foreman who are qualified and available to perform the work stated in this proposal: | Superintendents: | | | | |
| | Crew leaders/foreman: | | | | |
| ADDITIONAL ITEMS | | | | | |
| The following items shall be submitted as attachments: | | | | | |
| (1) Affidavit stating any OSHA violations occurring within the past three (3) years. | | | | | |
| (2) A statement provided by the Surety Company stating the Bidder's bonding limit and a statement of the amount of work currently under bond. | | | | | |
| (3) A statement listing any judgments, claims, arbitration proceedings, or suits pending or outstanding against organization or its officers. | | | | | |

| (4) A statement listing any filed lawsuits, judgments, claims, arb pending with regard to construction contracts within the last | | |
|---|--------|--|
| (5) The resumes or brief summary of key personnel of the organization. Identify the person that will be primarily responsible for the project. | | |
| (6) List of equipment that is available for use on the subject project | ect. | |
| | | |
| The Owner may conduct such investigations/verifications as deemed necessary to establish the responsibility, qualification and financial ability of the Bidder. Should the Owner adjudge that the apparent low bidder is not the lowest responsive, responsible bidder by virtue of the above information furnished, said apparent low bidder will be so notified and his bid security shall be returned to him without prejudice. Failure or refusal to furnish any items of information requested by the Owner shall be considered as non-responsive and therefore, basis for rejection of the bid. | | |
| | | |
| Submitted By: | Date: | |
| Printed Name: | Title: | |

LIST OF SUBCONTRACTORS

In compliance with the Instructions to Bidders and the Supplementary Conditions, the undersigned submits the following names of Subcontractors to be used in performing the Work.

The Bidder certifies that all Subcontractors listed are eligible to perform the Work and that all Subcontractors performing more than five percent of the work are listed.

| Subcontractor's Work | Subcontractor's Name |
|----------------------|----------------------|
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | Bidder's Signature |

BID BOND

This is a Bid Bond that is subject to the provisions of Article 3 of Chapter 44A of the North Carolina General statutes.

| This Bond is executed on | , 20 _ | · |
|----------------------------------|--|-----|
| The name of the PRINCIPAL is | | (1) |
| | | (2) |
| The name of the SURETY is | | |
| | | |
| Fayetteville Public Works Commis | ssion, Fayetteville, North Carolina is the OWNER | |
| The amount of the Bond is | | |
| | (Dollars) (\$ |) |

KNOW BY ALL MEN BY THESE PRESENTS, the Principal and Surety above named are hereby held and firmly bound unto the above named OWNER hereinafter called the OWNER in the penal sum of the amount stated above in lawful money of the United States, for the payment of which, well and truly to be made, we hereby jointly and severally bind ourselves, our heirs, executors, administrators, successors and assigns.

The condition of the above obligation is such that whereas the Principal has submitted to the OWNER a certain Bid, attached hereto and hereby made a part hereof to enter into a Contract in writing, for the construction of:

FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

NOW, THEREFORE

- (a) If said Bid shall be rejected, or in the alternate,
- (b) If said Bid shall be accepted and the Principal shall execute and deliver a Contract in the Form of Contract attached hereto (properly completed in accordance with said Bid) and shall furnish a bond for his faithful performance of said Contract, and for the payment of all persons performing labor or furnishing materials in connection therewith, and shall in all other respects perform the agreement created by the acceptance of said Bid, then this obligation shall be void, otherwise the same shall remain in force and effect; it being expressly understood and agreed that the liability of the Surety for any and all claims hereunder shall, in no event, exceed the penal amount of this obligation as herein stated.

The Surety, for value received, hereby stipulates and agrees that the obligations of said Surety and its Bond shall be in no way impaired or affected by any extension of the time within which the Owner may accept such Bid; and said Surety does hereby waive notice of any such extension.

IN WITNESS WHEREOF, the Principal and the Surety have hereunto set their hands and seals, and such of them as are corporations have caused their corporate seals to be hereto affixed and these presents to be signed by their proper officers, the day and year first set forth above.

| | Principal | |
|-----|-----------|---------------------|
| BY: | | (3) |
| | (Address) | |
| | Surety | |
| | (Address) | |
| | | |
| | | |
| | | |
| | | |
| | BY: | BY:(Address) Surety |

- (1) Correct name of Contractor
- (2) A Corporation, a Partnership or an Individual, as the case may be
- (3) If Contractor is a Partnership, all partners should execute Bond

POWER OF ATTORNEY (Attach)

AFFIDAVIT OF ORGANIZATION AND AUTHORITY SWORN STATEMENT FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

| STATE OF | - |
|---|---|
| COUNTY OF | |
| oath deposes and says that the Bidder on the attached Bid Form id and that all statements herein made are made on behalf of such Bi authorized to make them. | being the first duly sworn on organized as indicated below dder and that this deponent is |
| (Fill Out Applicable Paragraph) | |
| 1. CORPORATION | |
| The bidder is a corporation organized and existing under the laws of and its President is | the State of, and its |
| and its President is and does have a corport is authorized to sign construction Corcompany by action of its Board of Directors taken copy of which is hereto attached. (Strike out last sentence if not applications) | , a certified |
| 2. PARTNERSHIP | |
| The Bidder is a Partnership consisting of, partners doing business under the na | and ame of |
| 3. SOLE TRADER | |
| The Bidder is an individual and if operating under a trade name, suc | h trade name is as follows: |
| 4. ADDRESS | |
| The business address of the Bidder is as follows: | |
| Its phone number is | |
| Bidder | |
| Ву: | |

EQUAL EMPLOYMENT OPPORTUNITY

During the performance of this Contract the Contractor agrees as follows:

- a. The Contractor will not discriminate against any employee or applicant because of race, color, religion, sex, or national origin. The Contractor will take affirmative action to ensure that applicants are employed, and that employees are treated during employment, without regard to race, color, religion, sex, or national origin. Such action shall include but not be limited to the following: employment, upgrading, demotion, or transfer, recruitment or recruitment advertising, layoff or termination, rates of pay or other forms of compensation, and selection for training, including apprenticeship. The Contractor agrees to post in conspicuous places, available to employees and applicants for employment, notices setting forth the provisions of the nondiscrimination clause.
- b. The Contractor will, in all solicitations or advertisements for employees placed by or on behalf of the Contractor, state that all qualified applicants will receive consideration for employment without regard to race, color, religion, sex, or national origin.
- c. The Contractor will send to each labor union or representative of workers with which he has a collective bargaining agreement or other Contract understanding, a notice, to be provided, advising the labor union or worker's representative of the Contractor's commitments under the Equal Employment Opportunity Section of this Contract, and shall post copies of the notice in conspicuous places available to employees and applicants for employment.
- d. In the event of the Contractor's noncompliance with the nondiscrimination clauses of this Contract or with any of such rules, regulations, or orders, this Contract may be canceled, terminated, or suspended in whole or in part and the Contractor may be declared ineligible for further OWNER Contracts.
- e. The Contractor will include the provisions of this section in every subcontract or purchase order unless exempted by rules, regulations, or orders of the OWNER so that such provisions will be binding upon each Subcontractor or vendor.

| (Use the following form for signatures by a C | CORPORATION): | |
|---|----------------|-------------------------|
| - | | Corporate Name |
| ATTEST: | | |
| (Assistant) Secretary | | (Vice) President |
| (CORPORATE SEAL) | | |
| (Use the following form for signatures by and | d INDIVIDUAL): | |
| | BY: | (Seal) |
| WITNESS: | | |
| | | |
| | | |
| (ACKNOWLEDGEMENT OF THE ABOVE S ON FOLLOWING PAGE) | SIGNATURE MUST | BE NOTARIZED USING FORM |

NONDISCRIMINATION CLAUSE

It is specifically agreed as part of the consideration of the signing of this Contract that the parties hereto, their agents, officials, employees or servants will not discriminate in any manner on the basis of age, handicap, race, color, creed, sexual orientation or national origin with reference to the subject matter of this Contract, no matter how remote.

This provision being incorporated for the benefit of Fayetteville Public Works Commission, Fayetteville, North Carolina and its residents may be enforced as set out in said ordinances, enforcement of this provision shall be by action for specific performance, injunctive relief, or other remedy as by law provided.

This provision shall be binding on the successors and assigns of the parties hereto with reference to the subject matter of this Contract.

(Printed Name)

NON-COLLUSIVE AFFIDAVIT

| State | e of) | | | |
|-------|---|--|---|--|
| Cour | nty of) | | | |
| | | | being first | duly sworn, |
| depo | oses and says that: | | | |
| (1) | He is the | | | |
| | (Owner, Partner, Office of | er, Representative o the | or Agent) BIDDER | that has |
| | ofsubmitted the attached BID; | | 2.222.1 | mac mac |
| (2) | He is fully informed respecting the preparation pertinent circumstances respecting such BIE | | e attached E | BID and of all |
| (3) | Such BID is genuine and is not a collusive o | r sham BID; | | |
| (4) | Neither the said BIDDER nor any of its office employees or parties in interest, including this connived or agreed, directly or indirectly, with a collusive or sham BID in connection with been submitted; or to refrain from bidding in manner, directly or indirectly, sought by acconference with any BIDDER, firm, or person or of any other BIDDER, or to fix any overhor the BID price of any other BIDDER, or to connivance, or unlawful agreement any accinterested in the proposed Contract; | s affiant, have in any any other BIDDER, the Contract for whiconnection with such greement or collusion to fix the price or pead, profit, or cost eto secure through all dvantage against (R | way colluded firm, or persich the attack Contract; or n, or comm rices in the a lements of the ny collusion, ecipient), or | d, conspired, con to submit ned BID has have in any unication, or attached BID ne BID price conspiracy, any person |
| (5) | The price or prices quoted in the attached B any collusion, conspiracy, connivance, or ur or any other of its agents, representatives including this affidavit. | nlawful agreement or | the part of | the BIDDER |
| | BY | | | |
| | ITS | | | |
| | s <u>-</u> | (1 | itle) | |
| Sub | bscribed and sworn to before me this d | ay of | , 20 | · |
| | | Notary I | Public | |
| Му | Commission Expires: | | | |
| | END OF AFFI | DAVIT | | |

F.T.A. CERTIFICATION REGARDING LOBBYING

Certification for Contracts, Grants, Loans, and Cooperative Agreements

(To be submitted with each bid or offer exceeding \$100,000)

The undersigned ____certifies, to the best of his or her knowledge and belief, that:

- (1) No federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of an agency, a member of Congress, an officer or employee of Congress, or an employee of a member of Congress in connection with the awarding of any federal contract, the making of any federal grant, the making of any federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any federal contract, grant, loan, or cooperative agreement.
- (2) If any funds other than federal appropriated funds have been paid or will be paid to any person for making lobbying contacts to an officer or employee of any agency, a member of Congress, an officer or employee of Congress, or an employee of a member of Congress in connection with this federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form--LLL, "Disclosure Form to Report Lobbying," in accordance with its instructions [as amended by "Government wide Guidance for New Restrictions on Lobbying," 61 Fed. Reg. 1413 (1/19/96). Note: Language in paragraph (2) herein has been modified in accordance with Section 10 of the Lobbying Disclosure Act of 1995 (P.L. 104-65, to be codified at 2 U.S.C. 1601, et seq .)]
- (3) The undersigned shall require that the language of this certification be included in the award documents for all subawards at all tiers (including subcontracts, subgrants, and contracts under grants, loans, and cooperative agreements) and that all subrecipients shall certify and disclose accordingly.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by 31, U.S.C. § 1352 (as amended by the Lobbying Disclosure Act of 1995). Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

[Note: Pursuant to 31 U.S.C. § 1352(c)(1)-(2)(A), any person who makes a prohibited expenditure or fails to file or amend a required certification or disclosure form shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such expenditure or failure.]

| The Contractor,, certifies or affirms the truthfulness and accuracy of each statement of its certification and disclosure, if any. In addition, the Contractor understands and agrees that the provisions of 31 U.S.C. A 3801, <i>et seq., apply</i> to this certification and disclosure, if any. | | |
|--|--|--|
| | _ Signature of Contractor's Authorized Official | |
| | _ Name and Title of Contractor's Authorized Official | |
| | _ Date | |
| | | |

CERTIFICATION OF PRIMARY PARTICIPANT REGARDING DEBARMENT, SUSPENSION AND OTHER RESPONSIBILITY MATTERS

| | imary Participant, ontractor), certifies to the best of its knowledge | (ma e and belief, that it and its principa | |
|--|--|--|---|
| 1. | Are not presently debarred, suspended, proportion voluntarily excluded from covered transactions | | |
| 2. | Have not within a three-year period preceding civil judgment rendered against them for conconnection with obtaining, attempting to obtain local) transaction or contract under a public antitrust statutes or commission of embezzler destruction or records, making false statement | ommission of fraud or a criminal in, or performing a public (Federa c transaction; violation of Federa ement, theft, forgery, bribery, fals | offense in al, State or al or State |
| 3. | Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated in paragraph (2) of this certification; and | | |
| 4. | Have not within a three-year period preceding this application/proposal had one or more public transactions (Federal, State or local) terminated for cause or default. | | |
| | primary participant is unable to certify to any pant shall attach an explanation to this certificat | | cation, the |
| THE PRIMARY PARTICIPANT CERTIFIES OR AFFIRMS THE TRUTHFULNESS AND ACCURACY OF THE CONTENTS OF THE STATEMENTS SUBMITTED ON OR WITH THIS CERTIFICATION AND UNDERSTANDS THAT THE PROVISIONS OF 31 U.S.C. SECTIONS 3801 ET. SEQ. ARE APPLICABLE THERETO. | | | |
| Signati | ure | Title | |
| Printed | l Name | Date | |



MINORITY, WOMEN, AND DISADVANTAGED BUSINESS ENTERPRISE PROGRAM

for

Construction, A&E Services, Purchase Contracts, Professional Services, and General Services

Contents

| PU: | RPOS | E | 4 |
|------|------------|--|----|
| ov | ERVI | EW | 4 |
| I. | INT | RODUCTION | 5 |
| II. | ADN | IINISTRATION | 5 |
| III. | DEF | INITIONS | 5 |
| | | CEDURES FOR CONSTRUCTION CONTRACTS | |
| | Α. | Purpose and Application | |
| | В. | MWDBE Aspirational Goals | 7 |
| | C. | Invitation for Bids | 7 |
| | D. | PWC Responsibilities | 8 |
| | E. | Contractor Good-Faith Efforts | 9 |
| | F. | Awarding of Construction Contracts | 11 |
| | G. | Counting MWDBE Participation Toward Meeting the Aspirational Goals | 12 |
| | Н. | Documentation of Attainment of MWDBE Participation Requirements | 13 |
| V. | | CEDURES FOR ARCHITECTURE & ENGINEERING (A&E) CONTRACTS | |
| | Α. | Purpose and Application | |
| | В. | MWDBE Aspirational Goals | |
| | C. | Request for Qualifications | |
| | D. | PWC Responsibilities | |
| | E. | Meeting MWDBE Aspirational Goals | |
| | F. | Counting MWDBE Participation | |
| | G. | Provider Good-Faith Efforts | |
| | Н. | Documenting Good-Faith Efforts | |
| VI. | PRO A. | CEDURES FOR PURCHASE CONTRACTSPurpose and Application | |
| | В. | MWDBE Aspirational Goals | |
| | C. | Request for Quotes or Invitation for Bids | |
| | D. | PWC Responsibilities | |
| | E. | Award of Purchase Contracts | |
| VII | | CEDURES FOR PROFESSIONAL, GENERAL (OTHER) SERVICE CONTRACTS | |
| V 11 | A . | Purpose and Application | |
| | В. | MWDBE Aspirational Goals | 20 |
| | C. | PWC's Responsibilities | 20 |
| | D. | Request for Proposals | 21 |
| | E. | Meeting MWDBE Aspirational Goals | 21 |
| | F. | Counting MWDBE Participation | 21 |

| G. | Provider Good-Faith Efforts | 22 |
|----------|--|----|
| I. | Documenting Good-Faith Efforts | 23 |
| VIII. | UTILIZATION OF JOINT VENTURE | 23 |
| IX. MW | DBE REPORTING PROCEDURE | 24 |
| MWDB | E COMPLIANCE PROVISIONS | 25 |
| Affidavi | t A: Listing of the Good Faith Efforts | 27 |
| Affidavi | t B: Intent to Perform Contract with Own Workforce | 28 |
| Affidavi | t C: Percentage of MWDBE Participation | 29 |
| Affidavi | t D: Good Faith Efforts | 31 |
| Affidavi | t E: Identification of MWDBE/Local Participation | 32 |
| MWDB | E ADD / CHANGE FORM | 33 |
| | | |

PURPOSE

The Fayetteville Public Works Commission (PWC) is committed to promoting the utilization of Minorities, Women, and Disadvantaged Businesses by providing equal opportunity for participating in all aspects of PWC's contracting and procurement programs, including but not limited to, construction projects, A&E services, purchase contracts, and professional and general (other) service contracts.

To achieve this purpose, PWC has established this Minority, Women, and Disadvantaged Business Enterprise Program (MWDBE) to support historically underutilized businesses, encourage capacity development, and offer procurement opportunities to certified business enterprises.

OVERVIEW

PWC's MWDBE Program is a voluntary goals program in construction, A&E services, purchase contracts, and professional and general (other) services based on "good-faith efforts." These goals are established for a five-year period and achievement will be evaluated annually.

The aspirational goals of PWC for the utilization of Minority, Women, and Disadvantaged Business Enterprises are:

| Minority business participation in construction services | 14% |
|---|-----|
| Women business participation in construction services | 11% |
| Minority business participation in A&E services | 6% |
| Women business participation in A&E services | 5% |
| Minority business participation in purchase contracts | 4% |
| Women business participation in purchase contracts | 4% |
| Minority business participation in professional services | 19% |
| Women business participation in professional services | 3% |
| Minority business participation in general (other) services | 9% |
| Women business participation in general (other) services | 4% |

I. INTRODUCTION

In 2021, Fayetteville Public Works Commission (PWC) contracted with Griffin & Strong, P.C. (GSPC) to conduct a Disparity Study to determine the effectiveness of the current policies related to local, minority, and women owned businesses and to recommend modifications and adjustments, if necessary, to PWC's policies that comply with the law.

PWC continues to implement race and gender conscious and race and gender-neutral measures to try to increase utilization of Minority, Women, and Disadvantaged Business Enterprise (MWDBE) firms. PWC has a basis to continue race and gender conscious remedies or policies toward achieving annual aspirational goals.

The MWDBE aspirational goals and guidelines developed and recommended do not require nor provide for racially based set-asides; rather they require good-faith effort by both local government and contractors to recruit and select minorities and women businesses, consistent with North Carolina Statues and the Constitution of the United States as interpreted by the Croson Decision.

II. ADMINISTRATION

PWC General Manager/CEO is authorized to take all usual and legal administrative actions necessary to implement this Program. The ultimate responsibility for the MWDBE Program administration is assigned to the PWC General Manager/CEO or its designee. PWC General Manager/CEO or its designee is either to be personally responsible or to designate a specific person to coordinate and manage this Program. PWC General Manager/CEO or its designee is responsible for determining whether a contractor has complied with this Program and shown good-faith efforts to do so. Except for those staff services specifically assigned by this Program to other departments, the heads of departments responsible for the construction, and procurement of services and goods shall be responsible to PWC General Manager/CEO or its designee and shall cooperate with PWC General Manager/CEO or its designee in implementing this Program.

The MWDBE Program shall apply to all construction contracts, A&E contracts, purchase contracts, and services as specified in Sections IV through VII. The provisions of this Program take precedence over any other department plans or procedures in conflict herewith, except specific requirements mandated by terms or conditions of agreements in force between PWC and the federal government or the State of North Carolina that require different procedures than those described in this Program. This Program will be evaluated at the end of five years to determine its effectiveness and what adjustments are required.

III. DEFINITIONS

Affirmative Action - Specific steps to eliminate discrimination and efforts to ensure nondiscriminatory results and practices in the future, and to fully involve Minority, Women, and Disadvantaged Business Enterprises in contracts and programs.

Aspirational Goal/Goal - A voluntary percentage or quantitative objective.

Bidder/Participant - Any person, firm, partnership, corporation, association, or joint venture seeking to be awarded a public contract or subcontract.

Contract - A mutually binding legal relationship or any modification thereof obligating the seller to furnish equipment or service, including construction and leases, and obligating the buyer to pay for them.

Contractor - Any person, firm, partnership, corporation, association, or joint venture that has been awarded a public contract or lease, including every subcontract on such a contract.

Day – A calendar day of 24 hours measured from midnight to the next midnight. Also referred to throughout the Program documents as "days or "calendar days."

Discrimination - To distinguish, differentiate, separate and/or segregate on the basis of age, race, religion, color, sex, national origin, handicap and/or veteran status.

Equipment - Includes materials, supplies, commodities, and apparatus.

Joint Venture - An association of two or more businesses to carry out a single business enterprise for profit, for which purpose they combine their property, capital, efforts, skills, and knowledge.

Lessee - A business that leases, or is negotiating to lease, property from PWC or equipment or services to PWC, or to the public on PWC property.

Minority - A person who is a citizen or lawful permanent resident of the United States and who is:

- a. Black American (a person having origins in any of the black racial groups of Africa);
- b. Hispanic American (a person of Mexican, Puerto Rican, Cuban, Central or South American, or other Spanish culture or origin, regardless of race);
- c. Portuguese (a person of Portuguese, Brazilian, or other Portuguese culture origin, regardless of race);
- d. Asian American (a person having origins in any of the original people of the Far East, Southeast Asia, the Indian sub-continent, or the Pacific Islands); and
- e. Native American (a person having origins in any of the original people of North America).

MWDBE - Any certified minority, women, and disadvantaged business enterprise.

Minority, Women, Disadvantaged Business Enterprise (MWDBE) - A business that is at least fifty-one (51) percent owned and controlled by minority group members or women. An MWDBE is **bona fide** only if the minority group or female ownership interests are real and continuing and not created solely to meet the MWDBE requirement. In addition, the MWDBE must itself perform satisfactory work or services or provide supplies under the contract and not act as a mere conduit. In short, the contractual

IV. PROCEDURES FOR CONSTRUCTION CONTRACTS

A. Purpose and Application

- 1. The general purpose of this Program is to help develop and support Minority, Women, and Disadvantaged Business Enterprises (MBE, WBE, and DBE) by providing opportunities for participation in the performance of all construction contracts financed entirely with PWC funds.
- 2. This Program shall apply to construction contracts when the PWC's estimated contract cost is \$100,000 or more, except when a contract is exempt from competitive bidding under the General Statutes of North Carolina. Contracts between \$30,000 and \$99,999.99 will also be covered by the exemption.
- 3. Where contracts are financed in whole or in part with federal or state funds, including grants, loans, or other funding sources containing MBE, WBE, DBE Programs, PWC will follow the federal government or the State of North Carolina. PWC General Manager/CEO or its designee will be responsible for monitoring the Program to ensure the goals are met.
- 4. Since PWC construction contracts are prepared by the Engineering and Facilities Departments, each of these departments shall prepare such documents with Procurement pre-approved templates for the bidding process, which includes the Program goals as required to implement this Program.
 - a. Within sixty (60) days of the Commission's approval of this Program, the departmental procedures and contract provisions shall be in effect for all bid documents issued after the date of Commission approval.

B. MWDBE Aspirational Goals

- 1. To implement the purpose of this Program, the goal shall be to award at least fourteen (14) percent of the total of all construction contract award amounts in each fiscal year to MBE firms and at least eleven (11) percent to WBE firms.
- PWC General Manager/CEO or its designee may determine that higher or lower goals are appropriate on a project-by-project basis, where it can be shown that the type, size, or location of the project will affect the availability of MBE, WBE, or DBE firms, so long as the aggregate of all contracts does not lower the annual goals.

C. Invitation for Bids

1. Bidders shall submit MWDBE information with their bids. Such information shall be subject to verification by MWDBE Program staff before awarding the contract. The information shall include the names of the MWDBEs to be used and the dollar value of each such MWDBE transaction.

 Contractors, subcontractors, suppliers, or MWDBE members of a joint venture intended to satisfy the PWC's MBE/WBE/DBE goals shall be certified by the State Department of Transportation (DOT) or North Carolina Office of Historically Underutilized Business (HUB).

D. PWC Responsibilities

1. MWDBE Directory – The MWDBE Program staff will establish and maintain a directory of certified Minority, Women, and Disadvantaged Business Enterprises. The purpose of the directory is to provide a resource for prime bidders on PWC construction projects who intend to solicit bids from MBE and WBE subcontractors and suppliers to meet PWC's MBE and WBE goals. The directory will not constitute a recommendation or endorsement of any listed firm.

The directory will be developed and maintained by the MWDBE Program Staff.

- a. The directory will include:
 - i. Business name, address, telephone number, and email address;
 - ii. Name(s) of business owner(s);
 - iii. Type of license;
 - iv. NAICS:
 - v. Type of MWDBE certification, and;
 - vi. Certification and expiration date with an acceptable agency.
- b. PWC shall advertise on a contract-by-contract basis throughout the year as deemed necessary for MWDBE outreach. Advertisements shall be placed with minority/women-focused publications (state and local). Notification will also be sent to community organizations which might have knowledge of MWDBE firms.
- c. The department heads and MWDBE Program staff should attend local and regional business fairs to promote the MWDBE Program. The departments shall also identify potentially eligible contractors through affirmative action efforts and the normal course of business. The names of identified contractors shall be forwarded to the MWDBE Program staff.
- 2. **MWDBE Eligibility Standards –** The eligibility of a business is determined by the ownership and control of the business.
 - a. An eligible Minority Business Enterprise owner is a citizen or lawful permanent resident of the United States, a member of a recognized ethnic or racial group, and fifty-one (51) percent owner of the business.
 - b. The eligible ethnic or racial groups are:
 - i. Black/African American
 - ii. Hispanic American
 - iii. Asian American

iv. Native American

- c. An eligible Women Business Enterprise owner is a citizen or lawful resident of the United States and a fifty-one (51) percent owner of the business and is female.
- Removal of MWDBE Procedures A contractor certified as a MWDBE may be removed from the program directory for, but not limited to, any of the following reasons:
 - a. Change of Status PWC General Manager/CEO or its designee may remove a MWDBE if he/she finds that the ownership or control of the business changes so that the business no longer meets the requirements of Section IV, D(2) (b) and (c) above.
 - b. **Failure to comply with the MWDBE Program** The certification of a business as a MWDBE may be removed by PWC General Manager/CEO or its designee if he/she finds any of the following conditions:
 - i. That a business has submitted inaccurate, false or incomplete information to PWC;
 - ii. That in performance of a contract, a business has failed to comply with requirements of the contract with PWC;
 - That in performance of a contract, a business has failed to comply with MWDBE requirements of a contract established by a contractor with PWC in response to PWC requirements; or
 - iv. That a business has otherwise failed to comply with the provisions of this MWDBE Program.
 - c. **Appeal of Removal -** A business may appeal a determination of a MWDBE by satisfying the eligibility requirements in Section IV, D (2) (b) and (c).
 - d. Pre-bid Meeting or Site Visit PWC may hold a pre-bid meeting on formal and informal bid contracts for all prospective bidders, subcontractors, and MWDBEs for the purpose of explaining the provisions of the MWDBE Program, the process for bidding, and the contract to be performed. Available data on MWDBEs interested and/or capable of engaging in the prospective contract shall be made available to prospective bidders, contractors, and subcontractors.

E. Contractor Good-Faith Efforts

The contractor (bidder) shall make good-faith efforts to encourage the participation of MWDBEs in projects prior to submission of bids in order to be considered as a responsive bidder. A good-faith effort shall include, at a minimum, specific affirmative action steps and complete documentation thereof. The following list of factors to determine good-faith effort is not exclusive or exhaustive:

1. Whether the bidder attended any pre-submittal or pre-bid meetings, if scheduled

by PWC;

- 2. Whether the bidder identified and selected specific items of the project for which the contract could be performed by Minority and/or Women Business Enterprises, to provide an opportunity for participation by those enterprises (including, where appropriate, breaking down contracts into economically feasible units to facilitate MWDBE participation);
- 3. Whether the bidder advertised, a reasonable time before the date the bids are opened, in one or more daily or minority weekly newspapers or trade associations (i.e., N.C. Minority Business Association), trade journals, or other media;
- 4. Whether the bidder provided email notice of their interest in bidding on the contract to at least three (3) Minority, Women, or Disadvantaged Business Enterprises (for each identified sub-item of the contract) licensed to provide the specific items of the project a reasonable time prior to the opening of bids;
- 5. Whether the bidder provided interested Minority, Women, and Disadvantaged Business Enterprises with information about the Plan, specifications, and requirements for the selected subcontracting or material supply work;
- 6. Whether the bidder contacted PWC's MWDBE Program staff for assistance in identifying minority and women businesses certified with approved public agencies as referenced in Section IV, D (2) (b) and (c);
- 7. Whether the bidder negotiated in good-faith with Minority, Women, or Disadvantaged Business Enterprises and did not unjustifiably reject as unsatisfactory bids prepared by a Minority, Women, or Disadvantaged Business Enterprises, as defined by PWC;
- 8. Whether the bidder, where applicable, advised and made efforts to assist interested MWDBEs in obtaining bonds, lines of credit, or insurance required by PWC or contractor:
- Whether the bidder's efforts to obtain MWDBEs participation could reasonably be expected by PWC to produce a level of participation sufficient to meet the goals of PWC.

Bidders are cautioned that even though their submittal indicates they will meet the MWDBE goals, they should document their good- faith efforts and be prepared to submit this information to protect their eligibility for award of the contract in the event PWC questions whether the good-faith requirement has been met.

10. Performance of MBE/WBE/DBE Subcontractors and Suppliers - The MWDBEs listed by the contractor on the Program Affidavits, which is determined by PWC to be certified, shall perform the work and supply the materials for which they are listed unless the contractor has received prior written authorization from PWC to perform the work with other forces or to obtain the materials from other sources.

The contractor shall enter into subcontracts and supply copies of all fully executed subcontracts with each MWDBE listed on the Program Affidavits to PWC's MWDBE Program staff after award of the contract and prior to the issuance of a Notice to Proceed. Any amendments to the subcontracts shall be submitted to the MWDBE Program staff within **five (5) days** of execution.

Authorization to utilize other forces or sources of materials shall be requested by submitting a "Change or Add a Subcontractor Form" for the following reasons:

- a. The listed MWDBE, after having had a reasonable opportunity to do so, fails or refuses to execute a written contract, when such written contract, based upon the general terms, conditions, plans and specifications for the project, or on the terms of such subcontractor's or supplier's written bid, is presented by the contractor.
- b. The listed MWDBE becomes bankrupt or insolvent.
- c. The listed MWDBE fails or refuses to perform his/her subcontract or furnish the listed materials.
- d. The work performed by the listed subcontractor is unsatisfactory according to industry standards and is not in accordance with the plans and specifications; or the subcontractor is substantially delaying or disrupting the progress of the work.

All "Change or Add a Subcontractor Forms" shall be accompanied by good faith efforts documentation as specified on the form.

F. Awarding of Construction Contracts

- 1. If a construction contract is to be awarded, it shall be awarded in accordance with North Carolina General Statutes to the lowest responsible bidder who complies with all of the prescribed requirements and either:
 - a. Made a good-faith effort to comply with these goals and requirements before the time bids are opened as described above. Where a goodfaith effort is claimed by the apparent lowest responsible bidder, the bidder shall be required to submit documentation WITHIN TWENTY-FOUR (24) HOURS OF PWC'S NOTIFICATION, which in most instances will occur the day of bid opening to show that the criteria for good-faith efforts have been met, or
 - b. Once a firm is determined to be an eligible MWDBE, and before the contract is awarded, the total dollar value to be paid to the MWDBE shall be evaluated by the MWDBE Program Staff to ensure that it is in accordance with the bidder's proposal.

If the evaluation shows that the bidder has misrepresented MWDBE participation or has not made a good-faith effort to meet the contract goals for MBE or WBE

participation, the bidder may be disqualified.

G. Counting MWDBE Participation Toward Meeting the Aspirational Goals

The degree of participation by MWDBE contractors, subcontractors, suppliers, or joint-venture partners in contract awards shall be counted in the following manner:

- 1. Once a firm is determined to be an eligible MWDBE contractor in accordance with this Program, the total dollar value of the contract awarded to the MWDBE is counted as participation.
- 2. The goals can be met by any certified MWDBE contractor, subcontractor, supplier, trucker, or joint-venture partner as listed in PWC and agency directory. All MWDBEs used to meet the goal must be certified by an approved agency and verified by PWC at the time of bid opening. Only certified firms can be counted toward the goal. The standard for certification is set forth in this Program.
- 3. The total dollar value of a contract with a disadvantaged business owned and controlled by a minority woman is counted toward either the minority goal or the goal for women, but not toward both. The contractor or MWDBE Program staff may choose the goal to which the value is applied.
- 4. In the case of a joint venture, the joint venture recipient or contractor may count toward its MWDBE goals a portion of the total dollar value of the contract that the MWDBE partner's participation in the joint-venture represents. Credit will be given equal to the minority partner's percentage of ownership in the joint venture. A MWDBE joint-venture partner must be responsible for a clearly defined portion of the work to be performed in addition to satisfying requirements for ownership and control.
- 5. A recipient or contractor may count toward its MWDBE goals only expenditures to MWDBEs whose ownership interests are real and continuing and not created solely to meet PWC's goals for participation, and that perform a commercially useful function in the work of a contract. A MWDBE is considered to perform a commercially useful function when it is responsible for execution of a distinct element of the work of a contract and carries out its responsibilities by actually performing, managing, and supervising the work involved. To determine whether a MWDBE is performing a commercially useful function, the MWDBE Program staff shall evaluate the amount of work subcontracted, industry practices, and other relevant factors. Consistent with normal industry practices, an MWDBE may enter into subcontracts. If a MWDBE contractor subcontracts a significantly greater portion of the work of the contract than would be expected on the basis of normal industry practices, the MWDBE shall be presumed not to be performing a commercially useful function. Evidence to rebut this presumption may be presented to the MWDBE Program staff. The MWDBE may present evidence to rebut this presumption. The MWDBE Program staff decision on the rebuttal of this presumption is subject to review by PWC General Manager/CEO or its designee. Once a contractor is determined to be an eligible MWDBE in accordance with this section, the total dollar value of the contract awarded to MWDBE is counted toward the applicable MWDBE goals, except as provided in

the provisions of this section.

6. A contractor may count toward its MWDBE goals expenditures for materials and supplies obtained from MWDBE suppliers and manufacturers, provided that the MWDBE assumes the actual and contractual responsibility for the provision of the materials and supplies.

H. Documentation of Attainment of MWDBE Participation Requirements

In order that PWC General Manager/CEO or its designee may make a recommendation to PWC as to the responsiveness of bidders, bidders shall be required to submit the following information on each MWDBE-related subcontract:

- A description of the subcontract and purchase(s) of significant equipment and supplies to be used to perform the subcontract or prime contract, including the name and address of each MWDBE firm selected, and the name and telephone number of a contact person;
- 2. The dollar amount of participation of each MWDBE;
- 3. A statement of intent from the MWDBE subcontractor or material supplier as:
 - a. Identified in Section IV, H(1) above that they intend to contract or supply the materials, or
 - b. Sworn statements, with appropriate documentation, showing that the contractor made a good-faith effort to comply with the MWDBE Program in accordance with Section IV, E of this Program.

V. PROCEDURES FOR ARCHITECTURE & ENGINEERING (A&E) CONTRACTS

A. Purpose and Application

- 1. The general purpose (goal) of this Program is to help develop and support MWDBEs by providing opportunities for participation in the performance of PWC's A&E contracts financed entirely with PWC funds.
- 2. This Program applies to all A&E contracts except contracts in those unique circumstances where written exemption of particular contracts is determined as an exception, and less than fifty thousand dollars (\$50,000.00) by PWC General Manager/CEO. PWC General Manager/CEO or its designee will be responsible for administering and monitoring the Program to ensure that appropriate action(s) are taken in efforts of achieving the goals.
- 3. Where contracts are funded in whole or in part with federal or state funds and the grants, loans, or other funding sources containing MWDBE Program requirements, PWC General Manager/CEO or its designee will be responsible for monitoring the Program to ensure the goals are met.

4. Since PWC Request for Qualifications (RFQ) are prepared by the Engineering and Facilities Departments, each of these departments shall prepare such documents with Procurement pre-approved templates for the qualification-based selection process, which includes the Program goals as required to implement this Program.

B. MWDBE Aspirational Goals

1. To implement this Program, the goal shall be to award six percent (6%) of the total A&E contract dollars awarded in each fiscal year to MBE firms and five percent (5%) to WBE firms. The goals will become effective on the date that PWC approves the Program and continue for a period of five (5) years.

C. Request for Qualifications

It is not required that contracts under \$50,000 meet the contract goal. When
possible, at least twenty-five (25) percent of the firms notified of the contract
opportunity shall be MWDBE. A list of available firms will be provided by the
MWDBE Program staff to the Procurement Advisor and Department. The
MWDBE Program staff shall track and report the firms that are notified and that
provide submittals.

D. PWC Responsibilities

1. Identification of MWDBE Firms

- a. The MWDBE Program staff will establish and maintain a directory of certified Minority, Women, and Disadvantaged Business Enterprises. The purpose of the directory is to provide a resource on PWC A&E projects. The directory will not constitute a recommendation or endorsement of any listed firm. The directory will be developed and maintained by the MWDBE Program Staff.
- b. The directory will include:
 - i. Business name, address, telephone number, and email address;
 - ii. Name(s) of business owner(s);
 - iii. Type of license;
 - iv. NAICS;
 - v. Type of MWDBE certification, and;
 - vi. Certification and expiration date with an acceptable agency.
- c. PWC shall advertise on a contract-by-contract basis throughout the year as deemed necessary for MWDBE outreach. Advertisements shall be placed with minority/women-focused publications (state and local). Notification will also be sent to community organizations which might have knowledge of MWDBE firms.

d. The department heads and MWDBE Program staff should attend local and regional business fairs to promote the MWDBE Program. The departments shall also identify potentially eligible firms through affirmative action efforts and the normal course of business. The names of identified firms shall be forwarded to the MWDBE Program staff.

E. Meeting MWDBE Aspirational Goals

1. Goals must be met by awarding contracts to certified MWDBE firms. The MWDBE must be certified at the time of the contract award. MWDBE firms not certified at the time of the contract award will not be counted towards MWDBE goals. MWDBE goals may be met by a certified joint venture or partnership. In the case of joint ventures or partnerships, MWDBE participation counted toward the goal will be equal to the percentage of the total dollar value of the contract that the MWDBE partner is responsible for performing.

F. Counting MWDBE Participation

- The total dollar value of a contract with a disadvantaged business owned and controlled by a minority woman is counted toward either the minority goal or the goal for women, but not toward both. The contractor or MWDBE Program staff may choose the goal to which the value is applied.
- 2. If a determination is made by the MWDBE Program staff that the goals have not been met, the prime service provider will be required to submit a good-faith effort statement prior to PWC awarding the contract.

G. Provider Good-Faith Efforts

The following is a list of the efforts that should be made by the prime A&E firm to encourage MWDBE participation. In order to receive credit for having made "good faith efforts", the prime A&E firm should document all actions taken to include the following:

- 1. Attending pre-bid meetings scheduled by the department;
- 2. Identifying selected specific items of the project which could be executed by a MWDBE:
- 3. Soliciting MWDBE A&E firm participation in a reasonable time before the solicitations are due through advertisements in circulation media, trade publications, and minority-focused media;
- 4. Contacting local firms, firms owned by minorities or women, and associations or business development centers which disseminate information to local businesses and businesses owned by minorities or women in a timely manner to allow sufficient time for MWDBEs to respond;
- 5. Following up on initial solicitations of interest by contacting the MWDBE to determine whether the MWDBE was interested in performing specific items of the

project;

- 6. Attempting to enter into joint venture or partnership arrangements with MWDBEs and provide interested MWDBEs with information about the requirements for the project;
- 7. Providing assistance to MWDBEs in the review of qualification submittal and work to be done by sub-A&E firms;
- 8. Using available directories of certified MWDBEs and other available resources;
- 9. Ensuring that the firm negotiated in good faith with the MWDBE and did not unjustifiably reject as unsatisfactory qualifications prepared by any Minority, Women, or Disadvantaged Business Enterprise;
- 10. Making every effort to obtain Minority, Women, or Disadvantaged Business Enterprise participation that could reasonably be expected to produce a level of participation sufficient to meet the goals of PWC; and
- 11. Providing interested minority, women, and disadvantaged businesses with information relative to project requirements.

H. Documenting Good-Faith Efforts

If the prime A&E firm does not meet the goals for MWDBE participation at the time of qualification submittal, then the following documents indicating "good-faith efforts" should be submitted as a minimum:

- A report of all proposals received by the prime service provider from MWDBE sub-A&E firms must indicate the action taken by the prime A&E firm in response to the qualification submittal. In cases where proposals have been rejected, the reason for rejection must be indicated.
- 2. Documentation of efforts to enter into agreements with MWDBEs for sub-A&E work or arrangements for joint ventures, partnerships, or other multi-entity relationships. Also included should be a statement of why agreements or arrangements were not made.
- 3. Proof of contact with MWDBEs and associations or business development centers that disseminate information to MWDBEs.
- 4. A copy of emails or notices sent to groups in Section VI, J(3) above notifying them of the firm's intent to submit a qualification submittal to PWC. The emails or notices should indicate the areas of work available for sub-A&E firms.
- 5. Description of assistance provided to MWDBEs in review of the qualification submittal and work to be done by sub-A&E firms.
- 6. Description of the use made by firms of available resources such as directories of MWDBEs.

- 7. Documentation of advertisements sent to general circulation media, trade publications, and minority-focused media.
- 8. Proof of attendance at any pre-bid meeting.

If the prime A&E firm fails to meet the MWDBE goals with its proposed project team and cannot provide documentation of "good-faith efforts", these failures will be noted to the involved department by the MWDBE Program Staff, and the firm may be disqualified.

VI. PROCEDURES FOR PURCHASE CONTRACTS

A. Purpose and Application

- The general purpose of this Program is to help develop and support Minority, Women, and Disadvantaged Business Enterprises (MBE, WBE, and DBE) by providing opportunities for participation in purchase contracts financed entirely with PWC funds.
- 2. This Program shall apply to purchase contracts over \$30,000 for apparatus, materials, supplies and purchase contracts for goods where the patent-holder is not the sole supplier. PWC General Manager/CEO or its designee will be responsible for monitoring the Program to ensure the goals are met.
- 3. Where contracts are funded in whole or in part with federal or state funds and the grants, loans, or other funding sources containing MWDBE Program requirements, PWC General Manager/CEO or its designee will be responsible for monitoring the Program to ensure the goals are met.
- 4. Since PWC purchase contracts are prepared by various departments, each of these departments shall prepare such documents with Procurement preapproved templates for the quote or bid process, which includes the goals as required to implement this Program. PWC Departments shall document and provide to the MWDBE Program staff a list of all providers notified and responses received for informal purchases.

B. MWDBE Aspirational Goals

 To implement the purpose of this Program, the goal shall be to award at least four (4) percent of the total of all purchase contract award amounts in each fiscal year to MBEs and at least four (4) percent to WBE firms. It is further the intent of PWC to encourage, to the extent allowed the use of local vendors (defined as located within Cumberland, Hoke, or Harnett County) whenever doing so is consistent with the requirements under G.S. 143-129.

C. Request for Quotes or Invitation for Bids

 The various departments soliciting goods will be responsible for contacting from the directory at least one MBE and one WBE for a price quotation of \$30,000 or more on each purchase contract with MWDBE availability. 2. A list of available MWDBEs will be provided by the MWDBE Program staff to the Procurement Advisor and Department. The MWDBE Program staff shall track and report the MWBDEs that are notified and that provide submittals.

D. PWC Responsibilities

1. Identification of MWDBEs

- a. The MWDBE Program staff will establish and maintain a directory of certified Minority, Women, and Disadvantaged Business Enterprises. The purpose of the directory is to provide a resource for on PWC purchase contracts. The directory will not constitute a recommendation or endorsement of any listed supplier. The directory will be developed and maintained by the MWDBE Program Staff.
- b. The directory will include:
 - i. Business name, address, telephone number, and email address:
 - ii. Name(s) of business owner(s);
 - iii. NAICS:
 - iv. Type of MWDBE certification, and;
 - v. Certification and expiration date with an acceptable agency.
- c. PWC shall advertise on a contract-by-contract basis throughout the year as deemed necessary for MWDBE outreach. Advertisements shall be placed with minority/women-focused publications (state and local). Notification will also be sent to community organizations which might have knowledge of MWDBE suppliers.
- d. The department heads and MWDBE Program staff should attend local and regional business fairs to promote the MWDBE Program. The departments shall also identify potentially eligible suppliers through affirmative action efforts and the normal course of business. The names of identified suppliers shall be forwarded to the MWDBE Program staff.
- 2. **MWDBE Eligibility Standards –** The eligibility of a business is determined by the ownership and control of the business.
 - a. An eligible Minority Business Enterprise owner is a citizen or lawful permanent resident of the United States, a member of a recognized ethnic or racial group, and fifty-one (51) percent owner of the business.
 - b. The eligible ethnic or racial groups are:
 - i. Black/African American
 - ii. Hispanic American
 - iii. Asian American
 - iv. Native American

- c. An eligible Women Business Enterprise owner is a citizen or lawful resident of the United States and a fifty-one (51) percent owner of the business and is female.
- Removal of MWDBE Procedures A supplier certified as a MWDBE may be removed from the program directory for, but not limited to, any of the following reasons:
 - a. Change of Status PWC General Manager/CEO or its designee may remove a MWDBE if he/she finds that the ownership or control of the business changes so that the business no longer meets the requirements of Section IV, D(2) (b) and (c) above.
 - b. Failure to comply with the MWDBE Program The certification of a business as a MWDBE may be removed by PWC General Manager/CEO or its designee if he/she finds any of the following conditions:
 - i. That a business has submitted inaccurate, false or incomplete information to PWC;
 - ii. That in performance of a contract, a business has failed to comply with requirements of the contract with PWC;
 - iii. That in performance of a contract, a business has failed to comply with MWDBE requirements of a contract established by a contractor with PWC in response to PWC requirements; or
 - iv. That a business has otherwise failed to comply with the provisions of this MWDBE Program.
 - c. Appeal of Removal A business may appeal a determination of a MWDBE by satisfying the eligibility requirements in Section IV, D (2) (b) and (c).
 - d. Pre-bid Meeting or Site Visit PWC may hold a pre-bid meeting on formal and informal bid contracts for all prospective bidders, subcontractors, and MWDBEs for the purpose of explaining the provisions of the MWDBE Program, the process for bidding, and the contract to be performed. Available data on MWDBEs interested and/or capable of engaging in the prospective contract shall be made available to prospective bidders, contractors, and subcontractors.

E. Award of Purchase Contracts

1. If a purchase contract is to be awarded, it shall be awarded in accordance with North Carolina General Statutes and/or other applicable PWC, Commission, and State regulations.

VII. PROCEDURES FOR PROFESSIONAL, GENERAL (OTHER) SERVICE CONTRACTS

A. Purpose and Application

- The general purpose (goal) of this Program is to help develop and support MWDBEs by providing opportunities for participation in the performance of PWC's professional service contracts and general (other) service contracts (hereinafter referred to as service contracts).
- 2. This Program applies to all service contracts except contracts under \$30,000, and in those unique circumstances where PWC General Manager/CEO or its designee determines that an exception is necessary.
- 3. Where contracts are funded in whole or in part with federal or state funds and the grants, loans, or other funding sources containing MWDBE Program requirements, PWC General Manager/CEO or its designee will be responsible for monitoring the Program to ensure the goals are met.
- 4. PWC General Manager/CEO or its designee will be responsible for administering and monitoring the Program to ensure that appropriate action(s) are taken in efforts of achieving the goals.

B. MWDBE Aspirational Goals

1. To implement this Program, the goal shall be to award nine percent (9%) of the total service contract dollars awarded in each fiscal year to MBE firms and four percent (4%) to WBE firms. The goals will become effective on the date that PWC approves the Program and continue for a period of five (5) years.

C. PWC's Responsibilities

1. Identification of MWDBE Firms

- a. The MWDBE Program staff shall establish and maintain a directory of certified MWDBE service providers that shall be made available to all departments to assist them in identifying appropriate MWDBE service providers that can be used to meet PWC's MWDBE goals. The directory shall include the businesses which provide the services routinely procured by PWC and the NAICS which the businesses are capable of providing. The directory will not constitute a recommendation or endorsement of any listed business. The directory will include:
 - i. Business name, address, and telephone number;
 - ii. Name(s) of business owner(s);
 - iii. NAICS of services available;
 - iv. Type of MWDBE certification, and;
 - v. Certification and expiration date with an acceptable agency.
- b. PWC shall provide a list of opportunities at least 30 days prior to each fiscal year (July) for MWDBE service providers. Advertisements shall

- be placed with minority/women-focused publications (state and local). Notification will also be sent to community organizations that might have knowledge of MWDBE firms. Interested MWDBEs shall provide a letter of interest within **14 calendar days** of the advertisement.
- c. For opportunities that arise throughout the fiscal year, PWC shall provide an Advertisement for opportunity to but not limited to MWDBE service providers within the MWDBE directory and identified MWDBEs from the Disparity Study. Advertisements shall be placed with minority/women-focused publications (state and local). Notification will also be sent to community organizations that might have knowledge of MWDBE firms. Interested MWDBEs shall provide a letter of interest within 7 calendar days.
- d. The department heads and MWDBE Program staff should attend local and regional business fairs to promote the MWDBE Program. The departments shall also identify potentially eligible service providers through affirmative action efforts and the normal course of business. The names of identified businesses shall be forwarded to the MWDBE Program staff.

D. Request for Proposals

- 1. MWDBE contract goals shall be set for service contracts over \$30,000.00. The request for proposals shall state the contract goals of four (4) percent for both MWDBE Professional and General Service contractors.
- 2. Contracts under \$30,000 and contracts without letters of interest are not required to meet the contract goal.
- A list of available service providers will be provided by the MWDBE Program staff
 to the Procurement Advisor(s) and department(s). The MWDBE Program staff
 shall track and report the service providers that are notified and that provide
 proposals.

E. Meeting MWDBE Aspirational Goals

1. Goals must be met by awarding contracts to certified MWDBE service providers. The MWDBE must be certified at the time of the contract award. MWDBE service providers not certified at the time of the contract award will not be counted towards MWDBE goals. MWDBE goals may be met by a certified joint venture or partnership. In the case of joint ventures or partnerships, MWDBE participation counted toward the goal will be equal to the percentage of the total dollar value of the contract that the MWDBE partner is responsible for performing.

F. Counting MWDBE Participation

 The total dollar value of a contract with a disadvantaged business owned and controlled by a minority woman is counted toward either the minority goal or the goal for women, but not toward both. The contractor or MWDBE Program staff may choose the goal to which the value is applied.

2. If a determination is made by the MWDBE Program staff that the goals have not been met, the prime service provider will be required to submit a good-faith effort statement prior to PWC awarding the contract.

G. Provider Good-Faith Efforts

The following is a list of the efforts that should be made by the prime service provider to encourage MWDBE participation. In order to receive credit for having made "good faith efforts", the prime service provider should document all actions taken to include the following:

- 1. Attending pre-bid meetings scheduled by the department;
- Identifying selected specific items of the project which could be executed by a MWDBE;
- 3. Soliciting MWDBE service provider participation in a reasonable time before the proposals are due through advertisements in circulation media, trade publications, and minority-focused media;
- 4. Contacting local firms, firms owned by minorities or women, and associations or business development centers which disseminate information to local businesses and businesses owned by minorities or women in a timely manner to allow sufficient time for MWDBEs to respond;
- 5. Following up on initial solicitations of interest by contacting the MWDBE to determine whether the MWDBE was interested in performing specific items of the project;
- Attempting to enter into joint venture or partnership arrangements with MWDBEs and provide interested MWDBEs with information about the requirements for the project;
- 7. Providing assistance to MWDBEs in the review of proposals and work to be done by sub-service providers;
- 8. Using available directories of certified MWDBEs and other available resources;
- Ensuring that the proposer negotiated in good faith with the MWDBE and did not unjustifiably reject as unsatisfactory quotes prepared by any Minority, Women, or Disadvantaged Business Enterprise;
- 10. Making every effort to obtain Minority, Women, or Disadvantaged Business Enterprise participation that could reasonably be expected to produce a level of participation sufficient to meet the goals of PWC; and
- 11. Providing interested minority, women, and disadvantaged businesses with information relative to project requirements.

I. Documenting Good-Faith Efforts

If the prime service provider does not meet the goals for MWDBE participation at the time the proposals are due, then the following documents indicating "good-faith efforts" should be submitted as a minimum:

- A report of all proposals received by the prime service provider from MWDBE sub-providers must indicate the action taken by the prime service provider in response to the proposal. In cases where proposals have been rejected, the reason for rejection must be indicated.
- Documentation of efforts to enter into agreements with MWDBEs for sub-provider work or arrangements for joint ventures, partnerships, or other multi-entity relationships. Also included should be a statement of why agreements or arrangements were not made.
- 3. Proof of contact with MWDBEs and associations or business development centers that disseminate information to MWDBEs.
- 4. A copy of emails or notices sent to groups in Section VI, J(3) above notifying them of the firm's intent to submit a qualification submittal to PWC. The emails or notices should indicate the areas of work available for sub-providers.
- 5. Description of assistance provided to MWDBEs in review of the qualification submittal and work to be done by the sub-provider.
- Description on use made by firms of available resources such as directories of MWDBEs.
- 7. Documentation of advertisements sent to general circulation media, trade publications, and minority-focused media.
- 8. Proof of attendance at any pre-bid meeting.

If the prime service provider fails to meet the MWDBE goals with its proposed project team and cannot provide documentation of "good-faith efforts", these failures will be noted to the involved department by the MWDBE Program Staff, and the service provider may be disqualified.

VIII. UTILIZATION OF JOINT VENTURE

PWC is committed to promoting the utilization of joint venturing amongst business enterprises and to support, encourage, and offer procurement opportunities to support utilization when available so that business enterprises can meet capacity development.

The purpose of Joint Venturing is to connect high potential MWDBEs with a Prime Contractor that will supplement their growth and development. Joint Venturing is seen as an important approach to help MWDBEs compete for larger contracts. PWC conducts many outreach events to connect certified MWDBEs with PWC decision makers and prime contractors. PWC shall provide targeted outreach, training, and technical support

to MWDBEs and urge Prime contractors to provide an equivalent level of outreach and support when joint venturing is available. PWC's mission is to provide an innovative program to the industry that focuses on the accelerated growth of diverse partnerships.

IX. MWDBE REPORTING PROCEDURE

- 1. The MWDBE Program staff shall submit quarterly progress reports to PWC Departments. The quarterly progress reports shall be prepared by the MWDBE Program staff from information (i.e. pay applications, MWDBE forms, and requisition checklist form) submitted by each department involved in procurement within thirty (30) days following the period (each quarter). Progress reports shall indicate the type of procurement contract (i.e., construction, A&E, purchase, professional services, or general services) and shall include the following:
 - vi. Number and dollar value of total procurement contracts;
 - vii. Number and dollar value of all procurement contracts awarded to MWDBEs by the department;
 - viii. Where goals are not met, the progress report shall specify the reasons and include recommendations for increasing participation.
- PWC General Manager/CEO or its designee shall submit an annual report to Commission. The report shall include the total number of procurement contracts by departments and the dollar value of all contracts with MWDBE participation. The level of MWDBE participation shall be reported annually.

FAYETTEVILLE PUBLIC WORKS COMMISSION'S MWDBE COMPLIANCE PROVISIONS

APPLICATION:

The requirements of Fayetteville Public Works Commission (PWC) Minority, Women, and Disadvantaged Business Enterprise (MWDBE) Program for participation specific contracts are hereby made part of the Contract Documents. Copies of the Program may be obtained from:

Fayetteville Public Works Commission Economic Inclusion Programs P.O. Box 1089 Fayetteville, North Carolina 28302 Phone (910) 223-4016 Fax (910) 483-1429 E-mail: ElProgram@faypwc.com

NCDOT DBE Directory: <u>www.ebs.nc.gov/VendorDirectory</u>
HUB Directory: <u>https://ncadmin.nc.gov/businesses/hub</u>

MWDBE Compliance Requirements:

- The Bidder shall provide, with their Bid Form, at the time bids are due, the
 documents set forth below, properly executed. Returning executed copies
 indicates and establishes that the Bidder understands and agrees to any
 incorporated MWDBE contract provisions.
- 2. All Bidders must provide with their Bid Form, at the time bids are due, a properly completed and executed copy of either:
 - Affidavit A Listing of Good-Faith Efforts OR
 - *Affidavit B Intent to Self-Perform with Own Workforce.
 - *Affidavit B should **only** be used if the Contractor will perform **ALL Elements** of the Work on this project with their own forces **AND** will complete **ALL Elements** of this project **WITHOUT** the use of subcontractors, material suppliers, or providers of professional services.
- 3. Upon being identified as the apparent lowest responsive, responsible Bidder, a Bidder shall, within <u>twenty-four (24) hours</u> of PWC's notification provide a properly completed and executed copy of <u>either</u>:
 - Affidavit C Percentage of MWDBE Participation OR
 - Affidavit D Good-Faith Efforts.
- 4. All Bidders must provide with their Bid Form, at the time bids are due, a properly completed and executed copy of Affidavit E- Identification of MWDBE/Local Participation Form

All written statements, certifications, or intentions made by the Bidder shall become a part of the agreement between the Contractor and Fayetteville Public Works Commission for performance of this contract.

SUBCONTRACTOR PAYMENT REQUIREMENTS:

North Carolina General Statutes 143-134.1 (N.C.G.S.) states that the percentage of retainage on payments made by the prime contractor to the subcontractor shall not exceed the percentage of retainage on payments made by the Fayetteville Public Works Commission to the prime contractor. Failure to comply with this provision shall be considered a breach of the contract, and the contract may be terminated in accordance with the termination provisions of the contract.

The Contractor shall provide an itemized statement of payments to each MWDBE subcontractor before final payment is processed.

The Contractor shall provide an itemized statement of payments to each NON-MWDBE subcontractor before final payment is processed.

| Contractor | |
|--------------|-------------------|
| Signature | |
| Printed Name | <u>,</u> Title |
| Date | |

Affidavit A: Listing of the Good Faith Efforts

| Affidavit of | |
|--------------|------------------|
| _ | (Name of Bidder) |

I have made a good faith effort to comply under the following areas checked:

| i nave made a | i good faith effort to compl | y under the following areas checked: | | |
|-----------------|---|---|--|--|
| Total Available | Total Available GFE Points: 155 Minimum Number GFE Points Required: 50 | | | |
| Points | | | | |
| 10 | quote and that were known to the government-maintained lists at le notifying them of the nature and | hat reasonably could have been expected to submit a e contractor or available on State or local east 10 days before the bid or proposal date and scope of the work to be performed. | | |
| 10 | Making the construction plans, specifications and requirements available for review by prospective minority businesses or providing these documents to them at least 10 days before the bid or proposals are due. | | | |
| 15 | Breaking down or combining eler facilitate minority participation. | ments of work into economically feasible units to | | |
| 10 | | munity, or contractor organizations identified by the ed Businesses and included in the bid documents that of minority businesses. | | |
| 10 | Attending any pre-bid meetings s | scheduled by the public owner. | | |
| 20 | Providing assistance in getting re to bonding or insurance for subco | equired bonding or insurance or providing alternatives ontractors. | | |
| 15 | as unqualified without sound reas | erested minority businesses and not rejecting them sons based on their capabilities. Any rejection of a of qualification should have the reasons documented | | |
| 25 | equipment, loan capital, lines of c supplies, or letters of credit, inclu Assisting minority businesses in | wise qualified minority business in need of credit, or joint pay agreements to secure loans, iding waiving credit that is ordinarily required. obtaining the same unit pricing with the bidder's y businesses in establishing credit. | | |
| 20 | Negotiating joint venture and partnership arrangements with minority businesses in order to increase opportunities for minority business participation on a public construction or repair project when possible. | | | |
| 20 | Providing quick pay agreements suppliers to meet cash-flow demands | and policies to enable minority contractors and ands. | | |
| Total GFE Poin | nts (Claimed by Bidder): | Total GFE Points (Assessed by PWC): | | |

In accordance with NCGS 143-128.2(d) the undersigned will enter into a formal agreement with the firms listed in the Identification of Small Disadvantaged Business Participation schedule conditional upon execution of a contract with the Owner. Failure to abide by any applicable statutory provision may constitute a breach of the contract. The undersigned hereby certifies that he or she has read the terms of the MWDBE business commitment and is authorized to bind the Bidder to the commitment herein set forth.

| Date: | Name of Authorized Officer: | |
|----------|--|--|
| | State of North Carolina, County of | |
| (SEAL) | Subscribed and sworn to before me thisday of20 Notary Public | |
| | My commission expires | |

Affidavit B: Intent to Perform Contract with Own Workforce

| Affidavit of | |
|--------------------------------------|---|
| | (Name of Bidder) |
| I hereby certify that it is our inte | nt to perform 100% of the work required for contract: |
| | (Name of Project) |

In making this certification, the Bidder states that the Bidder does not customarily subcontract elements of this type project, and normally performs and has the capability to perform and will perform all elements of the work on this project with his/her own current workforces; and will complete all elements of this project without the use of subcontractors, material suppliers, or providers of professional services.

The Bidder agrees to provide any additional information or documentation requested by the Owner in support of the above statement.

The undersigned hereby certifies that he or she has read this certification and is authorized to bind the Bidder to the commitments herein contained.

| Date: | Name of Authorized Officer: |
|-------|--|
| SEAL | State of North Carolina, County ofday of 20 Subscribed and sworn to before me thisday of 20 Notary Public My commission expires |
| | |

ATTACH TO BID ATTACH TO BID ATTACH TO BID

Affidavit C: Percentage of MWDBE Participation

| Affidavit of | | | | |
|--|--------------------|--------------------|-----------------------|----------------|
| | (Nam | e of Bidder) | | |
| I hereby certify that on contract: | | | | |
| | | e of Project) | | |
| | | | | |
| \$ | | | | |
| | (Dollar Aı | mount of Total Bio | d) | |
| I will expend a minimum of% Disadvantaged Business Enterprises (M providers of professional services. Such | WDBE). MWD | BEs will be emplo | oyed as subcontractor | s, vendors, or |
| Name, Address, & Phone No. | *MWDBE Category | <u>NAICS</u> | <u>Dollar Value</u> | % of Contract |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |

^{*}MWDBE categories: Black-African Americans (B), Hispanic-Americans (H), Asian- Americans (A), Native-Americans (I), Women (F), Socially/Economically Disadvantaged (D)

Pursuant to NCGS 143-128.2(d), the undersigned will enter into a formal agreement with MWDBEs for work listed in this schedule conditional upon execution of a contract with the Owner. Failure to fulfill this commitment may constitute a breach of the contract.

The undersigned hereby certifies that he or she has read the terms of this commitment and is authorized to bind the Bidder to the commitment herein set forth.

| Date: | Name of Authorized Officer: |
|-------|--|
| | State of North Carolina, County of |
| SEAL | Subscribed and sworn to before me thisday20 Notary Public |
| | My commission expires |

Affidavit D: Good Faith Efforts

If Owner determines using reasonable discretion that Affidavit C is insufficient, Bidder agrees to provide the following information regarding any good-faith efforts.

| Name, Address, & Phone No. | *MWDBE Category | NAICS | Dollar Value |
|----------------------------|-----------------|-------|--------------|
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |
| | | | |

*MWDBE categories: Black-African Americans (B), Hispanic-Americans (H), Asian- Americans (A), Native-Americans (I), Women (F), Socially/Economically Disadvantaged (D)

Bidder may be requested to provide documentation of the Bidder's good-faith efforts. Examples of documentation may include the following:

- a. Copies of solicitations for quotes to MWDBEs. Each solicitation may include a specific description of the work to be subcontracted, location where bid documents can be reviewed, representative of the Prime Bidder to contact, and location, date and time when quotes must be received.
- b. Copies of guotes or responses received from each firm responding to the solicitation.
- c. A telephone log of follow-up calls to each firm sent a solicitation.
- d. For subcontracts where a MWDBE is not considered the lowest responsible sub- bidder, copies of quotes received from all firms submitting quotes for that particular subcontract.
- e. Documentation of any contacts or correspondence to MWDBE, community or contractor organizations in an attempt to meet the goal.
- f. Copy of pre-bid roster.
- g. Letter documenting efforts to provide assistance in obtaining required bonding or insurance for MWDBEs.
- h. Letter detailing reasons for rejection of a MWDBE due to lack of qualification.
- Letter documenting proposed assistance offered to MWDBEs in need of equipment, loan capital, lines of credit, or joint pay agreements to secure loans, supplies, or letter of credit, including waiving credit that is ordinarily required.

Failure to provide the documentation as listed in these provisions may result in rejection of the bid and award to the next lowest responsible and responsive Bidder.

| Date: | Name of Authorized Officer: | |
|----------|--|--|
| | State of North Carolina, County of | |
| (SEAL) | Subscribed and sworn to before me thisday20 Notary Public | |
| | My commission expires | |

Affidavit E: Identification of MWDBE/Local Participation

| | (Name | of Bidder) | | |
|--|--|--|--------------|-----------------------------|
| I hereby certify that on contra | act: | | | |
| | (Name | of Project) | | |
| We will use the following Minor Local (Cumberland, Hoke, Harr providers of professional service | nett County) as construc | • | | • |
| Name, Address, & Phone | No. *MWDBE Cate | egory / **Local | NAICS | <u>Dollar Value</u> |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| | | | | |
| *MWDBE categories: Black-Afr Americans (I), Women (F), Soc **Local: Fayetteville Metropolita County, and Harnett County. P use of local entities will not be Program. | cially/Economically Disact an Statistical Area (MSA WC is requesting this in | dvantaged (D) Somprising of Conformation for repo | umberland Co | ounty, Hoke es only, and |
| The total value of MWDBE | /local business cont | racting will be \$ | | |
| Date: | Name of Autho | orized Officer: _ | | |
| | State of North Carolina | - | | |
| (SEAL) | Subscribed and sworn Notary Public | | | |
| | My commission expire | s | | |

FAYETTEVILLE PUBLIC WORKS COMMISSION MWDBE ADD / CHANGE FORM

If a MWDBE subcontractor fails to complete work under the subcontract for any reason, the recipient must require the prime contractor to employ the good faith efforts set forth in the MWDBE Program if soliciting a replacement or additional subcontractor.


For MWDBE Change Request, please provide all information below:

| Prime Contractor: | | | |
|--|---|---|---|
| Subcontracted Work: | | | |
| Previous Subcontractor: Reason this for change requ | | | |
| | | | |
| New Subcontractor: | | MW[| DBE Category: |
| To Add MWDBE Subcontra | actor/Subcontra | cted work: | |
| Project Bid Information subroriginal MWDBE instructions firms contacted to perform the not reasonably available firm | nittal, then good f s indicate. Please his work along wit ns in the work are ullest extent prac | faith efforts to solicit a M' e provide all good faith ef th any additional good fa ea. PWC's MWDBE Prog ticable. If solicitations we | not documented in the original NDBE must be documented, as the forts below showing all the MWDB ith efforts or evidence that there ar ram requires that good faith efforts are not carried out due to being |
| Name, Address, & Conta | ct Information | MBE or WBE and Certifying agency | How was this firm contacted (email, letter, or Phone) and what was the result of the solicitation? * |
| | | | |
| | | | |
| *Must submit copies of emails o | r letters. If phone ca | alls were made this sheet ca | n serve as documentation of calls |
| Date: | Name | of Authorized Office | r: |
| | State of Nort | th Carolina, County of | |
| (SEAL) | Notary Publi | c | |
| | My commiss | sion expires | |

SMALL LOCAL SUPPLIER / MWDBE SUBCONTRACTOR DISCLOSURE FORM

| Contractor: | | |
|--|------------------------------|---|
| Address & Phone: | | |
| Project: | | |
| Name: | | |
| Pay Application # | | |
| Please complete the below form by providing to each subcontractor, vendor, or supplier for tapplication. This form must be fully completed | the work associated with the | e identified pay |
| Firm Name, Address, and Contact Information | Payment Amount | Type of Work/Commodity (Include NAICS Code) |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| | | |
| Signature | _ | |
| Printed Name | Title | _ |
| Date | _ | |
| | | |

| SECTION B - CONTRACT EXECUTION DOCUMENTS | |
|--|--|
| | |
| | |
| | |
| | |
| | |

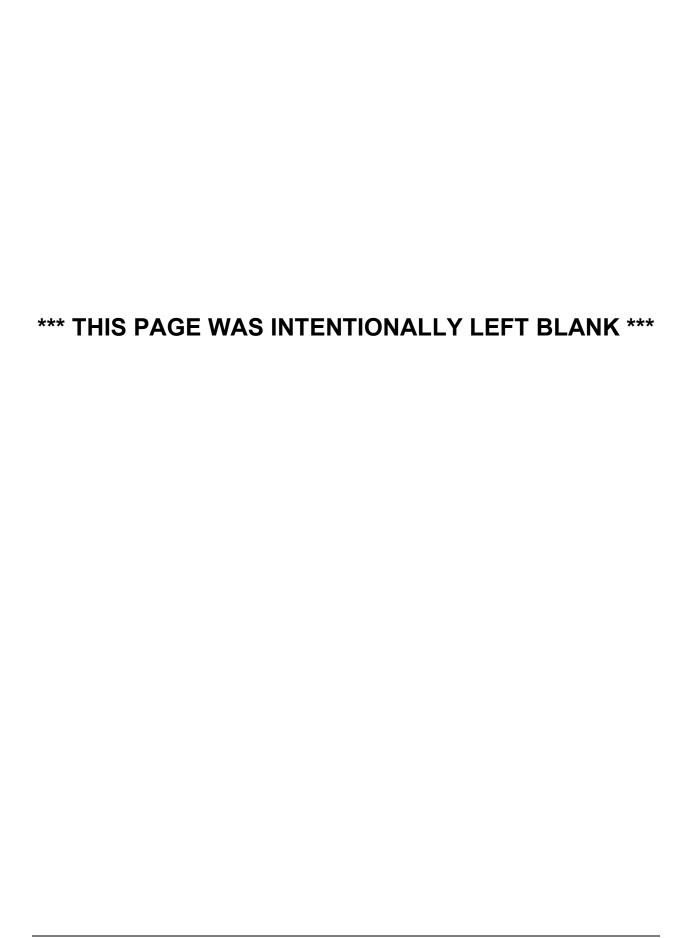

NOTICE OF AWARD

| TO: | | | | |
|--|-------------------------------|---|------------------|------------------|
| | | | | |
| PROJECT DESCRIPTIO CONSTRUCTION AREA | | | I PHASE V, | PROJECT XII |
| The OWNER has consider to its Advertisement for Bid | | | | work in response |
| You are hereby notified tha \$ | | been accepted for iter | ns in the amou | nt of |
| You are required by the Ins Performance Bond, Paym from the date of this NOTI | ent Bond, and (| | | |
| If you fail to execute said A of this Notice, said Owner acceptance of your BID as entitled to such other rights | will be entitled abandoned an | to consider all your riç d as a forfeiture of yo | ghts arising out | of the OWNER's |
| You are required to return | an acknowledg | ed copy of this NOTIC | E OF AWARD | to the OWNER. |
| Dated this | day d | of | , 20 <u>24.</u> | |
| | OWNER: | FAYETTEVILLE PI FAYETTEVILLE, N | | COMMISSION |
| | BY: TITLE: | Victoria McAllister Procurement Mana | ger | |

ACCEPTANCE OF AWARD

FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

| Receipt of the preceding NOTIC | CE OF AWARD is hereby acknowledged this the |
|--------------------------------|---|
| day of, 2 | 20 <u>24</u> . |
| | |
| | (CONTRACTOR) |
| | By: |
| | Title: |
| | |
| | |
| | - END OF SECTION - |

CONSTRUCTION AGREEMENT

| | THIS CONSTRUCTION AGREEMENT ("Agreement" or "Contract") is made by and |
|--------|---|
| betwe | een the Fayetteville Public Works Commission ("PWC"), a North Carolina public authority, |
| and | PER THE CHARTER (SEE SEC 6A.20), THE |
| CONS | STRUCTION CONTRACT, IF MORE THAN \$500K, MUST BE BETWEEN THE CITY (BY |
| | THROUGH PWC) AND THE CONTRACTOR], ("Contractor"), a |
| regist | ered to do business in North Carolina (each of PWC and Contractor is a "Party" and both |
| | ollectively the "Parties") as of the date of execution last written below (the "Effective Date"). |
| The F | Parties agree as follows: |

- The Construction Project. Contractor shall furnish and bear solely the entire 1. cost of all labor and materials necessary for the construction and/or renovation of the Project (defined hereinbelow) as specified in the Contract Documents (defined hereinbelow) and complete all Work on the Project in a Workmanlike manner in strict accordance with the Contract Documents, schedule delivery of the new materials, furnish and bear solely the entire cost of all supervision, contract administration, equipment, tools, and other means necessary to complete the Project, perform every obligation imposed by the Contract Documents, and be solely responsible for the clean-up and disposal of all materials and debris relating to or arising from the construction and renovation, subject to any exceptions that are specifically set forth in the Contract Documents. Except as otherwise specifically provided in the Contract Documents, Contractor is solely responsible for all construction means, methods, techniques, sequences, procedures, safety precautions or programs, supervising, coordinating, and performing all the Work necessary to complete the Project; provided, however, PWC shall have the right, without incurring any liability to the Contractor, to suspend Contractor's performance when a PWC employee, in his or her opinion, observes a safety violation involving a threat to life or imminent danger of bodily injury, and the suspension shall remain in effect until Contractor remedies the safety violation.
 - 2. Terms. Capitalized terms used in this Agreement have the meaning specified below:

"Business Day" means each calendar day that is not a Saturday, Sunday, holiday observed by the federal government for its employees, or holiday observed by the State of North Carolina for its employees.

"Completion of the Project" means: (i) the Project is completed in accordance with this Agreement, except for punch list items; (ii) PWC has received any required temporary or final certificate of occupancy from the governmental agency with jurisdiction over the Project; and (iii) the registered architects or engineers (the "Designer(s)") who designed portions or components of the Project have issued certificates of Completion of the Project as to those portions or components.

"Contract Documents" means the following documents that were either made available to Contractor by PWC during the bid solicitation process (including Drawings) or executed by the Parties or both, which are all incorporated by reference herein:

- a. This Agreement
- b. General Conditions
- c. Bid Submittal Documents
- d. Contractor's Submitted Bid
- e. Bid Bond
- f. [Form of Exceptions]
- g. Notice of Award
- h. Acceptance of Award
- i. Performance Bond
- i. Payment Bond
- k. Copy of General Contractor's License
- I. Power of Attorney
- m. Certificate of Insurance
- n. Section C Administrative Provisions
- o. Section D Technical Specifications
- p. [Additional Specifications]
- q. [Appendices]

The following documents may be delivered or issued on or after the Effective Date of the Agreement and may not be attached to this Agreement, but are considered Contract Documents when executed by the Parties:

- r. Notice to Proceed and Acceptance of Notice
- s. Work Change Directive(s)
- t. Change Order(s)
- u. Field Order(s)

There are no Contract Documents other than those identified in this Agreement. The Contract Documents may only be amended, modified, or supplemented as provided in this Agreement in a writing signed by the Parties.

"Fault" means a breach of contract by Contractor, negligent, reckless, or intentional act(s) or omission(s) constituting a tort under applicable statutes or common law by one or more Responsible Persons, or violation(s) of applicable statute(s) or regulation(s) by a Responsible Person.

| <u>"Project"</u> means | |
|-------------------------------------|------------------------|
| | , as more specifically |
| set forth in the Contract Documents | |

"Responsible Person" means the Contractor and each of its employees, agents, representatives, subcontractors, or other persons and entities for which Contractor may be liable or responsible as a result of any statutory, tort, or contractual duty.

The terms used in this Agreement shall have the meaning as stated herein and in the General Conditions. In the event of a conflict between the terms of this Agreement and any other component(s) of the Contract Documents, the terms of this Agreement shall govern.

3. <u>Contract Price</u>. PWC shall pay Contractor for Completion of the Project in accordance with the Contract Documents the amount identified in the accepted Bid Form of

Contractor, being in the total amount of \$______ (the "Price"). Contractor understands and acknowledges that the Price is derived from a specific appropriation of funds provided for the Project. Contractor agrees and acknowledges the Price is equal to the aggregate cost of all Work to be done on the Project, including all labor, materials, equipment, apparatus, and supplies, set in accordance with the amount specified on the Bid Form submitted by Contractor and accepted by PWC.

- 4. <u>Contract Times</u>. The Parties shall perform their obligations under this Agreement in compliance with all scheduling deadlines set forth in the Contract Documents. The Contractor shall commence the Work to be performed under this Agreement on a date to be specified in accordance with the Notice to Proceed issued by PWC. Contractor shall achieve Completion of the Project no later than 360 consecutive calendar days from said date plus any modifications thereof allowed in accordance with the Contract Documents (the "Completion Date").
- Payment, PWC shall pay Contractor in installment payments plus a final. payment, as set forth in the Contract Documents. For each applicable installment payment, Contractor shall submit an application for payment in accordance with the Contract Documents. An application for payment will be processed by PWC as provided in the Contract Documents. Such installment payments shall reflect the actual Cost of the Work, not to exceed in total the Price, and the allocable portion of the total Price for said installment. PWC shall make payment to the Contractor, less any applicable retainage set forth in the Contract Documents; provided, however, that PWC may withhold all or a portion of a payment on account of (1) incomplete Work, (2) defective or nonconforming Work, (3) claims filed or a reasonable basis to believe that such claims will be filed imminently, (4) failure of the Contractor to make payments properly for labor, services, materials, equipment or subcontracts, (5) damages caused to PWC or another party by one or more Responsible Persons, or (6) failure to comply with the terms and conditions of this Agreement. In the final payment, PWC shall pay the balance of the Price, including all retained amounts, less any Liquidated Damages and other applicable damage and claim amounts, to Contractor within forty-five (45) days of Completion of the Project; provided, however, that PWC may withhold a reasonable sum from the final payment to ensure correction of any final items or condition on the Project.
- Retainage. Subject to any restrictions applicable to any federal grant funds that may be utilized for the Project, PWC may, in its discretion, retain up to five percent (5%) of any periodic payment due Contractor; provided, however, when the Project is fifty percent (50%) complete, PWC, with written consent of the surety, shall not retain any further retainage from periodic payments due Contractor if Contractor continues to perform satisfactorily and any nonconforming Work identified in writing prior to that time by PWC or the Designer has been corrected by Contractor and accepted by PWC or the Designer, and provided further that full payment, less authorized deductions, shall also be made for those line item trades that have reached one hundred percent (100%) completion of their contract obligations by or before the Project is fifty percent (50%) complete if Contractor has performed satisfactorily in accordance with G.S. 143-134. 1(b2), contingent upon PWC's receipt of an approval or certification from the Designer that the Work performed by the subcontractor is acceptable and in accordance with the Contract Documents. If PWC determines Contractor's performance is unsatisfactory, PWC may, in its discretion, reinstate retainage for each subsequent periodic application for payment as authorized in this Section up to the maximum amount of five percent (5%). The Project shall be deemed fifty percent (50%) complete when Contractor's gross project invoices, excluding the value of materials stored off-site, equal or exceed fifty percent (50%) of the Price, except the value of materials stored on-site shall not exceed twenty percent (20%) of Contractor's gross project invoices for the purpose of determining whether the Project is fifty percent (50%)

complete. Within 60 days after the submission of a pay request and one of the following occurs. as specified in the Contract Documents, PWC, with written consent of the surety, shall release to Contractor all retainage on payments held by PWC: (i) PWC receives a certificate of Substantial Completion from the Designer in charge of the Project; or (ii) PWC receives beneficial occupancy or use of the Project; provided, however, PWC may in its discretion retain sufficient funds to secure Completion of the Project or corrections on any Work. If PWC retains funds, the amount retained shall not exceed two and one-half times the estimated value of the Work to be completed or corrected. Any reduction in the amount of the retainage on payments shall be with the consent of Contractor's surety. The existence of any third-party claims against Contractor or any additive change orders to the Construction Documents shall not be a basis for delaying the release of any retainage on payments. Notwithstanding anything in this Section to the contrary, following fifty percent (50%) completion of the Project, PWC shall be authorized to withhold additional retainage from a subsequent periodic payment, not to exceed five percent (5%), in order to allow PWC to retain two and one-half percent (2.5%) total retainage through the Completion of the Project. In the event that PWC elects to withhold additional retainage on any periodic payment subsequent to release of retainage on a line-item of Work pursuant to G.S. 143-134.1(b2), Contractor may also withhold from the subcontractors remaining on the project sufficient retainage to offset the additional retainage held by PWC, notwithstanding the actual percentage of retainage withheld by PWC of the Project as a whole. Neither PWC's nor Contractor's release of retainage on payments as part of a payment in full on a line-item of Work pursuant to G.S. 143-134.1(b2) shall affect any applicable warranties on Work done by Contractor or subcontractor, and the warranties shall not begin to run any earlier than either PWC's receipt of a certificate of Substantial Completion from the Designer in charge of the Project or PWC receives beneficial occupancy.

- 7. <u>Liquidated Damages</u>. Time is of the essence with respect to performance of each of the Parties' obligations under this Agreement. Contractor recognizes and acknowledges that PWC will suffer financial and other losses if the Project is not completed by the Completion Date. The Parties recognize and agree that the delays, expense, and difficulties involved in proving in a legal or arbitration proceeding the actual loss suffered by PWC if the Project is not completed by the Completion Date. Accordingly, instead of requiring any such proof, Contractor and PWC agree that in the event Contractor fails to achieve Completion of the Project by the Completion Date, Contractor shall pay to PWC as liquidated damages to compensate PWC for damages related to the delayed Completion of the Project one thousand dollars (\$1000.00) per day ("Liquidated Damages") for each calendar day Contractor fails to achieve Completion of the Project by the Completion Date.
- 8. <u>Contractor's Representations and Warranties</u>. In order to induce PWC to enter into this Agreement, Contractor makes the following representations and warranties to PWC:
 - a. Contractor is duly licensed in the State of North Carolina to complete all Work necessary for the Project, is duly organized, validly existing and in good standing and has all requisite powers, rights, and authority to execute, enter into, and perform this Agreement in accordance with the terms and conditions of this Agreement, and this Agreement constitutes a legal, valid, and binding obligation of Contractor enforceable against it in accordance with its terms.
 - b. Contractor has read the Contract Documents, and acknowledges and understands all data, materials, specifications, and requirements identified in the Contract Documents.

- c. Contractor has visited the site for the Project, conducted a thorough, visual examination of the site and adjacent areas, and become familiar with and is satisfied as to the general, local, and site conditions that may affect cost, progress, and performance in completing the Project. Contractor is familiar with and is satisfied as to all laws and regulations that may affect cost, progress, and performance to complete the Project.
- d. Contractor has carefully studied all: (1) reports of explorations and tests of subsurface conditions at or adjacent to the site and all drawings of physical conditions relating to existing surface or subsurface structures at the site that have been identified in the Contract Documents and any accompanying reports and drawings, and (2) reports and drawings relating to hazardous environmental conditions, if any, at or adjacent to the site that have been identified in the Contract Documents and any accompanying reports and drawings.
- e. Contractor has considered the information known to Contractor itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Contract Documents; and the Site-related reports and drawings identified in the Contract Documents, if any, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor; and (3) Contractor's safety precautions and programs.
- f. Based on the information and observations referred to in subsection e. of this Section, Contractor agrees that no further examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Price commencing on the commencement date and in accordance with the other terms and conditions of the Contract.
- g. Contractor is aware of the general nature of Work to be performed by PWC and others at the Site that relates to the Work as indicated in the Contract Documents.
- h. Contractor has given PWC's Designer written notice of all conflicts, errors, ambiguities, or discrepancies that Contractor has discovered in the Contract Documents, and the written resolution thereof by the Designer is acceptable to Contractor.
- i. The Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.
- j. Contractor's entry into this Agreement constitutes an incontrovertible representation by Contractor that, without exception, all prices in the Agreement are premised upon performing and furnishing the Work required by the Contract Documents.
- k. Contractor has no business or personal relationship with any PWC Commissioner, officer, director, manager, or supervisor and Contractor covenants to disclose immediately to PWC any such relationship that develops

during the performance of Work on the Project.

- 9. <u>Contractor's Payment Obligations</u>. Contractor shall pay all of its obligations arising out of or in connection with the Project in a timely manner to all persons supplying materials in the prosecution of the Work and to all laborers and others employed thereon.
- 10. Performance and Payment Bonds. Contractor shall obtain and deliver to PWC a performance bond in the amount of one hundred percent (100%) of the Price, conditioned upon the faithful performance of the Project and all Work in accordance with the Contract Documents, which bond shall be solely for the protection of PWC. Contractor shall obtain and deliver to PWC a payment bond in the amount of one hundred percent (100%) of the Price, conditioned upon the prompt payment for all labor or materials for which the Contractor or one or more of its subcontractors is liable, which payment bond shall be solely for the protection of the persons furnishing materials or performing labor for which the Contractor is liable. The performance bond and the payment bond shall be executed by one or more surety companies legally authorized to do business in the State of North Carolina, shall become effective upon the awarding of the construction contract by PWC to Contractor, and shall at all times comply with the requirements set forth in Article 3 of North Carolina General Statutes Chapter 44A. In the event PWC deems the surety or sureties upon any bond necessary for this Agreement and the completion of the Project, or if for any reason, such bond ceases to be adequate to cover the performance and/or payment of the Work, Contractor shall, at its expense, within five (5) days after the receipt of notice from PWC, furnish an additional bond or bonds in such form and amount, and with such surety or sureties as shall be satisfactory to PWC. In such event no further payment to Contractor shall be deemed to be due under this Agreement until new or additional security for the performance and payment of the Project shall be furnished in manner and form satisfactory to PWC. Contractor understands and acknowledges that PWC, as a public authority, is not subject to the provisions of Articles 1 and 2 of Chapter 44A of the General Statutes, in accordance with G.S. 44A-34 and applicable law.
- 11. <u>Contractor's Damage Repair Obligations</u>. Contractor shall be responsible for all damages to the property of the City of Fayetteville and of PWC that may result from the normal procedure of a Responsible Person's actions in the prosecution of the Work or that may be caused by or result from the negligence of a Responsible Person during the progress of or connected with the prosecution of the Work, whether within the limits of the Work or elsewhere. Contractor shall promptly restore all such property so damaged to a condition as good as it was immediately prior to Contractor initiating the Work on the Project.
- 12. Defective Work. The Project shall be subject to observation and approval by PWC, Designer, and representatives of governmental agencies with jurisdiction over the Project. PWC and Designer shall be entitled to enter at all reasonable times the premises subject to construction or renovation to inspect the Work performed by or on behalf of Contractor, provided that such entry and inspection does not materially interfere with the progress of construction. Contractor shall correct promptly, at no cost to PWC, all Work reasonably rejected by PWC or by its representatives. Should Contractor fail to correct rejected Work, PWC may, acting in its sole discretion, correct such Work and the Contractor shall pay PWC's actual costs of correction and any other applicable amounts identified in the Contract Documents.
- 13. <u>As-Built Drawings</u>. Contractor shall maintain during the progress of the Project as-built drawings indicating the current status of the Project as actually performed. Upon Completion of the Project, Contractor shall prepare a final version of such as-built drawings and

submit them to PWC for approval.

- 14. <u>Assignment</u>. This Agreement shall be binding upon and inure to the benefit of the Parties, their legal representatives, successors, and assigns. Contractor may not assign, transfer, convey, or encumber, whether voluntarily or by operation of law, this Agreement or any obligations, rights under, or interests in this Agreement to a third party without the prior written consent of PWC; and, specifically, but without limitation, money that may become due and money that is due may not be assigned without such consent (except to the extent that the effect of this restriction may be limited by law), and unless specifically stated to the contrary in any written consent to an assignment, no assignment will release or discharge the assignor from any duty or responsibility under the Contract Documents.
- 15. <u>Indemnity</u>. Contractor shall indemnify, defend, and hold harmless PWC and its Commissioners, officers, employees, agents, and representatives and the City of Fayetteville and its elected officials, managers, employees, agents, and representatives and Design Engineer (collectively "Indemnitees") from and against all claims, actions, liabilities, damages, losses, costs, and expenses (including, without limitation, injury to or death of any persons and damage to property, economic and consequential damages and attorneys' fees) asserted by one or more third parties against one or more of the Indemnitees if the Fault of one or more Responsible Persons is a proximate cause of the loss, damage, or expense indemnified. Contractor's obligation to indemnify, defend, and hold harmless the Indemnitees shall survive the termination of this Agreement.
- Insurance. Contractor shall maintain during the Work and for at least three (3) 16. years following Completion of the Project the insurance coverage set forth in the Contract Documents, which insurance shall be placed with insurance companies authorized to do business in the State of North Carolina and rated A minus VII or better by the current edition of Best's Key Rating Guide or otherwise approved in writing by PWC. Prior to initiating any Work, Contractor shall deliver certificates of insurance confirming each such coverage required by the Contract Documents, and Contractor shall direct its insurers to provide annually to PWC certificates confirming each such coverage during the coverage period. PWC shall be named as an additional insured in the comprehensive automobile and commercial liability insurance policies. Commercial general liability coverage shall be written on an "occurrence" basis. Contractor shall not reduce or allow the required insurance coverages to lapse without PWC's prior written approval. All policies for insurance must be endorsed to contain a provision giving PWC a thirty (30) calendar day prior written notice by certified mail of any cancellation of that policy or material reduction in coverage. Should a notice of cancellation be issued for nonpayment of premiums or any part thereof, or should Contractor fail to provide and maintain certificates as set forth herein, PWC shall have the right, but shall not have the obligation, to pay such premium to the insurance company or to obtain such coverage and to deduct such payment from any sums that may be due or become due to Contractor, or to seek reimbursement for said payments from Contractor. Any such sums paid by PWC shall be due and payable immediately by Contractor upon notice from PWC. The insurance provisions of this Agreement shall not be construed as a limitation on Contractor's responsibilities and liabilities pursuant to the terms and conditions of this Agreement. Contractor's obligation to maintain insurance for three (3) years after Completion of the Project shall survive the termination of this Agreement.
- 17. <u>Warranty</u>. The Contractor hereby grants to PWC a warranty on all materials and Workmanship involved in the Project for a period of one (1) year from the Completion Date and a period of two (2) years from the Completion Date for any latent structural defects. PWC shall

give written notice to Contractor of any claim under this Section within the time specified hereinabove. This warranty shall be in addition to, and not in derogation of, all other rights and privileges which PWC may have under law, equity, or instrument, and shall survive the Completion Date and the final settlement and shall be binding on Contractor notwithstanding any provision in any other writing executed by PWC heretofore or contemporaneous with the execution of the Agreement or prior to the Completion Date.

- 18. <u>Waiver</u>. No failure on the part of any party to exercise, and no delay in exercising, any right, power, or privilege hereunder shall operate as a waiver thereof, nor shall any single or partial exercise of any right hereunder preclude any other or further cumulative and not exclusive of any remedies provided by law. This Agreement shall be binding upon and inure to the benefit of the parties, their legal representatives, successors, and assigns. This Agreement may not be assigned, transferred, conveyed, or encumbered, whether voluntarily or by operation of law, by either party without the prior written consent of the other party, which consent shall not be unreasonably withheld.
- 19. <u>Law</u>. THIS AGREEMENT SHALL BE GOVERNED BY AND INTERPRETED AND ENFORCED IN ACCORDANCE WITH THE LAWS OF THE STATE OF NORTH CAROLINA WITHOUT GIVING EFFECT TO THE CHOICE OF LAW PROVISIONS THEREOF. The Contractor shall at all times comply with all applicable Federal, state, and local laws and building codes in the performance of its obligations under the Agreement.
- Dispute Resolution. In the event of any dispute, controversy, or claim of any kind or nature arising under or in connection with this Agreement (a "Dispute") and involving any two or more of the following parties, PWC, Designer, Contractor or any subcontractor of Contractor, the party initiating the Dispute shall serve written notice of a Dispute on the party(ies) to the dispute, and those parties shall endeavor to settle the dispute first through direct, informal discussions between the parties' selected representatives. Any such representative(s) shall have binding authority to settle the Dispute. In the event the parties do not settle the Dispute within ten (10) days from the date of written notice of the Dispute, any party to the Dispute may, by written notice to the other party(ies), engage a mediator certified under the laws of the State of North Carolina to mediate the Dispute within thirty (30) days of such notice. The parties to the Dispute shall attend mediation in good faith. In the event mediation is unsuccessful, any party to the dispute may initiate arbitration proceedings. Any controversy or claim arising out of or relating to the Contract Documents, or the breach thereof, shall be settled by binding arbitration administered by the American Arbitration Association under its Construction Industry Arbitration Rules, and judgment on the award rendered by the arbitrator(s) may be entered in any court having jurisdiction thereof. All of the foregoing dispute resolution procedures shall be held in Cumberland County, North Carolina. The costs of the mediator and arbitrator in a dispute resolution process shall be divided equally among the parties to the process; provided, however, PWC shall bear at least one-third of the cost if PWC is a party to the dispute resolution and the remainder of the cost shall be divided equally among the other parties participating in the dispute resolution. PWC shall, in its contractual arrangements with Designer, and Contractor shall, in its contracts with subcontractors and they in their contracts with lower-tier subcontractors authorize and direct such parties to participate in the dispute resolution procedures set forth in this Section. Unless otherwise directed in writing by PWC, Contractor shall continue the Project and maintain compliance with the scheduling deadlines set forth in the Contract Documents during any dispute resolution proceedings. If Contractor continues to perform, PWC shall make payments due for the continued performance in accordance with this Agreement. The provisions of this Section shall not extend any applicable statutes of limitation or repose.

- 21. Execution; Modification; Entire Agreement; Severability. This Agreement may be executed in counterparts with the same effect as if the signatures to each counterpart were upon a single instrument, and all such counterparts together shall be deemed an original of this Agreement. For purposes of this Agreement, a facsimile copy or scanned copy or photocopy of a party's signature shall be sufficient to bind such party. This Agreement shall be subject to execution by electronic means in accordance with Article 40 of Chapter 66 of the North Carolina General Statutes. No oral communication, promise, understanding, or agreement before, contemporaneous with, or after the execution of this Agreement shall affect or modify any of the terms and conditions and obligations of the Contract Documents. The Contract Documents shall be modified only by a subsequent writing signed by both Parties. The Contract Documents shall be conclusively considered to contain and express all the terms and conditions agreed upon by the Parties, notwithstanding any prior or contemporaneous written communication, promise, understanding or agreement. Should any provision of this Agreement or any of the Contract Documents at any time be in conflict with any law, statute, rule, regulation, order, or ruling and thus be unenforceable, or be unenforceable for any other reason, then the remaining provisions of this Agreement shall remain in full force and effect and the court or arbitrator shall give the offending provision the fullest meaning and effect permitted by law. The titles of the Sections throughout this Agreement are for convenience only and the words contained therein shall in no way be held to explain, modify, amplify or aid in the interpretation, construction, or meaning of the provisions of this instrument.
- 22. <u>Notices</u>. Any notice which either Party is required or desires to give the other hereunder shall be deemed sufficiently given if, in writing, it is delivered personally, or sent by certified U.S. mail, return-receipt requested, postage prepaid, to the addresses listed herein below, or such other address as either Party shall give to the other Party by written notice in accordance herewith. Any notice given herein by personal delivery shall be deemed delivered when received. Any properly addressed notice given herein by certified mail shall be deemed delivered on third Business Day after the same is deposited in an official United States Post Office, postage prepaid, or if sooner upon the date when the return receipt therefore is signed, or refusal to accept the mailing by the addressee is noted thereon by the postal authorities.

To PWC:
Fayetteville Public Works Commission
Attn: Timothy Bryant, CEO/General Manager

PO Box 1089 Fayetteville, NC 28302

To Contractor:

- 23. <u>Termination</u>. PWC may terminate this Agreement immediately if during the progress of the Work or during the warranty period, the Contractor:
 - a. Persistently fails to prosecute the Work properly and in accordance with this contract, including but not limited to include failure to provide sufficient crews, equipment, or resources, or failure to adhere to the schedule;

- b. Demonstrates disregard for the policies, procedures, or requirements of PWC;
- c. Demonstrates complete disregard of the authority of PWC or its designated representatives; or
- d. Violates in any substantial way the provisions and requirements of this Agreement.

Such termination shall be effective upon written notice to Contractor and its surety. PWC may terminate the contract for its convenience by providing Contractor at least seven (7) calendar days prior written notice, in which event Contractor shall be paid for all Work completed, plus other expenses as mutually agreed upon between PWC and Contractor.

Compliance. Contractor hereby acknowledges that "E-Verify" is the federal E-Verify program operated by the US Department of Homeland Security and other federal agencies which is used to verify the Work authorization of newly hired employees pursuant to federal law and in accordance with Article 2, Chapter 64 of the North Carolina General Statutes. Contractor further acknowledges that all employers, as defined by Article 2, Chapter 64 of the North Carolina General Statutes, must use E-Verify and after hiring an employee to Work in the United States, shall verify the Work authorization of the employee through E-Verify in accordance with N.C.G.S. §64-26(a). Contractor hereby pledges, attests, and warrants through execution of this Agreement that Contractor complies with the requirements of Article 2, Chapter 64 of the North Carolina General Statutes and further pledges, attests, and warrants that all subcontractors currently employed by or subsequently hired by Contractor shall comply with all E-Verify requirements. Failure to comply with the above requirements shall be considered a breach of this Agreement. Contractor hereby further acknowledges that the execution and delivery of this Agreement constitutes Contractor's certification to PWC and to the North Carolina State Treasurer that, as of the date of the Effective Date of this Agreement, Contractor is not listed on (a) the Final Divestment List created and maintained by the North Carolina Department of State Treasurer pursuant to the Iran Divestment Act of 2015, Chapter 147, Article 6E of the General Statutes of North Carolina (the "Iran Divestment Act"); or (b) the list of companies that the North Carolina State Treasurer determines to be engaged in a boycott of Israel in accordance with Article 6G of Chapter 147 of the General Statutes of North Carolina. Contractor represents and warrants to Commission that Contractor, and all persons and entities owning (directly or indirectly) an ownership interest in it: (i) are not, and will not become, a person or entity with whom a party is restricted from doing business with under regulations of the Office of Foreign Asset Control ("OFAC") of the Department of the Treasury (including, but not limited to, those named on OFAC's Specially Designated and Blocked Persons list) or under any statute, executive order (including, but not limited to, the September 24, 2001, Executive Order 13224 Blocking Property and Prohibiting Transactions with Persons Who Commit, Threaten to Commit, or Support Terrorism), or other governmental action; and (ii) are not knowingly engaged in, and will not knowingly engage in, any dealings or transactions or be otherwise associated with such persons or entities described in clause (i) above. Contractor also shall at all times during the term of this Agreement comply with Executive Order 11246, including but not limited to the Equal Opportunity Clause requirements set forth in 41 C.F.R. § 60-1.4. Contractor shall abide by the requirements of 41 CFR 60-300.5(a) and 60-741.5(a) prohibiting discrimination against qualified individuals on the basis of protected veteran status or disability and requiring affirmative action by covered prime contractors and subcontractors to employ and advance in employment qualified protected veterans and individuals with disabilities.

IN WITNESS WHEREOF, the Parties have executed this Agreement by their duly authorized representatives.

| Fayetteville Public Works Commission | CONTRACTOR |
|--|---|
| [PER OUR CHARTER (SEE SEC 6A.20), | |
| THE CONSTRUCTION CONTRACT, IF MORE | |
| THAN \$500K, MUST BE BETWEEN THE CITY | |
| (BY AND THROUGH PWC) AND THE CONTRA | CTOR |
| By: Timothy Bryant, CEO/GM | Ву: |
| Date: | (Printed Name, Title) Date: |
| This instrument has been preaudited in the manne Fiscal Control Act (N.C. Gen. Stat. § 159-1 et seq.). | r required by the Local Government Budget and |
| By: | |
| Approved as to form: | |
| Legal Dept. | |



GENERAL CONDITIONS FOR FAYETTEVILLE PUBLIC WORKS COMMISSION

| General Condit | tions | 5 |
|-----------------------|---|----|
| Article I. Defi | nitions and Terminology | 5 |
| Section 1.01 | Definitions | 5 |
| Section 1.02 | Terminology | 9 |
| Article II. Pr | eliminary Matters | 10 |
| Section 2.01 | Delivery of Bonds and Evidence of Insurance | 10 |
| Section 2.02 | Copies of Documents | 10 |
| Section 2.03 | Before Starting any Work | 10 |
| Section 2.04 | Preconstruction Conference; Designation of Authorized Representatives | 10 |
| Section 2.05 | Initial Acceptance of Schedules | 11 |
| Section 2.06 | Electronic Transmittals | 11 |
| Article III. Co | ontract Documents: Intent, Requirements, Reuse | 12 |
| Section 3.01 | Intent | 12 |
| Section 3.02 | Reference Standards | 12 |
| Section 3.03 | Reporting and Resolving Discrepancies | 12 |
| Section 3.04 | Reuse of Documents | 13 |
| Article IV. Co | ommencement and Progress of the Work | 13 |
| Section 4.01 | Commencement of Work | 13 |
| Section 4.02 | Reference Points | 14 |
| Section 4.03 | Progress Schedule | 14 |
| Section 4.04 | Delays in Contractor's Progress | 14 |
| Article V. Av | vailability of Lands; Subsurface and Physical Conditions; Hazardous | |
| | Conditions | |
| Section 5.01 | Availability of Lands | |
| Section 5.02 | Use of Site and Other Areas | |
| Section 5.03 | Differing Subsurface or Physical Conditions or Underground Facilities | |
| Section 5.04 | Underground Utilities | |
| Section 5.05 | Hazardous Environmental Conditions at Site | |
| | onds and Insurance | |
| Section 6.01 | Performance and Payment Bonds | |
| Section 6.02 | Insurance | |
| Article VII. Co | ontractor's Responsibilities | |
| Section 7.01 | Supervision and Superintendence | 22 |
| Section 7.02 | Labor; Working Hours | |
| Section 7.03 | Services, Materials, and Equipment | |
| Section 7.04 | "Or Equals" | |
| Section 7.05 | Concerning Subcontractors, Suppliers, and Others | 24 |
| Section 7.06 | Patent Fees and Royalties | 25 |

| Section 7.07 | Permits | 25 |
|-----------------|---|-----|
| Section 7.08 | Taxes | 26 |
| Section 7.09 | Laws and Regulations | 26 |
| Section 7.10 | Record Documents | 26 |
| Section 7.11 | Safety and Protection | 26 |
| Section 7.12 | Emergencies | 27 |
| Section 7.13 | Shop Drawings, Samples, and Other Submittals | 27 |
| Section 7.14 | Contractor's General Warranty and Guarantee | 29 |
| Section 7.15 | Indemnification | 30 |
| Section 7.16 | Claims Procedure | 31 |
| Section 7.17 | Delegation of Professional Design Services | 31 |
| Article VIII. F | PWC's Responsibilities | 32 |
| Article IX. Am | ending the Contract Documents; Changes in the Work | 32 |
| Section 9.01 | Amending and Supplementing Contract Documents | 33 |
| Section 9.02 | PWC-Authorized Changes in the Work | 33 |
| Section 9.03 | Unauthorized Changes in the Work | 33 |
| Section 9.04 | Change of Contract Price | 34 |
| Section 9.05 | Change of Contract Times | 34 |
| Section 9.06 | Change Proposals | 34 |
| Section 9.07 | Execution of Change Orders | 35 |
| Section 9.08 | Notification to Surety | 35 |
| | sts, Inspections, and Approvals; Correction, Removal, or Acceptance | |
| | | |
| Section 10.01 | Access to Work | |
| Section 10.02 | , , , , , , , , , , , , , , , , , , , | |
| Section 10.03 | Defective Work | |
| | Acceptance of Defective Work | |
| | Uncovering Work | |
| | PWC May Stop the Work | |
| | PWC May Correct Defective Work | |
| | ims | |
| | Claims Process | |
| | Submittal of Claim | |
| | Review and Resolution | |
| | Dispute Resolution | |
| - | ments to Contractor; Set-Offs; Completion; Correction Period | |
| | Progress Payments | |
| Section 12 02 | Substantial Completion | //3 |

| Section 12.03 | Partial Llag or Occupancy | 11 |
|-----------------|---|----|
| | Partial Use or Occupancy | |
| Section 12.04 | Final Inspection | 44 |
| Section 12.05 | Final Payment | 44 |
| Section 12.06 | Waiver of Claims | 45 |
| Section 12.07 | Correction Period | 45 |
| Article XIII. S | Suspension of Work and Termination | 46 |
| Section 13.01 | PWC May Suspend Work | 46 |
| Section 13.02 | PWC May Terminate for Cause | 46 |
| Section 13.03 | PWC May Terminate For Convenience | 47 |
| Section 13.04 | Contractor May Stop Work or Terminate | 48 |
| Section 13.05 | Morality | 48 |
| Article XIV. N | /liscellaneous | 48 |
| Section 14.01 | Additional General Terms and Conditions | 48 |
| Section 14.02 | Giving Notice | 48 |
| Section 14.03 | Computation of Times | 49 |
| Section 14.04 | Cumulative Remedies | 49 |
| Section 14.05 | Limitation of Damages | 49 |
| Section 14.06 | No Waiver | 49 |
| Section 14.07 | Survival of Obligations | 49 |
| Section 14.08 | Controlling Law | 49 |
| Section 14 09 | Headings | 49 |

General Conditions

Article I. Definitions and Terminology

Section 1.01 Definitions

Capitalized terms used in the Bid Documents or Contract Documents, including the singular and plural forms, shall have the meaning indicated in the definitions below. In addition to terms specifically defined below, terms with initial capital letters in the Contract Documents include references to identified articles and paragraphs, and the titles of other documents or forms.

- (a) Addenda—Written or graphic instruments issued before the opening of Bids which clarify, correct, or change the Bid Documents or other Contract Documents.
- (b) Agreement—The written instrument, executed by PWC and Contractor, that sets forth the Contract Price and Contract Times, identifies the parties, designates the specific documents that encompass the Contract Documents, and provides other material provisions that govern the relationship between the parties as it relates to the Project. The Agreement is also referred to, and titled as, the "Construction Agreement."
- (c) Application for Payment—The form that Contractor shall use during the Work in requesting progress or final payments. Any Application for Payment shall be accompanied by such supporting documentation as is required by the Contract Documents.
- (d) Bid—The offer of a Bidder submitted on the prescribed form setting forth the prices for the Work to be performed.
- (e) Bidder—An individual or entity that submits a Bid to PWC for the Project.
- (f) Bid Documents—The Bidding Requirements, the proposed Contract Documents, and all Addenda.
- (g) Bidding Requirements—The Invitation to Bid, Instructions to Bidders, Bid Bond or other Bid security, if any, the Bid Form, and the Bidder's original Bid with any requisite attachments.
- (h) Business Day—each calendar day that is not a Saturday, Sunday, or holiday observed by PWC (New Year's Day, Martin Luther King, Jr. Day, Good Friday, Memorial Day, Independence Day, Labor Day, Veteran's Day, Thanksgiving Day (and the day after), and Christmas (2 days) for its employees.
- (i) Change Order—A document that is signed by Contractor and PWC, which authorizes an addition, deletion, or revision in the Work, an adjustment in the Contract Price or the Contract Times, a change in the scope of the Project, or other revision to the Agreement, issued on or after the Effective Date of the Agreement.
- (j) Change Proposal—A written request by Contractor, submitted in compliance with the procedural requirements set forth in the Contract Documents, seeking an adjustment in Contract Price or Contract Times, or both; contesting an initial decision by PWC concerning the requirements of the Contract Documents or the acceptability of Work under the Contract Documents; challenging a set-off against payments due; or seeking other relief with respect to the terms of the Agreement.

- (k) Completion of the Project—Has the meaning as set forth in the Construction Agreement.
- (I) Constituent of Concern—Asbestos, petroleum, radioactive materials, polychlorinated biphenyls (PCBs), hazardous waste, and any substance, product, waste, or other material of any nature whatsoever that is or becomes listed, regulated, or addressed pursuant to (a) the Comprehensive Environmental Response, Compensation and Liability Act, 42 U.S.C. §\$9601 et seq. ("CERCLA"); (b) the Hazardous Materials Transportation Act, 49 U.S.C. §\$5101 et seq.; (c) the Resource Conservation and Recovery Act, 42 U.S.C. §\$6901 et seq. ("RCRA"); (d) the Toxic Substances Control Act, 15 U.S.C. §\$2601 et seq.; (e) the Clean Water Act, 33 U.S.C. §\$1251 et seq.; (f) the Clean Air Act, 42 U.S.C. §\$7401 et seq.; or (g) any other federal, state, or local statute, law, rule, regulation, ordinance, resolution, code, order, or decree regulating, relating to, or imposing liability or standards of conduct concerning, any hazardous, toxic, or dangerous waste, substance, or material.
- (m) Contract Price—The money that PWC has agreed to pay Contractor for Completion of the Project in accordance with the Contract Documents. May also be referred to as "Price" throughout the Contract Documents.
- (n) Contract Times—The number of days or the dates by which Contractor shall: (a) achieve Milestones, if any; and (b) Completion of the Project.
- (o) Contractor—The individual or entity with which PWC has contracted for performance of the Work and Completion of the Project.
- (p) Day—a calendar day of 24 hours measured from midnight to the next midnight. Also referred to throughout the Contract Documents as "days" or "calendar days."
- (q) Design Engineer—The Engineering firm identified on the Contract Drawings and their duly authorized employees and agents, such employees and agents acting within the scope of the particular duties entrusted to them in each case.
- (r) Drawings—The part of the Contract that graphically shows the scope, extent, and character of the Work to be performed by Contractor.
- (s) Field Order—A written order issued by Project Engineer which requires minor changes in the Work but does not change the Contract Price or the Contract Times.
- (t) Final Completion—The day the on which any specified Work is complete in accordance with the Contract Documents.
- (u) Hazardous Environmental Condition—The presence at the Site of Constituents of Concern in such quantities or circumstances that may present a danger to persons or property exposed thereto. The presence at the Site of materials that are necessary for the execution of the Work, or that are to be incorporated in the Work, and that are controlled and contained pursuant to industry practices, Laws and Regulations, and the requirements of the Contract Documents, does not establish a Hazardous Environmental Condition.
- (v) Laws and Regulations; Laws or Regulations—Any and all applicable laws, statutes, rules,

- regulations, ordinances, codes, and orders of any and all governmental bodies, agencies, authorities, and courts having jurisdiction. Such terms, unless otherwise specified, shall refer to North Carolina laws and regulations.
- (w) Milestone—A principal event in the performance of the Work that the Agreement requires Contractor to achieve by an intermediate completion date or by a time prior to Completion of the Project.
- (x) Non-Compliance Notice—A written notice issued by PWC to Contractor indicating a violation of any term, provision, or requirement of the Contract Documents.
- (y) Notice of Award—The written notice by PWC to a Bidder providing of PWC's acceptance of the Bid upon timely compliance by the Bidder with any conditions precedent provided in the notice.
- (z) Notice to Proceed—A written notice by PWC to Contractor fixing the date on which the Contract Times will commence to run and on which Contractor shall start to perform the Work.
- (aa) Progress Schedule—A schedule, prepared and maintained by Contractor, describing the sequence and duration of the activities comprising the Contractor's plan to accomplish the Work within the Contract Times.
- (bb) Project—has the meaning ascribed to it in the Agreement and is as more specifically set forth throughout the Contract Documents. "Project" includes the total undertaking to be accomplished for PWC by engineers, contractors, and others, including planning, study, design, construction, testing, commissioning, and start-up, and of which the Work to be performed under the Contract Documents is a part.
- (cc) Project Engineer—the PWC employee assigned by PWC to coordinate, manage, monitor, and otherwise perform the administration necessary and consistent with PWC's responsibilities for the Completion of the Project. The Project Engineer has authority to coordinate and work with the Design Engineer regarding any engineering questions, concerns, revisions, alterations, deletions, or additions to the Work, and has authority to approve any changes in the scope of the Work. Project Engineer may assign a "Project Coordinator" who will also be an employee of PWC and have the duties and responsibilities set by the Project Engineer.
- (dd) PWC—Fayetteville Public Works Commission. PWC may also be referred to in the Contract Documents as "Owner."
- (ee) Samples—Physical examples of materials, equipment, or workmanship that are representative of some portion of the Work and that establish the standards by which such portion of the Work will be judged.
- (ff) Schedule of Submittals—A schedule, prepared and maintained by Contractor, of required submittals and the time requirements for Project Engineer's review of the submittals and the performance of related construction activities.
- (gg) Schedule of Values—A schedule, prepared and maintained by Contractor, allocating portions of the Contract Price to various portions of the Work and used as the basis for reviewing Contractor's Applications for Payment.

- (hh) Shop Drawings—All drawings, diagrams, illustrations, schedules, and other data or information that are specifically prepared or assembled by or for Contractor and submitted by Contractor to illustrate some portion of the Work. Shop Drawings, whether approved or not, are not Contract Drawings and are not Contract Documents.
- (ii) Site—Lands or areas indicated in the Contract Documents as being furnished by PWC upon which the Work is to be performed, including rights-of-way and easements, and such other lands furnished by PWC which are designated for the use of Contractor.
- (jj) Specifications—The part of the Contract that consists of written requirements for materials, equipment, systems, standards, and workmanship as applied to the Work, and certain administrative requirements and procedural matters applicable to the Work.
- (kk) Subcontractor—An individual or entity having a direct contract with Contractor or with any other Subcontractor for the performance of a part of the Work.
- (II) Substantial Completion—The time at which the Work (or a specified part thereof) has progressed to the point where, in the opinion of Project Engineer, the Work (or a specified part thereof) is sufficiently complete, in accordance with the Contract Documents, so that the Work (or a specified part thereof) can be utilized for the purposes for which it is intended. The terms "substantially complete" and "substantially completed" as applied to all or part of the Work refer to Substantial Completion thereof.
- (mm) Successful Bidder—The Bidder whose Bid PWC accepts, and to which PWC provides a Notice of Award.
- (nn) Supplementary Conditions—Any part of the Agreement that amends or supplements these General Conditions.
- (oo) Supplier—A manufacturer, fabricator, supplier, distributor, materialman, or vendor having a direct contract with Contractor or with any Subcontractor to furnish materials or equipment to be incorporated in the Work by Contractor or a Subcontractor.
- (pp) Technical Data—Those items expressly identified as Technical Data in the Supplementary Conditions, with respect to either (a) subsurface conditions at the Site, or physical conditions relating to existing surface or subsurface structures at the Site (except Underground Facilities) or (b) Hazardous Environmental Conditions at the Site. If no such express identifications of Technical Data have been made with respect to conditions at the Site, then the data contained in boring logs, recorded measurements of subsurface water levels, laboratory test results, and other factual, objective information regarding conditions at the Site that are set forth in any geotechnical or environmental report prepared for the Project and made available to Contractor are hereby defined as Technical Data with respect to conditions at the Site under Paragraphs 5.03, 5.04, and 5.06.
- (qq) Underground Facilities—All underground pipelines, conduits, ducts, cables, wires, manholes, vaults, tanks, tunnels, or other such facilities or attachments, and any encasements containing such facilities, including but not limited to those that convey electricity, gases, steam, liquid petroleum products, telephone or other communications, fiber optic transmissions, cable television, water, wastewater, storm water, other liquids or chemicals, or traffic or other control systems.

- (rr) Unit Price Work—Work to be paid for on the basis of unit prices.
- (ss) Work—The entire construction or the various separately identifiable parts thereof required to be provided under the Contract Documents. Work includes and is the result of performing or providing all labor, services, materials, equipment, and documentation necessary to produce such construction; furnishing, installing, and incorporating all materials and equipment into such construction; and may include related services such as testing, start-up, and commissioning, all as required by the Contract Documents and necessary to achieve Completion of the Project.
- (tt) Work Change Directive—A written directive to Contractor issued on or after the Effective Date of the Contract, signed by PWC and recommended by the Project Engineer, ordering an addition, deletion, or revision in the Work.

Section 1.02 <u>Terminology</u>

The words and terms discussed in the following paragraphs are not defined but, when used in the Bidding Requirements or Contract Documents, have the indicated meaning.

- (a) Intent of Certain Terms or Adjectives:
 - (i) The Contract Documents include the terms "as allowed," "as approved," "as ordered," "as directed" or terms of like effect or import to authorize an exercise of professional judgment by Project Engineer. In addition, the adjectives "reasonable," "suitable," "acceptable," "proper," "satisfactory," or adjectives of like effect or import are used to describe an action or determination of Project Engineer as to the Work. It is intended that such exercise of professional judgment, action, or determination will be solely to evaluate, in general, the Work for compliance with the information in the Contract Documents and with the design concept of the Project as a functioning whole as shown or indicated in the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective is not intended to and shall not be effective to assign to Project Engineer any duty or authority to supervise or direct the performance of the Work, or any duty or authority to undertake responsibility contrary to the provisions the Contract Documents.
- (b) Defective—when modifying the word "Work," refers to Work that is unsatisfactory, faulty, or deficient in that it:
 - (i) does not conform to the Contract Documents; or
 - (ii) does not meet the requirements of any applicable inspection, reference standard, test, or approval referred to in the Contract Documents; or
 - (iii) has been damaged prior to Project Engineer's recommendation of final payment (unless responsibility for the protection thereof has been assumed by PWC at Substantial Completion in accordance with the Contract Documents).
- (c) Furnish, Install, Perform, Provide
 - (i) The word "furnish," when used in connection with services, materials, or equipment, shall mean to supply and deliver said services, materials, or equipment to the Site (or some other specified location) ready for use or installation and in usable or operable condition.
 - (ii) The word "install," when used in connection with services, materials, or equipment, shall mean to put into use or place in final position said services, materials, or equipment

- complete and ready for intended use.
- (iii) The words "perform" or "provide," when used in connection with services, materials, or equipment, shall mean to furnish and install said services, materials, or equipment complete and ready for intended use.
- (iv) If the Contract Documents establish an obligation of Contractor with respect to specific services, materials, or equipment, but do not expressly use any of the four words "furnish," "install," "perform," or "provide," then Contractor shall furnish and install said services, materials, or equipment complete and ready for intended use.

Unless stated otherwise in the Contract Documents, words or phrases that have a well-known technical or construction industry or trade meaning are used in the Contract Documents in accordance with such recognized meaning.

Article II. Preliminary Matters

Section 2.01 Delivery of Bonds and Evidence of Insurance

- (a) Bonds: Contractor shall deliver to PWC such bonds as Contractor is required to furnish simultaneously with delivering the executed Agreement to PWC.
- (b) Contractor's Insurance: Contractor shall deliver to PWC the certificates and other evidence of the insurance required by the Contract Documents simultaneously with delivering the executed Agreement to PWC.

Section 2.02 Copies of Documents

- (a) PWC will furnish to Contractor up to five (5) printed copies of the Contract Documents upon request by Contractor, and one (1) copy in electronic portable document format (PDF). Additional printed copies will be furnished upon request at the cost of reproduction.
- (b) PWC will maintain and safeguard at least one original printed record version of the Agreement, including Drawings and Specifications signed and sealed by Design Engineer or other design professionals as applicable. PWC agrees to make such original printed record version of the Agreement reasonably available to Contractor for review during PWC's normal business hours. PWC may delegate the responsibilities under this provision to Design Engineer.

Section 2.03 Before Starting any Work

- (a) Within ten (10) Days after the Contractor receives the Notice of Award from PWC (or as otherwise specifically required by the Contract Documents), Contractor shall submit to PWC for timely review:
 - (i) a preliminary Progress Schedule indicating the times (numbers of days or dates) for starting and completing the identifiable aspects of the Work, including any Milestones specified in the Contract Documents;
 - (ii) a preliminary Schedule of Submittals; and
 - (iii) Any Shop Drawings, Samples, and other submittals required by the Contract Documents before the Preconstruction Conference.

Section 2.04 Preconstruction Conference; Designation of Authorized Representatives

- (a) Before any Work at the Site is started, a preconstruction conference attended by PWC, Project Engineer, Contractor, Design Engineer, and others as appropriate will be held to establish a working understanding among the parties as to the Work and to discuss general Project issues including, but not limited, the following:
 - (i) The schedules and submittals referred to in Section 2.03;
 - (ii) Contractor's designated authorized representative as described in Section 2.04(b);
 - (iii) Safety;
 - (iv) Procedures for handling Shop Drawings, Samples, and other submittals;
 - (v) Processing Applications for Payment, electronic or digital transmittals;
- (b) At the preconstruction conference Contractor shall designate, in writing, a specific individual to act as its authorized representative with respect to its services and responsibilities under the Contract Documents. Such individual shall have the authority to transmit and receive information, render decisions relative to the requirements of the Contract Documents, and otherwise act on behalf of the Contractor.

Section 2.05 Initial Acceptance of Schedules

- (a) At least twenty (20) Days before submission of the first Application for Payment a conference, attended by Contractor, PWC, and others as appropriate, will be held to review for acceptability to Project Engineer as provided below the schedules submitted in accordance with Paragraph 2.03(a). PWC shall have ten (10) Days to review the submission and provide feedback to Contractor. Contractor shall then have ten (10) days to make any corrections and adjustments as indicated by PWC and to complete and resubmit the schedules as necessary. No progress payment shall be made to Contractor until acceptable schedules are submitted to and approved by Project Engineer.
- (b) The Progress Schedule will be acceptable to Project Engineer if it provides an orderly progression of the Work to achieve Completion of the Project within the Contract Times. Such acceptance will not impose on Project Engineer responsibility for the Progress Schedule, for sequencing, scheduling, or progress of the Work, nor interfere with or relieve Contractor from Contractor's full responsibility therefor.
- (c) Contractor's Schedule of Submittals will be acceptable to Project Engineer if it provides a workable arrangement for reviewing and processing the required submittals.

Section 2.06 Electronic Transmittals

- (a) Except as otherwise stated elsewhere in the Contract Documents, PWC and Contractor and their authorized agents may transmit, and shall accept, Project-related correspondence, text, data, documents, drawings, information, and graphics, including but not limited to Shop Drawings and other submittals, in electronic media or digital format, either directly, or through electronic mail at the address(es) designated by each Party.
- (b) When transmitting items in electronic media or digital format, the transmitting party makes no representations as to long term compatibility, usability, or readability of the items resulting from the recipient's use of software application packages, operating systems, or computer hardware differing from those used in the drafting or transmittal of the items, or from those established in applicable transmittal protocols.

Article III. Contract Documents: Intent, Requirements, Reuse

Section 3.01 Intent

- (a) The Contract Documents are complementary; what is required by one is as binding as if required by all.
- (b) It is the intent of the Contract Documents to describe a functionally complete project (or part thereof) to be constructed in accordance with the Contract Documents.
- (c) Project Engineer, Design Engineer, or both, will issue clarifications and interpretations of the Contract Documents as provided herein.
- (d) To the extent necessary that Work, construction, or conditions not covered by these General Conditions is required for Contractor to achieve Completion of the Project, "Special Conditions" for such Work will be provided to Contractor and shall be part of the Contract Documents.
- (e) In case of any inconsistency, conflict, or ambiguity among the Contract Documents, the documents shall govern in the following order: (1) Change Orders; (2) Addenda; (3) the fully executed Agreement; (4) Special Conditions; (5) any Drawings and Technical Specifications; and (6) General Conditions.

Section 3.02 Reference Standards

- (a) Standards Specifications, Codes, Laws and Regulations
 - (i) Reference in the Contract Documents to standard specifications, manuals, reference standards, or codes of any technical society, organization, or association, or to Laws or Regulations, whether such reference be specific or by implication, shall mean the standard specification, manual, reference standard, code, or North Carolina laws and regulations in effect as of the Effective Date of the Agreement, except as may be otherwise specifically stated in the Contract Documents.
 - (ii) No provision of any such standard specification, manual, reference standard, or code, or any instruction of a Supplier shall be effective to change the duties or responsibilities of PWC or Contractor, or any of their subcontractors, consultants, agents, or employees, from those set forth in the Contract Documents. No such provision or instruction shall be effective to assign to PWC or any of its officers, directors, members, partners, employees, agents, consultants, or subcontractors, any duty or authority to supervise or direct the performance of the Work or any duty or authority to undertake responsibility inconsistent with the provisions of the part of the Contract Documents.

Section 3.03 Reporting and Resolving Discrepancies

- (a) Contractor's Verification of Figures and Measurements
 - (i) Before undertaking any portion of the Work, Contractor shall review all of the Contract Documents to and check and verify all figures and dimensions for the Project. Contractor shall promptly report in writing to Project Engineer any conflict, error, ambiguity, or discrepancy that Contractor discovers, or has actual knowledge of, and shall not proceed with any Work affected thereby until the conflict, error, ambiguity, or discrepancy is

- resolved, by a clarification or interpretation by Project Engineer, or by an amendment or supplement to the Contract Documents issued pursuant to these General Conditions.
- (ii) If, before or during the performance of the Work, Contractor discovers any conflict, error, ambiguity, or discrepancy within the Contract Documents, or between the Contract Documents and (a) any applicable Law or Regulation, (b) actual field conditions, (c) any standard specification, manual, reference standard, or code, or (d) any instruction of any Supplier, then Contractor shall promptly report it to Project Engineer in writing. Contractor shall not proceed with the Work affected thereby (except in an emergency as defined hereinafter) until the conflict, error, ambiguity, or discrepancy is resolved, by a clarification or interpretation by Project Engineer, or by an amendment or supplement to the Contract Documents issued pursuant to these General Conditions.

(b) Resolving Discrepancies:

- (i) Except as may be otherwise specifically stated in the Contract Documents, the provisions of the part of the Contract Documents prepared by or for PWC shall take precedence in resolving any conflict, error, ambiguity, or discrepancy between such provisions of the Contract Documents and:
- 1) the provisions of any standard specification, manual, reference standard, or code, or the instruction of any Supplier (whether or not specifically incorporated by reference as a Contract Document); or
- 2) the provisions of any Laws or Regulations applicable to the performance of the Work (unless such an interpretation of the provisions of the Contract Documents would result in violation of such Law or Regulation).

Section 3.04 Reuse of Documents

- (a) Contractor and its Subcontractors and Suppliers shall not have or acquire any title to or ownership rights in any of the:
 - (i) Drawings, Specifications, or other documents (or copies of any thereof) prepared by or bearing the seal of Design Engineer or its consultants, including electronic media editions, or reuse any such Drawings, Specifications, other documents, or copies thereof on extensions of the Project or any other project without written consent of PWC and Design Engineer and specific written verification or adaptation by Design Engineer, where applicable; or
 - (ii) Contract Documents and shall not reuse any such Contract Documents for any purpose without PWC's express written consent.
- (b) The prohibitions of this provision shall survive final payment or termination of the Agreement. Nothing herein shall preclude Contractor from retaining copies of the Contract Documents for record purposes.

Article IV. Commencement and Progress of the Work

Section 4.01 Commencement of Work

(a) The Contract Times will commence to run on the day indicated in the Notice to Proceed issued by PWC to Contractor. A Notice to Proceed may be given at any time after the Effective Date of the Contract.

(b) Contractor shall start to perform the Work on the date when the Contract Times commence to run. No Work shall be done at the Site prior to such date. Contractor's failure to commence the Work within fifteen (15) Days of the date stated in the Notice to Proceed shall be deemed a material breach of the Agreement unless PWC otherwise determines in its sole discretion and agrees in writing to a delay of the Contract Times based on the applicable circumstances.

Section 4.02 Reference Points

- (a) Construction staking will be performed by Design Engineer, who will also prepare and furnish construction cut sheets, signed and sealed by a North Carolina professional land surveyor, to PWC and Contractor. Contractor shall not install any utilities without a sheet. All requests for staking shall be made not less than 96 hours in advance.
- (b) Contractor shall be responsible for laying out the Work, shall protect and preserve the established reference points and staking, and shall make no changes or relocations without the prior written approval of Project Engineer. Contractor shall report to Project Engineer whenever any reference point staking is lost or destroyed or requires relocation because of necessary changes in grades or locations, and shall be responsible for the accurate replacement or relocation of such reference points or staking by professionally qualified personnel.

Section 4.03 Progress Schedule

- (a) Contractor shall adhere to the Progress Schedule established in accordance with Section 2.03 as it may be adjusted from time-to-time as provided below. Contractor shall submit to Project Engineer for acceptance any proposed adjustments in the Progress Schedule that will not result in changing the Contract Times. Proposed adjustments in the Progress Schedule that will change the Contract Times shall be submitted in accordance with the requirements of Article IX.
- (b) Contractor shall carry on the Work and adhere to the Progress Schedule during any disputes or disagreements with PWC. No Work shall be delayed or postponed pending resolution of any disputes or disagreements, or during any appeal process, except as permitted by these General Conditions or as PWC and Contractor may otherwise agree in writing.

Section 4.04 Delays in Contractor's Progress

- (a) If PWC, Project Engineer, anyone for whom PWC is responsible, or a Force Majeure Event delays, disrupts, or interferes with the performance or progress of the Work, then Contractor shall be entitled to an equitable adjustment in the Contract Times and Contract Price. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.
- (b) Contractor shall not be entitled to an adjustment in Contract Price or Contract Times for delay, disruption, or interference caused by or within the control of Contractor. Delay, disruption, and interference attributable to and within the control of a Subcontractor or Supplier shall be deemed to be within the control of Contractor.

(c) Contractor must submit any Change Proposal, consistent with the procedure set forth in Article IX, seeking an adjustment in Contract Price or Contract Times under this provision within ten (10) calendar days of the commencement of the event that causes the delay, disruption, or interference with the Work and Contract Times.

Article V. Availability of Lands; Subsurface and Physical Conditions; Hazardous Environmental Conditions

Section 5.01 Availability of Lands

- (a) PWC will be responsible for obtaining any required easements and encroachments, and otherwise furnishing the Site, necessary to complete the Work, except as provided elsewhere in the Contract Documents.
- (b) Upon reasonable written request, PWC shall furnish to Contractor a current statement of record legal title and legal description of the lands upon which the Work is to be completed and PWC's interest therein.
- (c) Contractor shall provide for all additional lands and access thereto that may be required for temporary construction facilities or storage of materials and equipment necessary to complete the Work. Any and all agreements between the Contractor and any individual property owner(s) shall not obligate PWC, PWC's employees, Project Engineer, or Design Engineer in any manner, and Contractor shall, before performing any work on any such property, obtain a signed and notarized release of liability of PWC and Design Engineer that is suitable to PWC as confirmed in writing.
- (d) Contractor and any of its Subcontractors shall exercise care and caution to avoid damage to any private property. Should any such damage to private property occur, it is Contractor's responsibility to notify the Project Engineer promptly in writing that such damage occurred, the extent of the damage, and Contractor's written plan to remedy the damage. If Contractor fails to timely correct damage to private property, PWC reserves the right to withhold progress payments until damage is corrected and/or to correct damage and back-charge Contractor for costs incurred. At the Completion of the Project, Contractor shall obtain a signed release from all owners of private property to which damage occurred that releases PWC and Design Engineer and acknowledges a settlement for the damage or that such damage was adequately remedied.

Section 5.02 Use of Site and Other Areas

(a) Contractor shall confine construction equipment, temporary construction facilities, the storage of materials and equipment, and the operations of workers to the Site and other adjacent areas permitted by Laws and Regulations and shall not unreasonably encumber the Site and such other adjacent areas with construction equipment or other materials or equipment. Contractor shall assume full responsibility for (a) damage to the Site; (b) damage to any such other adjacent areas used for Contractor's operations; (c) damage to any other adjacent land or areas; and (d) for injuries and losses sustained by the owners or occupants of any such land or areas; provided that such damage or injuries result from the performance of the Work or from other actions or conduct of the Contractor or those for which Contractor is responsible.

- (b) Contractor shall keep the Site and other adjacent areas free from accumulations of waste materials, rubbish, and other debris during the progress of the Work. Removal and disposal of such debris shall conform to applicable Laws and Regulations.
- (c) Prior to Completion of the Project, Contractor shall clean the Site and the Work and make it ready for utilization by PWC. At the completion of all of the Work, Contractor shall remove from the Site and adjacent areas all tools, appliances, construction equipment and machinery, and surplus materials and shall restore to original condition all property not designated for alteration by the Contract Documents.
- (d) Contractor shall not load nor permit any part of any structure to be loaded in any manner that will endanger the structure, nor shall Contractor subject any part of the Work or adjacent structures or land to stresses or pressures that will endanger them.

Section 5.03 <u>Differing Subsurface or Physical Conditions or Underground Facilities</u>

- (a) If Contractor believes that any subsurface or physical condition or Underground Facilities that is uncovered or revealed at the Site either:
 - (i) is of such a nature as to establish that any Technical Data on which Contractor is entitled to rely is materially inaccurate;
 - (ii) is of such a nature as to require a change in the Contract Documents;
 - (iii) differs materially from that shown or indicated in the Contract Documents; or
 - (iv) is of an unusual nature, and differs materially from conditions ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract Documents;

then Contractor shall, promptly after becoming aware thereof and before further disturbing the subsurface or physical conditions or Underground Facilities or performing any Work in connection therewith, notify PWC and Engineer in writing about such condition. Contractor shall not further disturb such condition or perform any Work in connection therewith (except with respect to an emergency) until receipt of a written statement approved by PWC permitting Contractor to do so.

- (b) After receipt of Contractor's written notice, Project Engineer will review the subsurface or physical condition or Underground Facilities in question; determine the necessity of PWC obtaining additional exploration or tests with respect to the condition; conclude whether the condition falls within any of the differing site condition categories in this Section5.03; and obtain any pertinent cost or schedule information from Contractor.
- (c) Project Engineer will issue a written statement to Contractor regarding the subsurface or physical condition or Underground Facilities in question, which addresses the resumption of Work in connection with such condition and indicates whether any change in the Contract Documents will be made.
- (d) Possible Price and Times Adjustments:
 - (i) Contractor shall be entitled to an equitable adjustment in Contract Price or Contract Times, or both, to the extent that the existence of a differing subsurface or physical condition or Underground Facilities, or any related delay, disruption, or interference, causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:

- 1) such condition must fall within at least one of the categories in this Section 5.03; and,
- 2) Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.
- (ii) Contractor shall not be entitled to any adjustment in the Contract Price or Contract Times with respect to a subsurface or physical condition or Underground Facilities if:
- 1) Contractor knew of the existence of such condition at the time Contractor proffered its Bid to PWC or executed the applicable Agreement for the Project; or
- 2) the existence of such condition reasonably could have been discovered or revealed as a result of any examination, investigation, exploration, test, or study of the Site and contiguous areas expressly required by the Bidding Requirements or Contract Documents to be conducted by or for Contractor prior to Contractor's Bid; or
- 3) Contractor failed to give the written notice as required.
- (iii) If PWC and Contractor agree regarding Contractor's entitlement to, and the amount or extent of, any adjustment in the Contract Price or Contract Times, or both, then any such adjustment shall be set forth in a Change Order.
- (iv) Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, or both, no later than 30 calendar days after Project Engineer's written statement to Contractor regarding the subsurface or physical condition or Underground Facilities in question.

Section 5.04 Underground Utilities

- (a) Contractor shall ascertain the location and type of all underground utility lines or structures that may be located within the limits of the Site or any area where Work is to be performed.
 - (i) The exact location of underground utilities or structures may vary from prior plans, permits, maps, or other documentation, and others may not be designated. The Contractor is fully responsible for verification of the exact location of all underground utility lines or structures within the limits of the Site or the area where the work is to be performed, whether known or unknown by PWC, and for providing necessary protection and/or repair if damage.
 - (ii) Should uncharted or incorrectly charted piping or other utilities be encountered during excavations, the Contractor shall immediately halt any Work, notify PWC, and await direction from PWC before proceeding with any Work. The Contractor shall fully cooperate with PWC and any other utility company in keeping respective services and facilities in operation.
- (b) PWC has used reasonable care to locate and depict existing underground installation on the construction drawings, but the accuracy cannot be guaranteed, and some items may not be shown which exist. Actual horizontal and vertical locations have not been verified. As part of the Work, the Contractor is required to dig up each utility which may conflict with construction in advance to verify locations. The utilities shall be "dug up" a minimum of fourteen (14) Days in advance of actual installation of new utilities to allow PWC an opportunity to adjust grades and alignments, to avoid a conflict, and to address

any other issues.

- (c) The Contractor shall adhere to the provisions of the North Carolina Underground Utility Safety and Damage Prevention Act. The Contractor shall make a documented request to the North Carolina One Call Center, and/or individual utility owners, in order to locate any facilities within the Site limits or any area where Work is to be performed at least forty-eight (48) hours in advance of the day the Work is scheduled to begin. The Contractor shall include the cost of any coordination and cooperation for utilities in its Bid.
 - (i) Location assistance requested from PWC by Contractor should include the actual horizontal location, type number, size, and depth of all lines. All costs associated with locating and marking existing utilities or the utilities representatives shall be the responsibility of the Contractor.
 - (ii) The Owner, Project Engineer, Design Engineer, and/or Consultants shall not be liable to the Contractor for any claims, costs, losses, or damages incurred or sustained on or in connection with locating existing underground installations.
- (d) If the Contractor fails to schedule locates or perform advance physical locations in advance of the construction and a conflict arises, the Contractor will be required to make corrective measures as instructed by the Project Engineer at the Contractor's expense. The Contractor's failure to advance plan (minimum fourteen (14) days) by physically uncovering existing utilities in advance of construction shall not be cause for claim of lost time or for additional compensation. No additional payment will be made for re-mobilization required by the utility locator.
 - (i) The Contractor shall inform all equipment operators, either those employed by him or those employed by his subcontractors, of information obtained from the utility owners prior to initiation of any aspect of any Work.
- (e) PWC and Design Engineer shall not be responsible for the accuracy or completeness of any information or data provided to the Contractor with respect to underground facilities.
- (f) The entire cost of all of the following will be included in the Contract Price, and Contractor shall bear full responsibilities for all such costs, including but not limited to:
 - (i) Reviewing and checking all such information and data;
 - (ii) Locating all underground facilities shown or indicated in the Contract Documents;
 - (iii) Coordination of the Work with the owners of such underground facilities, including PWC, during any portion of the Work; and
 - (iv) The safety and protection of all such underground facilities and repairing any damage thereto resulting from the Work.
 - (g) Contractor shall be responsible for the discovery of existing underground installations, in advance of any excavating or trenching as required in the Contract Documents.

- (h) If an underground facility is discovered at or contiguous to the Site that was not shown or indicated in the Contract Documents or of which Contractor was not aware prior to starting that portion of any Work, Contractor shall, immediately after becoming aware thereof and before further disturbing conditions affected thereby or performing any Work in connection therewith (except in an emergency), identify the owner of such underground facility and give written notice to PWC. Upon receipt of written notice, PWC will review the pertinent condition, determine the necessity of obtaining additional information, and advise Contractor in writing. During such time, Contractor shall be responsible for the safety and protection of such underground facility. If PWC concludes that a change in the Contract Documents is required, a Change Order will be issued.
 - (i) The Contract Price and/or the Contract Time, may be adjusted if PWC determines, in its discretion, that the existence of such differing subsurface or physical condition causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work subject to the following:
 - 1) Facility was not shown or indicated in the Contract Documents, and
 - 2) The Contractor did not know of or could not anticipate the facility.

Section 5.05 Hazardous Environmental Conditions at Site

- (a) Contractor shall not be responsible for removing or remediating any Hazardous Environmental Condition encountered, uncovered, or revealed at the Site unless such removal or remediation is expressly identified in the Contract Documents to be within the scope of the Work or Hazardous Environmental Condition was caused by Contractor.
- (b) Contractor shall be responsible for controlling, containing, and removing all Constituents of Concern brought to the Site by Contractor, Subcontractors, Suppliers, or anyone else for whom Contractor is responsible, and for any associated costs; and for the costs of removing and remediating any Hazardous Environmental Condition created by the presence of any such Constituents of Concern.
- (c) If Contractor encounters, uncovers, or reveals a Hazardous Environmental Condition whose removal or remediation is not expressly identified in the Contract Documents as being within the scope of the Work, or if Contractor or anyone for whom Contractor is responsible creates a Hazardous Environmental Condition, then Contractor shall immediately: (1) secure or otherwise isolate such condition; (2) stop all Work in connection with such condition and in any area affected thereby (except in an emergency); and (3) immediately notify Project Engineer (and promptly thereafter confirm such notice in writing). Project Engineer will evaluate such condition or take corrective action, if any. If Contractor or anyone for whom Contractor is responsible created the Hazardous Environmental Condition in question, then PWC may have the Hazardous Environmental Condition removed and remediated and impose a set-off against payments to Contractor to account for the reasonable associated costs.
- (d) Contractor shall not resume Work in connection with such Hazardous Environmental Condition or in any affected area until after PWC has delivered written notice to Contractor either (1) specifying that such condition and any affected area is or has been rendered safe for the resumption of Work, or (2) specifying any special conditions under which such Work may be resumed safely.

- (e) If PWC and Contractor cannot agree as to entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times, or both, as a result of such Work stoppage or such special conditions under which Work is agreed to be resumed by Contractor, then within thirty (30) calendar days of PWC's written notice regarding the resumption of Work, Contractor may submit a Change Proposal or PWC may impose a set-off.
- (f) If after receipt of such written notice Contractor does not agree to resume such Work based on reasonable evidence it is unsafe or does not agree to resume such Work under such special conditions, then PWC may order the portion of the Work that is in the area affected by such condition to be deleted from the Work.

Article VI. Bonds and Insurance

Section 6.01 Performance and Payment Bonds

- (a) Contractor shall obtain and furnish to PWC a performance bond in the amount of one hundred percent (100%) of the Contract Price, conditioned upon the faithful performance of the Project and all Work in accordance with the Contract Documents, which bond shall be solely for the protection of PWC.
- (b) Contractor shall obtain and furnish to PWC a payment bond in the amount of one hundred percent (100%) of the Contract Price, conditioned upon the prompt payment for all labor or materials for which the Contractor or one or more of its subcontractors is liable, which payment bond shall be solely for the protection of the persons furnishing materials or performing labor for which the Contractor is liable.
- (c) The performance bond and the payment bond shall be executed by one or more surety companies legally authorized to do business in the State of North Carolina, shall become effective upon the awarding of the construction contract by PWC to Contractor, and shall at all times comply with the requirements set forth in Article 3 of North Carolina General Statutes Chapter 44A.
- (d) In the event PWC deems the surety or sureties upon any bond necessary for the Agreement and the completion of the Project, or if for any reason, such bond ceases to be adequate to cover the performance and/or payment of the Work, Contractor shall, at its expense, and within ten (10) days after the receipt of notice from PWC, furnish such additional bond(s) in such form and amount, and with such surety or sureties, as shall be satisfactory to PWC. In such event no further payment to Contractor shall be deemed to be due under this Agreement until new or additional security for the performance and payment of the Project shall be furnished in manner and form satisfactory to PWC.
- (e) By executing the Agreement, Contractor understands and acknowledges that PWC, as a public authority, and the City, as a municipal corporation, are not subject to the provisions of Articles 1 and 2 of Chapter 44A of the General Statutes, in accordance with G.S. 44A-34 and applicable law.

Section 6.02 Insurance

(a) Contractor shall maintain during the life of the Agreement and during the completion of any Work the following insurance coverages, which insurance shall be placed with insurance companies authorized to do business in the State of North Carolina and rate A minus VII or

better by the current edition of Best's Key Rating Guide or otherwise approved in writing by PWC:

- (i) Commercial general liability insurance with limits of \$1,000,000 per occurrence, \$2,000,000 aggregate other than products/completed operations; \$2,000,000 aggregate for products/completed. Commercial general liability coverage shall be written on an "occurrence" basis.
- (ii) Automobile liability insurance in an amount not less than \$1,000,000 combined single limit per accident for bodily injury and property damage from owned, non-owned, and hired automobiles.
- (iii) Workers' compensation insurance as required by the Laws and Regulations. In the event any employee(s), contractor(s), or subcontractor(s) engaged to perform any Work under the Agreement is not protected under the applicable workers' compensation laws, the Contractor shall provide adequate coverage for the protection of such employee(s), contractor(s), or subcontractor(s) not otherwise protected.
- (iv) In the event the Project concerns building construction or repair work, Contractor shall purchase and maintain "Builder's Risk" insurance. This insurance shall include the interests of the PWC, Contractor, and any Subcontractor(s) and shall be written on a one hundred percent (100%) completed value basis (full value as of the date that all construction is finished and includes the Contractor's Contract Price), and to remain in force until Completion of the Project.
- (v) Regardless of the nature of the work to be performed, coverage must also be provided for the theft or damage of building materials and supplies, which are not permanently attached or stored on Site for any period of time. This coverage shall be an "Installation Floater." If no building construction or repair is involved for the Project, the amount of the coverage shall equal the value of the materials stored on site.
- (b) Prior to initiating any Work on the Project, Contractor shall deliver certificates of insurance confirming each such coverage set forth above, and Contractor shall direct its insurers to provide annually to PWC certificates confirming each such coverage during the coverage period.
- (c) PWC shall be named as an additional insured in the comprehensive automobile and commercial liability insurance policies.
- (d) Contractor shall not reduce or allow the required insurance coverages to lapse without PWC's prior written approval. All policies for insurance must be endorsed to contain a provision giving PWC a thirty (30) calendar day prior written notice by certified mail of any cancellation of that policy or material reduction in coverage. Should a notice of cancellation be issued for non-payment of premiums or any part thereof, or should Contractor fail to provide and maintain certificates as set forth herein, PWC shall have the right, but shall not have the obligation, to pay such premium to the insurance company or to obtain such coverage and to deduct such payment from any sums that may be due or become due to Contractor, or to seek reimbursement for said payments from Contractor. Any such sums paid by PWC shall be due and payable immediately by Contractor upon notice from PWC.
- (e) The insurance coverage requirements shall not be construed as a limitation on

Contractor's responsibilities and liabilities pursuant to the terms and conditions of this Agreement. Contractor's obligation to maintain insurance for three (3) years after Completion of the Project shall survive the termination of this Agreement.

- (f) If Contractor fails to obtain and maintain any required insurance, PWC may exclude Contractor from the Site, impose an appropriate set-off against payment, and exercise PWC's termination rights pursuant to the Contract Documents.
- (g) PWC does not represent that insurance coverage and limits established in this Contract necessarily will be adequate to protect Contractor or Contractor's interests.

Article VII. Contractor's Responsibilities

Section 7.01 Supervision and Superintendence

- (a) Contractor shall supervise, inspect, and direct the Work competently and efficiently, devoting such attention and applying such skills and expertise as may be necessary to perform the Work in accordance with the Contract Documents. Contractor shall be solely responsible for the means, methods, techniques, sequences, and procedures of construction subject to the terms, provisions, and specifications set forth in the Contract Documents.
- (b) At all times during the progress of the Work, Contractor shall assign a competent superintendent, satisfactory to Project Engineer, to supervise the Work and to respond to Project Engineer concerning PWC's interests in the Work.
- (c) Contractor's superintendent shall have full authority to act on behalf of Contractor and all communications, instructions, directions, and notices given to the superintendent by the Project Engineer shall be binding to the Contractor.
- (d) Contractor's superintendent shall be responsible for coordination of the Work with other contractors or subcontractors. The superintendent shall not be replaced without written notice to PWC except under extraordinary circumstances.

(e) Subcontractors

- (i) Contractor shall submit the names and references all Subcontractors to the Project Engineer for approval before commencing any Work.
- 1) In the event Contractor seeks to substitute any Subcontractor that was identified in Contractor's Bid, Contractor shall promptly provide PWC with: (1) the Subcontractor it seeks to substitute; (2) the identity of the Subcontractor to be substituted; and (3) the reason for the requested substitution.
- 2) PWC will review the requested substitution within five (5) Business Days and provide written approval or denial of the substitution, with such approval not to be unreasonably withheld.
- (ii) Contractor's superintendent shall be available to be present at the Site at any time that any Subcontractor(s) is performing any of the Work. Construction activity shall be

stopped if the Contractor's superintendent is not available to be at the Site.

Section 7.02 Labor; Working Hours

- (a) Contractor shall provide competent, suitably qualified personnel to survey and lay out the Work and perform construction as required by the Contract Documents. Contractor shall at all times maintain good discipline and order at the Site. Contractor shall remove from the Project any person who appears incompetent, disorderly, or otherwise unsatisfactory. Contractor shall also remove any person who appears in PWC's sole discretion to be incompetent, disorderly, or otherwise unsatisfactory
- (b) Except as otherwise required for the safety or protection of persons or the Work or property at the Site or adjacent thereto, and except as otherwise stated in the Contract Documents, all Work at the Site shall be performed on Business Days. Contractor will not perform Work on non-Business Days. Contractor may perform Work outside regular working hours or on Saturdays, Sundays, or legal holidays only with PWC's written consent, which will not be unreasonably withheld. In such circumstances, Contractor shall submit a written request to PWC at least two (2) Business Days prior to any Work that it requests to complete on a non-Business Day and PWC will, in its sole discretion, approve or deny such request. If such work outside of a Business Day is approved, PWC will set forth the specific parameters that Contractor must follow, including time of work, personnel, and any other issues.8

Section 7.03 Services, Materials, and Equipment

- (a) Unless otherwise specified in the Contract Documents, Contractor shall provide and assume full responsibility for all services, materials, equipment, labor, transportation, construction equipment and machinery, tools, appliances, fuel, power, light, heat, telephone, water, sanitary facilities, temporary facilities, and all other facilities and incidentals necessary for the performance, testing, start up, and Completion of the Project, whether or not such items are specifically called for in the Contract Documents.
- (b) All materials and equipment incorporated into the Work shall be of good quality and new, except as otherwise specified in the Contract Documents. All special warranties and guarantees required by the Specifications shall expressly run to the benefit of PWC. If required by PWC or its designee, Contractor shall furnish satisfactory evidence (including reports of required tests) as to the source, kind, and quality of materials and equipment.
- (c) All materials and equipment shall be stored, applied, installed, connected, erected, protected, used, cleaned, and conditioned in accordance with instructions of the applicable Supplier, except as otherwise may be specified in the Contract Documents.

Section 7.04 "Or Equals"

(a) Whenever an item of material or equipment is specified or described in the Contract Documents by using the name of a proprietary item or the name of a particular Supplier, the specification or description of such an item is intended to establish the type, function, appearance, and quality required. Unless the specification or description contains or is followed by words reading that no like, equivalent, or "or equal" item is permitted, Contractor may request that Project Engineer authorize the use of other items of material or equipment under the circumstances described below.

- (i) If Project Engineer determines that an item of material or equipment proposed by Contractor is functionally equal to that named and sufficiently similar so that no change in related Work will be required, Project Engineer shall deem it an "or equal" item and confirm such in writing to Contractor. A proposed item of material or equipment will be considered functionally equal to an item so named if:
- 1) in the exercise of reasonable judgment Project Engineer determines that:
- a) it is at least equal in materials of construction, quality, durability, appearance, strength, and design characteristics;
- b) it will reliably perform at least equally well the function and achieve the results imposed by the design concept of the completed Project as a functioning whole;
- c) it has a proven record of performance and availability of responsive service; and
- d) it is not objectionable to PWC.
- 2) Contractor certifies that, if approved and incorporated into the Work:
 - a) there will be no increase in the Contract Price or Contract Times; and
 - b) it will conform substantially to the detailed requirements of the item specified in the Contract Documents.
- (b) Contractor shall provide all data in support of any proposed "or equal" item at Contractor's expense.
- (c) Project Engineer will be allowed a reasonable time to evaluate each "or-equal" request. Project Engineer may require Contractor to furnish additional data about the proposed "or-equal" item. Project Engineer will be the sole judge of acceptability. Contractor shall not order, furnish, install, or utilize any "or-equal" it until Project Engineer has reviewed the request, determined that the proposed item is an "or-equal," and provided written confirmation to Contractor.
- (d) Project Engineer's denial of an "or-equal" request shall be final and binding and may not be reversed through an appeal under any provision of the Contract Documents.

Section 7.05 Concerning Subcontractors, Suppliers, and Others

- (a) Contractor may retain Subcontractors and Suppliers for the performance of parts of the Work. Such Subcontractors and Suppliers must be acceptable to PWC.
- (b) Contractor shall not subcontract more than forty-nine percent (49%) of the final Contract Price.
- (c) Contractor shall retain specific Subcontractors, Suppliers, or other individuals or entities for the performance of designated parts of the Work if required by the Contract Documents.
- (d) After the submittal of Contractor's Bid or final negotiation of the terms of the Agreement, PWC may not require Contractor to retain any Subcontractor, Supplier, or other individual or entity to furnish or perform any of the Work.
- (e) Prior to entry into any binding subcontract or purchase order, Contractor shall submit to PWC the identity of the proposed Subcontractor or Supplier (unless PWC has already deemed such proposed Subcontractor or Supplier acceptable, during the bidding process

- or otherwise). Such proposed Subcontractor or Supplier shall be deemed acceptable to PWC unless PWC raises a substantive, reasonable objection within five (5) Business Days.
- (f) No acceptance by PWC of any such Subcontractor, Supplier, or other individual or entity, whether initially or as a replacement, shall constitute a waiver of the right of PWC to the completion of the Work in accordance with the Contract Documents.
- (g) Contractor shall be fully responsible to PWC for all acts and omissions of the Subcontractors, Suppliers, and other individuals or entities performing or furnishing any of the Work just as Contractor is responsible for Contractor's own acts and omissions.
- (h) Contractor shall be solely responsible for scheduling and coordinating the Subcontractors, Suppliers, and all other individuals or entities performing or furnishing any of the Work.
- (i) Contractor shall restrict all Subcontractors, Suppliers, and such other individuals or entities performing or furnishing any of the Work from communicating with PWC, except through Contractor or in case of an emergency, or as otherwise expressly allowed herein.
- (j) All Work performed for Contractor by a Subcontractor or Supplier shall be pursuant to an appropriate contractual agreement that specifically binds the Subcontractor or Supplier to the applicable terms and conditions of the Contract Documents for the benefit of PWC.
- (k) PWC may furnish to any Subcontractor or Supplier, to the extent practicable, information about amounts paid to Contractor on account of Work performed for Contractor by the particular Subcontractor or Supplier.
- (I) Nothing in the Contract Documents:
 - (i) shall create for the benefit of any such Subcontractor, Supplier, or other individual or entity any contractual relationship between PWC or Design Engineer and any such Subcontractor, Supplier, or other individual or entity; nor
 - (ii) shall create any obligation on the part of PWC or Design Engineer to pay or to see to the payment of any money due any such Subcontractor, Supplier, or other individual or entity except as may otherwise be required by Laws and Regulations.

Section 7.06 Patent Fees and Royalties

(a) Contractor shall pay all license fees and royalties and assume all costs incident to the use in the performance of the Work or the incorporation in the Work of any invention, design, process, product, or device that is the subject of patent rights or copyrights held by others. If a particular invention, design, process, product, or device is specified in the Contract Documents for use in the performance of the Work and if, to the actual knowledge of PWC, its use is subject to patent rights or copyrights calling for the payment of any license fee or royalty to others, the existence of such rights shall be disclosed by PWC in the Contract Documents.

Section 7.07 Permits

(a) Unless otherwise specified in the Contract Documents, Contractor shall obtain and pay for all construction permits and licenses necessary to achieve Completion of the Project.

Contractor shall timely seek assistance from PWC if necessary to obtain any permits or

licenses; provided that, the Contract Time shall not be extended if PWC determines, in its discretion, that Contractor delayed or otherwise did not act expeditiously in requesting such assistance. PWC shall assist Contractor, when necessary, in obtaining such permits and licenses. Contractor shall pay all governmental charges and inspection fees necessary for Completion of the Project that are applicable at the time of the submission of Contractor's Bid.

Section 7.08 Taxes

(a) Contractor shall pay all sales, consumer, use, and other similar taxes required to be paid by Contractor in accordance with the applicable Laws and Regulations for the Project and which are applicable during the performance of the Work.

Section 7.09 Laws and Regulations

- (a) Contractor shall give all notices required by, and shall comply with, all Laws and Regulations applicable to the Project. Except as otherwise expressly required, PWC shall not be responsible for monitoring Contractor's compliance with any Laws or Regulations.
- (b) Contractor shall bear all resulting costs and losses for any of its actions or inactions that are contrary to Laws or Regulations.
- (c) PWC or Contractor may give notice to the other party of any changes after the submission of Contractor's Bid (or after the date when Contractor became bound under the Agreement) concerning any Laws or Regulations having an effect on the Contract Price or Contract Times, including but not limited to changes in Laws or Regulations having an effect on procuring permits and on sales, use, value-added, consumption, and other similar taxes. If PWC and Contractor are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times resulting from such changes, then within 30 calendar days of such notice Contractor may submit a Change Proposal.

Section 7.10 Record Documents

(a) Contractor shall maintain in good order one (1) printed record copy of all Drawings, Specifications, Addenda, Change Orders, Work Change Directives, Field Orders, written interpretations and clarifications, and approved Shop Drawings. These record documents, together with all approved Samples, will be available to Project Engineer for reference. Upon completion of the Work, Contractor shall deliver these record documents to PWC.

Section 7.11 Safety and Protection

- (a) Contractor shall be solely responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the Work. Such responsibility does not relieve Subcontractors of their responsibility for the safety of persons or property in the performance of their work, nor for compliance with applicable safety Laws and Regulations. Contractor shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury, or loss to:
 - (i) all persons on the Site or who may be affected by the Work;
 - (ii) all the Work and materials and equipment to be incorporated therein, whether in storage on or off the Site; and

- (iii) other property at the Site or adjacent thereto, including trees, shrubs, lawns, walks, pavements, roadways, structures, other work in progress, utilities, and Underground Facilities not designated for removal, relocation, or replacement in the course of construction.
- (b) Contractor shall comply with all applicable Laws and Regulations relating to the safety of persons or property, or to the protection of persons or property from damage, injury, or loss, and shall erect and maintain all necessary safeguards for such safety and protection. Contractor shall notify PWC, the owners of adjacent property or Underground Facilities, and other contractors and owners performing work at or adjacent to the Site, when prosecution of the Work may affect them, and shall cooperate with them in the protection, removal, relocation, and replacement of their property or work in progress.
- (c) Contractor shall comply with the requirement of any of PWC's applicable health programs, which may be revised from time to time based on specific circumstances or applicable guidance from the Center for Disease Control or other applicable entity. Such health programs will be identified in the Special Conditions if applicable to the Project.
- (d) Contractor shall comply with the requirements of PWC's applicable safety programs. The Special Conditions identify any of PWC's safety programs that are applicable to the Project.
- (e) Contractor shall remedy, at its expense, all damage, injury, or loss to any property caused, directly or indirectly, in whole or in part, by Contractor, any Subcontractor, Supplier, or any other individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable.
- (f) Contractor's duties and responsibilities for safety and protection shall continue until such time as Completion of the Project is achieved.
- (g) Contractor's duties and responsibilities for safety and protection shall resume whenever Contractor or any Subcontractor or Supplier returns to the Site to fulfill warranty or correction obligations, or to conduct other tasks arising from the Contract Documents.
- (h) Contractor shall designate in writing to PWC a qualified and experienced safety representative at the Site whose duties and responsibilities shall be the prevention of accidents and the maintaining and supervising of safety precautions and programs.

Section 7.12 Emergencies

(a) In emergencies affecting the safety or protection of persons or the Work or property at the Site or adjacent thereto, Contractor is obligated to, and shall, act to prevent threatened damage, injury, or loss. Contractor shall give PWC prompt written notice if Contractor believes that any significant changes in the Work or variations from the Contract Documents have been caused or are required as a result of any emergency. If PWC determines that a change in the Contract Documents is required because of the action taken by Contractor in response to such an emergency, a Work Change Directive or Change Order will be issued.

Section 7.13 Shop Drawings, Samples, and Other Submittals

(a) Contractor shall timely submit Shop Drawings and Samples required by the Contract

Documents to Project Engineer for review and approval in accordance with applicable specifications.

- (b) Before submitting a Shop Drawing or Sample, Contractor shall have
 - (i) reviewed the Shop Drawing or Sample with other Shop Drawings and Samples and with the requirements of the Work and the Contract Documents;
 - (ii) verified all measurements, quantities, dimensions, performance and design criteria, installation requirements, materials, catalog numbers, and similar information;
 - (iii) verified the suitability of all materials and equipment offered with respect to the indicated application, fabrication, shipping, handling, storage, assembly, and installation pertaining to the performance of the Work; and
- (iv) verified all information relative to Contractor's responsibilities for means, methods, techniques, sequences, and procedures of construction, and safety precautions and programs incident thereto.
- (c) With each submittal, Contractor shall give Project Engineer specific written notice of any variations that the Shop Drawing or Sample may have from the requirements of the Contract Documents. This notice shall be a written communication separate from the Shop Drawings or Sample submittal; and, in addition, in the case of Shop Drawings by a specific notation made on each Shop Drawing submitted to PWC for review and approval of each such variation.
- (d) Where a Shop Drawing or Sample is required by the Contract Documents, any related Work performed prior to Project Engineer's review and approval of the pertinent submittal will be at the sole expense and responsibility of Contractor.
- (e) Project Engineer will provide timely review of any required Shop Drawings and Samples. Such review, and subsequent determination of approval, will be only to determine if the items covered by the submittals will, after installation or incorporation in the Work, conform to the information given in the Contract Documents and be compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents.
- (f) Project Engineer's review and approval will not extend to means, methods, techniques, sequences, or procedures of construction or to safety precautions or programs incident thereto.
- (g) Project Engineer's review and approval of a Shop Drawing or Sample, or of a variation from the requirements of the Contract Documents, shall not change the Contract Times or Contract Price, unless such changes are included in a Change Order.
- (h) Project Engineer's receipt, review, acceptance or approval of a Shop Drawing, Sample, or other submittal shall not result in such item becoming a Contract Document.
- (i) Contractor shall perform the Work in compliance with the requirements and commitments set forth in approved Shop Drawings and Samples.
- (i) Resubmittal Procedures:
 - (i) Contractor shall make corrections required by Project Engineer and shall return the

required number of corrected copies of Shop Drawings and submit new Samples as required for review and approval. Contractor shall direct specific attention in writing to revisions other than the corrections called for by PWC or Project Engineer on previous submittals.

- (ii) Contractor shall furnish required submittals with sufficient information and accuracy to obtain required approval of an item with no more than three (3) submittals. If PWC has engaged a Design Engineer for the Project, Design Engineer will record Design Engineer's time for reviewing a fourth or subsequent submittal of a Shop Drawings, sample, or other item requiring approval, and Contractor shall be responsible for Design Engineer's charges to PWC for such time. PWC may impose a set-off against payments due to Contractor to secure reimbursement for such charges.
- (iii) If Contractor requests a change of a previously approved submittal item, Contractor shall be responsible for Design Engineer's charges to PWC for its review time, and PWC may impose a set-off against payments due to Contractor to secure reimbursement for such charges, unless the need for such change is beyond the control of Contractor.

Section 7.14 Contractor's General Warranty and Guarantee

- (a) In order to induce PWC to enter into an Agreement with Contractor for the Project, Contractor warrants and guarantees to PWC that:
 - (i) Contractor is duly licensed in the State of North Carolina to complete all Work necessary for the Project, is duly organized, validly existing and in good standing and has all requisite powers, rights, and authority to execute, enter into, and perform the Agreement in accordance with the terms and conditions of the Agreement, and the Agreement constitutes a legal, valid, and binding obligation of Contractor enforceable against it in accordance with its terms.
 - (ii) Contractor has read the Contract Documents, and acknowledges and understands all data, materials, specifications, and requirements identified in the Contract Documents.
 - (iii) Contractor has visited the site for the Project, conducted a thorough, visual examination of the site and adjacent areas, and become familiar with and is satisfied as to the general, local, and site conditions that may affect cost, progress, and performance in completing the Project.
- (iv) Contractor is familiar with and is satisfied as to all laws and regulations that may affect cost, progress, and performance to complete the Project.
- (v) Contractor has carefully studied all: (1) reports of explorations and tests of subsurface conditions at or adjacent to the site and all drawings of physical conditions relating to existing surface or subsurface structures at the site that have been identified in the Detail Specifications and any accompanying reports and drawings, and (2) reports and drawings relating to any Hazardous Environmental Condition at or adjacent to the site that have been identified in the Contract Documents and any accompanying reports and drawings.
- (vi) Contractor has considered the information known to Contractor itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Contract Documents; and the Site-related reports and drawings identified in the Contract Documents, if any, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor; and (3) Contractor's safety precautions and programs.

- (vii) Based on the information and observations referred to in subsection "(v)" of this Section, Contractor agrees that no further examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Contract Price and in accordance with the other terms and conditions of the Contract Documents.
- (viii) Contractor is aware of the general nature of work to be performed by PWC and others at the Site that relates to the Work as indicated in the Contract Documents.
- (ix) Contractor has given PWC written notice of all conflicts, errors, ambiguities, or discrepancies that Contractor has discovered in the Contract Documents, and the written resolution thereof by PWC is acceptable to Contractor.
- (x) The Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.
- (xi) Contractor's entry into this Agreement constitutes an incontrovertible representation by Contractor that, without exception, all prices in the Agreement are premised upon performing and furnishing the Work required by the Contract Documents.
- (xii) Contractor has no business or personal relationship with any PWC Commissioner, officer, director, manager, or supervisor and Contractor covenants to disclose immediately to PWC any such relationship that develops during the performance of Work on the Project.
- (b) Contractor's obligation to perform and complete the Work in accordance with the Contract Documents shall be absolute. None of the following will constitute an acceptance of Work that is not in accordance with the Contract Documents or a release of Contractor's obligation to perform the Work in accordance with the Contract Documents:
 - (i) observations by Project Engineer;
 - (ii) recommendation by Project Engineer or payment by PWC of any progress or final payment;
 - (iii) the issuance of a certificate of Substantial Completion by Project Engineer or any payment related thereto by PWC;
- (iv) use or occupancy of the Work or any part thereof by PWC;
- (v) any review and approval of a Shop Drawing or Sample submittal:
- (vi) the issuance of a notice of acceptability by Project Engineer;
- (vii) any inspection, test, or approval by others; or
- (viii) any correction of defective Work by PWC.
- (c) If the Contract Documents requires the Contractor to accept the assignment of a contract entered into by PWC, then the specific warranties, guarantees, and correction obligations contained in the assigned contract shall govern with respect to Contractor's performance obligations to PWC for the Work described in the assigned contract.

Section 7.15 Indemnification

- (a) Contractor shall indemnify, defend, and hold harmless PWC and its Commissioners, officers, employees, agents, and representatives and the City and its elected officials, managers, employees, agents, and representatives and Designer (collectively "Indemnitees") from and against all claims, actions, liabilities, damages, losses, costs, and expenses (including, without limitation, injury to or death of any persons and damage to property, economic and consequential damages and attorneys' fees) asserted by one or more third parties against one or more of the Indemnitees if the Fault of one or more Responsible Persons is a proximate cause of the loss, damage, or expense indemnified.
- (b) Contractor's obligation to indemnify, defend, and hold harmless the Indemnitees shall survive the termination of the Agreement.

(c) In any and all claims against the Indemnitees of Contractor, any Subcontractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, Contractor's indemnification obligation shall not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Contractor or any such Subcontractor, Supplier, or other individual or entity under workers' compensation acts, disability benefit acts, or other employee benefit acts.

Section 7.16 Claims Procedure

- (a) PWC shall notify the Contractor of all potential claims related to the Work within seven (7) calendar days of receiving notification or having knowledge of such potential claim. Should the Contractor receive a potential claim related to the Work, the Contractor shall notify PWC within seven (7) calendar days of receiving notification. The Contractor shall provide the claimant and PWC with a written response acknowledging receipt of the claim within seven (7) calendar days.
- (b) If the Contractor meets with the Claimant about the claim, a representative designated by PWC shall be present at all times. PWC shall maintain a record of any claim received, and the steps taken to resolve. PWC shall also concurrently investigate each case. The Contractor agrees to furnish PWC any information regarding the claim, the actions which led to the claim and/or the investigation of the claim. Contractor shall provide their proposed response to PWC within thirty (30) calendar days of receiving the claim. Upon receipt of the response PWC and the Contractor will discuss and reach a mutual agreement of the response necessary to send to the Claimant within fifteen (15) calendar days. Once the agreement is made the Contractor shall make a formal written resolution to the claimant.
- (c) Failure to act in good faith or respond to a claim in the timelines established by the Contract Documents will constitute a lack of response by the Contractor, therefore validating the claim. PWC will deduct the total amount of the claim from the monthly pay application. Failure to comply with the above requirements for resolving claims may, at the sole discretion of PWC, result in breach of contract.
- (d) The Contractor is aware of these claims procedures and understands that it is the PWC's practice to pursue reimbursement/subrogation for any and all claims related expenses, which are incurred as a result of the Contractor's performance under this Contract Documents and allowed within the applicable statute of limitations.

Section 7.17 Delegation of Professional Design Services

- (a) Contractor will not be required to provide professional design services unless such services are specifically required by the Contract Documents for a portion of the Work or unless such services are required to carry out Contractor's responsibilities for construction means, methods, techniques, sequences and procedures. Contractor shall not be required to provide professional services in violation of applicable Laws and Regulations.
- (b) If professional design services or certifications by a design professional related to systems, materials, or equipment are specifically required of Contractor by the Contract Documents, PWC will specify all performance and design criteria that such services must satisfy.

Contractor shall cause such services or certifications to be provided by a properly licensed professional, whose signature and seal shall appear on all drawings, calculations, specifications, certifications, and other submittals prepared by such professional. Shop Drawings and other submittals related to the Work designed or certified by such professional, if prepared by others, shall bear such professional's written approval when submitted to PWC.

- (c) PWC shall be entitled to rely upon the adequacy, accuracy, and completeness of the services, certifications, or approvals performed by such design professionals, provided PWC has specified to Contractor all performance and design criteria that such services must satisfy.
- (d) Pursuant to this Section, PWC's, or its designee's, review and approval of design calculations and design drawings will be only for the limited purpose of checking for conformance with performance and design criteria given and the design concept expressed in the Contract Documents. PWC specifically retains final approval of such submittals.
- (e) Contractor shall not be responsible for the adequacy of the performance or design criteria specified by PWC.

Article VIII. PWC's Responsibilities

- (a) In awarding the bid to Contractor and executing the applicable Agreement, PWC acknowledges the following responsibilities:
 - (i) Except as otherwise provided in these General Conditions, PWC shall issue all communications directly to Contractor or its designee.
 - (ii) PWC may at its discretion replace Design Engineer and Project Engineer. The replacement Design Engineer or Project Engineer's status under the Contract Documents shall be that of the former Design Engineer or Project Engineer.
 - (iii) PWC shall promptly furnish the data required of PWC under the Contract Documents.
- (iv) PWC shall make payments to Contractor when they are due as provided in the Contract Documents.
- (v) PWC shall not supervise, direct, or have control or authority over, nor be responsible for, Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work. PWC will not be responsible for Contractor's failure to perform the Work in accordance with the Contract Documents.
- (vi) Upon request of Contractor, PWC shall furnish to Contractor reasonable evidence that financial arrangements have been made to satisfy PWC's obligations under the Contract Documents (including obligations under proposed changes in the Work).
- (vii) While at the Site, PWC's employees and representatives shall comply with the specific applicable requirements of Contractor's safety programs of which PWC has been informed.
- (viii) PWC shall furnish copies of any applicable PWC safety program(s) to Contractor, which Contractor shall review and implement.

Article IX. Amending the Contract Documents; Changes in the Work

Section 9.01 <u>Amending and Supplementing Contract Documents</u>

- (a) The Contract Documents may be amended or supplemented by a Change Order, a Work Change Directive, or a Field Order.
 - (i) Change Orders: If an amendment or supplement to the Contract Documents includes a change in the Contract Price or the Contract Times, such amendment or supplement must be set forth in a Change Order. A Change Order also may be used to establish amendments and supplements of the Contract Documents that do not affect the Contract Price or Contract Times.
 - (ii) Work Change Directives: A Work Change Directive will not change the Contract Price or the Contract Times, but is evidence that the parties expect that the modification ordered or documented by a Work Change Directive will be incorporated in a subsequently issued Change Order, following negotiations by the parties as to the Work Change Directive's effect, if any, on the Contract Price and Contract Times; or, if negotiations are unsuccessful, by a determination under the terms of the Contract Documents governing adjustments, expressly including Paragraph 9.04 regarding change of Contract Price. Contractor must submit any Change Proposal seeking an adjustment of the Contract Price or the Contract Times, or both, no later than 30 days after the completion of the Work set out in the Work Change Directive. PWC must submit any dispute or request seeking an adjustment of the Contract Price or the Contract Times, or both, no later than 60 days after issuance of the Work Change Directive.
 - (iii) Field Orders: Project Engineer may authorize minor changes in the Work if the changes do not involve an adjustment in the Contract Price or the Contract Times and are compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents. Such changes will be accomplished by a Field Order and will be binding on PWC and on Contractor, which shall perform promptly the Work involved. If Contractor believes that a Field Order justifies an adjustment in the Contract Price or Contract Times, or both, then before proceeding with the Work at issue, Contractor shall submit a Change Proposal as provided herein.

Section 9.02 <u>PWC-Authorized Changes in the Work</u>

(a) Without invalidating the Agreement and without notice to any surety, PWC may, at any time or from time to time, order additions, deletions, or revisions in the Work. Such changes shall be supported by Design Engineer's recommendation when applicable and to the extent the change involves the design (as set forth in the Drawings, Specifications, or otherwise), or other engineering or technical matters. Such changes may be accomplished by a Change Order or by a Work Change Directive. Upon receipt of any such document, Contractor shall promptly proceed with the Work as revised. Nothing in this paragraph shall obligate Contractor to undertake work that Contractor reasonably concludes cannot be performed in a manner consistent with Contractor's safety obligations under the Contract Documents or Laws and Regulations.

Section 9.03 Unauthorized Changes in the Work

(a) Contractor shall not be entitled to an increase in the Contract Price or an extension of the Contract Times with respect to any work performed that is not required by the Contract Documents, as amended, modified, or supplemented.

Section 9.04 Change of Contract Price

- (a) The Contract Price may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Price shall comply with the provisions of these General Conditions.
- (b) An adjustment in the Contract Price will be determined as follows:
 - (i) where the Work involved is covered by unit prices contained in the Contract Documents, then by application of such unit prices to the quantities of the items involved; or
 - (ii) where the Work involved is not covered by unit prices contained in the Contract Documents, then by a mutually agreed lump sum (which may include an allowance for overhead and profit as agreed to in writing by the Parties); or
 - (iii) where the Work involved is not covered by unit prices contained in the Contract Documents and the Parties do not reach mutual agreement to a lump sum, then on the basis of the Cost of the Work plus a reasonable Contractor's fee for overhead and profit.
- (c) Contractor's Fee: When applicable, the Contractor's fee for overhead and profit shall be determined as follows:
 - (i) a mutually acceptable fixed fee; or
 - (ii) if a fixed fee is not agreed upon, then a fee based on the following percentages of the various portions of the Cost of the Work:
 - 1) for unit prices, the Contractor's fee shall be fifteen percent (15%);
 - 2) for all other costs incurred, the Contractor's fee shall be five percent (5%);
 - 3) the amount of credit to be allowed by Contractor to PWC for any change that results in a net decrease in the Contract Price will be the amount of the actual net decrease in cost plus a deduction in Contractor's fee by an amount equal to five percent of such net decrease; and
 - 4) when both additions and credits are involved in any one change, the adjustment in Contractor's fee shall be computed on the basis of the net change.

Section 9.05 Change of Contract Times

- (a) The Contract Times may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Times shall comply with the provisions of Paragraph 9.06.
- (b) An adjustment of the Contract Times shall be subject to the limitations set forth in these Contract Document as it concerns delays in Contractor's progress.

Section 9.06 Change Proposals

- (a) Contractor shall submit a Change Proposal to PWC to request an adjustment in the Contract Times and/or Contract Price. The Change Proposal shall specify any proposed change in Contract Times or Contract Price, or both, or other proposed relief, and explain the reason for the proposed change, with citations to any governing or applicable provisions of the Contract Documents.
 - (i) Procedures: Contractor shall submit each Change Proposal to PWC promptly (but in no event later than 30 days) after the start of the event giving rise thereto, or after such initial decision. The Contractor shall submit supporting data, including the proposed change in

- Contract Price or Contract Time (if any), to PWC within 15 calendar days after the submittal of the Change Proposal. The supporting data shall be accompanied by a written statement that the supporting data are accurate and complete, and that any requested time or price adjustment is the entire adjustment to which Contractor believes it is entitled as a result of said event.
- (ii) PWC Action: PWC will review each Change Proposal and, within 30 calendar days after receipt of the Contractor's supporting data, either deny the Change Proposal in whole, approve it in whole, or deny it in part and approve it in part. Such actions shall be in writing to Contractor. If PWC does not take action on the Change Proposal within 30 calendar days, then the Change Proposal is deemed denied, thereby commencing the time for appeal under these General Conditions.
- (iii) Binding Decision: PWC's decision will be final and binding unless Contractor appeals the decision.

Section 9.07 Execution of Change Orders

- (a) PWC and Contractor shall execute appropriate Change Orders covering:
 - (i) changes in the Contract Price or Contract Times that are agreed to by the parties, including any undisputed sum or amount of time for Work performed in accordance with a Work Change Directive;
 - (ii) changes in Contract Price resulting from a PWC set-off, unless Contractor has duly contested such set-off;
 - (iii) changes in the Work which are: (a) ordered by PWC, (b) required because of PWC's acceptance of defective Work or PWC's correction of defective Work, or (c) agreed to by the parties, subject to the need for Design Engineer's recommendation if the change in the Work involves the design (as set forth in the Contract Documents), or other engineering or technical matters; and
- (iv) changes in the Contract Price or Contract Times, or other changes, which embody the substance of any final and binding results.
- (b) If PWC or Contractor refuses to execute a Change Order that is required to be executed under the terms of this Section, it shall be deemed to be of full force and effect as if fully executed.

Section 9.08 Notification to Surety

(a) If the provisions of any bond require notice to be given to a surety of any change affecting the general scope of the Work or the provisions of the Contract Documents (including, but not limited to, Contract Price or Contract Times), the giving of any such notice will be Contractor's responsibility. The amount of each applicable bond will be adjusted to reflect the effect of any such change.

Article X. Tests, Inspections, and Approvals; Correction, Removal, or Acceptance of Defective Work

Section 10.01 Access to Work

(a) PWC, Design Engineer, their consultants and other representatives and personnel of PWC, independent testing laboratories, and authorities having jurisdiction will have access to the Site and the Work at reasonable times for their observation, inspection, and testing.

Contractor shall provide them proper and safe conditions for such access and advise them of Contractor's safety procedures and programs so that they may comply therewith as applicable.

Section 10.02 <u>Tests, Inspections, and Approvals</u>

- (a) Contractor shall give Project Engineer timely notice of readiness of the Work (or specific parts thereof) for all required inspections and tests and shall cooperate with inspection and testing personnel to facilitate required inspections and tests.
- (b) PWC shall retain and pay for the initial services of an independent inspector, testing laboratory, or other qualified individual or entity to perform all inspections and tests expressly required by the Contract Documents to be furnished and paid for by PWC, except those costs incurred in connection with tests or inspections of covered Work shall be governed by the provisions of Paragraph 10.05.
- (c) If Laws or Regulations of any public body having jurisdiction require any Work (or part thereof) specifically to be inspected, tested, or approved by an employee or other representative of such public body, Contractor shall assume full responsibility for arranging and obtaining such inspections, tests, or approvals, pay all costs in connection therewith, and furnish the required certificates of inspection or approval to PWC.
- (d) Contractor shall be responsible for arranging, obtaining, and paying for all inspections and tests required:
 - (i) by the Contract Documents, unless the Contract Documents expressly allocate responsibility for a specific inspection or test to PWC;
 - (ii) to attain PWC's and Design Engineer's acceptance of materials or equipment to be incorporated in the Work;
 - (iii) by manufacturers of equipment furnished under the Contract Documents;
- (iv) for testing, adjusting, and balancing of mechanical, electrical, and other equipment to be incorporated into the Work; and
- (v) for acceptance of materials, mix designs, or equipment submitted for approval prior to Contractor's purchase thereof for incorporation in the Work.

Such inspections and tests shall be performed by independent inspectors, testing laboratories, or other qualified individuals or entities acceptable to PWC, as confirmed in writing by Project Engineer to Contractor.

- (e) If the Contract Documents require the Work (or part thereof) to be approved by PWC or its designee, then Contractor shall assume full responsibility for arranging and obtaining such approvals.
- (f) If any Work (or the work of others) that is to be inspected, tested, or approved is covered by Contractor without written concurrence of Project Engineer, Contractor shall, if requested by Project Engineer, uncover such Work for observation. Such uncovering shall be at Contractor's expense unless Contractor had given PWC timely notice of Contractor's intention to cover the same and PWC had not acted with reasonable promptness in response to such notice.

Section 10.03 Defective Work

- (a) It is Contractor's obligation to assure that the Work is not defective.
- (b) PWC or its designee has the authority to determine whether Work is defective, and to reject defective Work.
- (c) Prompt notice of all defective Work of which PWC has actual knowledge will be given to Contractor.
- (d) Promptly after receipt of written notice of defective Work, Contractor shall correct all such defective Work, whether or not fabricated, installed, or completed, or, if PWC has rejected the defective Work, remove it from the Project and replace it with Work that is not defective.
- (e) When correcting defective Work, Contractor shall take no action that would void or otherwise impair PWC's special warranty and guarantee, if any, on said Work.
- (f) In addition to its correction, removal, and replacement obligations with respect to defective Work, Contractor shall pay all claims, costs, losses, and damages arising out of or relating to defective Work, including but not limited to the cost of the inspection, testing, correction, removal, replacement, or reconstruction of such defective Work, fines levied against PWC by governmental authorities because the Work is defective, and the costs of repair or replacement of work of others resulting from defective Work. Prior to final payment, if PWC and Contractor are unable to agree as to the measure of such claims, costs, losses, and damages resulting from defective Work, then PWC may impose a reasonable set-off against payments due.

Section 10.04 <u>Acceptance of Defective Work</u>

- (a) If, instead of requiring correction or removal and replacement of defective Work, PWC prefers to accept it, PWC may do so (subject, if such acceptance occurs prior to final payment, to Design Engineer's confirmation that such acceptance is in general accord with the design intent and applicable engineering principles and will not endanger public safety).
- (b) Contractor shall pay all claims, costs, losses, and damages attributable to PWC's evaluation of and determination to accept such defective Work (such costs to be approved by PWC as to reasonableness), and for the diminished value of the Work to the extent not otherwise paid by Contractor. If any such acceptance occurs prior to final payment, the necessary revisions in the Contract Documents with respect to the Work shall be incorporated in a Change Order.
- (c) If the parties are unable to agree as to the decrease in the Contract Price, reflecting the diminished value of Work so accepted, then PWC may impose a reasonable set-off against payments due. If the acceptance of defective Work occurs after final payment, Contractor shall pay an appropriate amount to PWC.

Section 10.05 <u>Uncovering Work</u>

- (a) PWC has discretion to require, at its initial cost, additional inspection or testing of the Work, whether or not the Work is fabricated, installed, or completed.
- (b) If any Work is covered contrary to the written request of PWC, then Contractor shall, if requested by PWC or its designee, uncover such Work for observation, and then replace

the covering, all at Contractor's expense.

- (c) If PWC considers it necessary or advisable that covered Work be observed by PWC or inspected or tested by others, then Contractor, at PWC's request, shall uncover, expose, or otherwise make available for observation, inspection, or testing as PWC may require, that portion of the Work in question, and provide all necessary labor, material, and equipment.
 - (i) If it is found that the uncovered Work is defective, Contractor shall be responsible for all claims, costs, losses, and damages arising out of or relating to such uncovering, exposure, observation, inspection, and testing, and of satisfactory replacement or reconstruction (including but not limited to all costs of repair or replacement of work of others); and pending Contractor's full discharge of this responsibility PWC shall be entitled to impose a reasonable set-off against payments due.
 - (ii) If the uncovered Work is not found to be defective, Contractor shall be allowed an increase in the Contract Price or an extension of the Contract Times, or both, directly attributable to such uncovering, exposure, observation, inspection, testing, replacement, and reconstruction. If the parties are unable to agree as to the amount or extent thereof, then Contractor may submit a Change Proposal within 30 calendar days of the determination that the Work is not defective.

Section 10.06 PWC May Stop the Work

(a) If the Work is defective, or Contractor fails to supply sufficiently skilled workers or suitable materials or equipment, or fails to perform the Work in such a way that the completed Work will conform to the Contract Documents, then PWC may order Contractor to stop the Work, or any portion thereof, until the cause for such order has been eliminated; however, this right of PWC to stop the Work shall not give rise to any duty on the part of PWC to exercise this right for the benefit of Contractor, any Subcontractor, any Supplier, any other individual or entity, or any surety for, or employee or agent of any of them.

Section 10.07 PWC May Correct Defective Work

- (a) If Contractor fails within the time specified by PWC in a written notice from PWC to correct defective Work, or to remove and replace rejected Work as required by PWC, or if Contractor fails to perform the Work in accordance with the Contract Documents, or if Contractor fails to comply with any other provision of the Contract Documents, then PWC may, after seven (7) calendar days written notice to Contractor, correct or remedy any such deficiency.
- (b) In exercising the rights and remedies under this Section, PWC shall proceed expeditiously. In connection with such corrective or remedial action, PWC may exclude Contractor from all or part of the Site, take possession of all or part of the Work and suspend Contractor's services related thereto, and incorporate in the Work all materials and equipment stored at the Site or for which PWC has paid Contractor but which are stored elsewhere. Contractor shall allow PWC and its officers, employees, representatives, agents and other contractors, and Design Engineer and its employees and agents access to the Site to enable PWC to exercise the rights and remedies under this Section.
- (c) All claims, costs, losses, and damages incurred or sustained by PWC in exercising the rights and remedies under this Section will be charged against Contractor as set-offs against payments due. Such claims, costs, losses and damages will include but not be limited to all costs of repair, or replacement of work of others destroyed or damaged by

- correction, removal, or replacement of Contractor's defective Work.
- (d) Contractor shall not be allowed an extension of the Contract Times because of any delay in the performance of the Work attributable to the exercise by PWC of PWC's rights and remedies under this Section.

Article XI. Claims

Section 11.01 Claims Process

- (a) The following disputes between PWC and Contractor shall be submitted to the Claims process set forth in this Article:
 - (i) Appeals by PWC or Contractor of Design Engineer's decisions regarding Change Proposals:
 - (ii) PWC or Contractor's demands for adjustments in the Contract Price or Contract Times, or other relief under the Contract Documents; and
 - (iii) Disputes that Design Engineer has been unable to address because they do not involve the design (as set forth in the Contract Documents), the acceptability of the Work, or other engineering or technical matters.

Section 11.02 Submittal of Claim

(a) The party submitting a claim shall deliver it directly to the other party to the Agreement promptly (but in no event later than 30 calendar days) after the start of the event giving rise thereto; in the case of appeals regarding Change Proposals within 30 calendar days of the decision under appeal. The responsibility to substantiate a claim shall rest with the party making the claim. In the case of a claim by Contractor seeking an increase in the Contract Times or Contract Price, or both, Contractor shall certify that the claim is made in good faith, that the supporting data are accurate and complete, and that to the best of Contractor's knowledge and belief the amount of time or money requested accurately reflects the full amount to which Contractor is entitled.

Section 11.03 Review and Resolution

(a) The party receiving a Claim shall review it thoroughly, giving full consideration to its merits. The two parties shall seek to resolve the Claim through the exchange of information and direct negotiations. The parties may extend the time for resolving the Claim by mutual agreement. All actions taken on a Claim shall be stated in writing and submitted to the other party.

Section 11.04 Dispute Resolution

(a) In the event of any dispute, controversy, or claim of any kindor nature arising under or in connection with this Agreement (a "Dispute") and involving any two or more of the following parties, PWC, Design Engineer, Contractor or any subcontractor of Contractor, the party initiating the Dispute shall serve written notice of a Dispute on the party(ies) to the dispute, and those parties shall endeavor to settle the dispute first through direct, informal discussions between the parties' selected representatives. Any such representative(s) shall have binding authority to settle the Dispute. In the event the parties do not settle the Dispute within ten (10) calendar days from the date of written notice of the Dispute, any

party to the Dispute may, by written notice to the other party(ies), engage a mediator certified under the laws of the State of North Carolina to mediate the Dispute within thirty (30) calendar days of such notice. The parties to the Dispute shall attend mediation in good faith. In the event mediation is unsuccessful, any party to the dispute may initiate arbitration proceedings. Any controversy or claim arising out of or relating to the Contract Documents, or the breach thereof, shall be settled by binding arbitration administered by the American Arbitration Association under its Construction Industry Arbitration Rules, and judgment on the award rendered by the arbitrator(s) may be entered in any court having jurisdiction thereof. All of the foregoing dispute resolution procedures shall be held in Cumberland County, North Carolina. The costs of the mediator and arbitrator in a dispute resolution process shall be divided equally among the parties to the process; provided, however, PWC shall bear at least one-third of the cost if PWC is a party to the dispute resolution and the remainder of the cost shall be divided equally among the other parties participating in the dispute resolution. PWC shall, in its contractual arrangements with Design Engineer, and Contractor shall, in its contracts with Subcontractors and they in their contracts with lower-tier subcontractors authorize and direct such parties to participate in the dispute resolution procedures set forth in this Section. Unless otherwise directed in writing by PWC, Contractor shall continue the Project and maintain compliance with the scheduling deadlines set forth in the Contract Documents during any dispute resolution proceedings. If Contractor continues to perform, PWC shall make payments due for the continued performance in accordance with this Agreement. The provisions of this Section shall not extend any applicable statutes of limitation or repose.

Article XII. Payments to Contractor; Set-Offs; Completion; Correction Period

Section 12.01 <u>Progress Payments</u>

- (a) The Schedule of Values will serve as the basis for progress payments and will be incorporated into a form of Application for Payment acceptable to the Project Engineer. Progress payments on account of Unit Price Work will be based on the number of units completed during the pay period. Progress payments for cost-based Work will be based on the Cost of the Work completed by the Contractor during the pay period.
- (b) Applications for Payments:
 - (i) Contractor shall submit to Project Engineer for review an Application for Payment filled out and signed by Contractor covering the Work completed as of the date of the Application and accompanied by such supporting documentation as is required by the Contract Documents. If payment is requested on the basis of materials and equipment not incorporated in the Work but delivered and suitably stored at the Site or another location agreed to in writing, the Application for Payment shall also be accompanied by a bill of sale, invoice, or other documentation warranting that PWC has received the materials and equipment free and clear, and evidence that the materials and equipment are covered by appropriate property insurance, a warehouse bond, or other arrangements to protect PWC's interest.
 - (ii) Beginning with the second Application for Payment, each Application shall include an affidavit of Contractor stating that all previous progress payments received on account of the Work have been applied on account to discharge Contractor's legitimate obligations associated with prior Applications for Payment.
 - (iii) The amount of retainage for progress payments will be as stipulated in the Contract

Documents.

(c) Review of Applications:

- (i) Project Engineer will, within ten (10) Business Days after receipt of each Application for Payment, including each resubmittal, either indicate in writing a recommendation of payment and present the Application to PWC, or return the Application to Contractor indicating in writing Project Engineer's reason(s) for refusing to recommend payment. In the latter case, the Contractor may make the necessary corrections and resubmit the Application.
- (ii) Project Engineer's recommendation of any payment requested in an Application for Payment will constitute a representation by Project Engineer to PWC, based on Project Engineer's observations of the executed Work, and on Project Engineer's review of the Application for Payment and the accompanying data and schedules, that to the best of Project Engineer's knowledge, information, and belief:
- 1) the Work has progressed to the point indicated;
- 2) the quality of the Work is generally in accordance with the Contract Documents (subject to an evaluation of the Work as a functioning whole prior to or upon Substantial Completion, the results of any subsequent tests called for in the Contract Documents, a final determination of quantities and classifications for Unit Price Work, and any other qualifications stated in the recommendation); and
- 3) the conditions precedent to Contractor's being entitled to such payment appear to have been fulfilled in so far as it is Project Engineer's responsibility to observe the Work.
- (iii) By recommending any such payment Project Engineer will not thereby be deemed to have represented that:
 - inspections made to check the quality or the quantity of the Work as it has been performed have been exhaustive, extended to every aspect of the Work in progress, or involved detailed inspections of the Work beyond the responsibilities specifically assigned to Project Engineer in the Contract Documents; or
 - 2) there may not be other matters or issues between the parties that might entitle Contractor to be paid additionally by PWC or entitle PWC to withhold payment to Contractor.
- (iv) Neither Project Engineer's review of Contractor's Work for the purposes of recommending payments nor Project Engineer's recommendation of any payment, including final payment, will impose responsibility on Project Engineer:
 - 1) to supervise, direct, or control the Work, or
 - 2) for the means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or
 - 3) for Contractor's failure to comply with Laws and Regulations applicable to Contractor's performance of the Work, or
 - 4) to make any examination to ascertain how or for what purposes Contractor has used the money paid on account of the Contract Price.
- (v) Project Engineer may refuse to recommend the whole or any part of any payment if, in Project Engineer's opinion, it would be incorrect to make the representations to PWC outlined in this Section.

- (d) Project Engineer will recommend reductions in payment (set-offs) necessary in Project Engineer's opinion to protect PWC from loss because:
 - (i) the Work is defective, requiring correction or replacement;
 - (ii) the Contract Price has been reduced by Change Orders;
 - (iii) PWC has been required to correct defective Work or has accepted defective Work in accordance with these General Conditions;
 - (iv) PWC has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible; or
 - (v) Project Engineer has actual knowledge of the occurrence of any of the events that would constitute a default by Contractor and therefore justify termination for cause under the Contract Documents.

(e) Payment Becomes Due:

(i) Twenty (20) Business Days after presentation of the Application for Payment to PWC with Project Engineer's recommendation, the amount recommended (subject to any PWC set offs) will become due, and when due will be paid by PWC to Contractor.

(f) Reductions in Payment by PWC:

- (i) In addition to any reductions in payment (set-offs) recommended by Project Engineer, PWC is entitled to impose a set-off against payment based on any of the following:
- PWC has incurred costs, losses, or damages on account of Contractor's conduct in the performance or furnishing of the Work, including but not limited to claims, costs, losses, or damages from workplace injuries, adjacent property damage, non-compliance with Laws and Regulations, and patent infringement;
- 2) Contractor has failed to take reasonable and customary measures to avoid damage, delay, disruption, and interference with other work at or adjacent to the Site;
- 3) Contractor has failed to provide and maintain required bonds or insurance;
- 4) PWC has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible;
- 5) PWC has incurred extra charges or engineering costs related to submittal reviews, evaluations of proposed substitutes, tests and inspections, or return visits to manufacturing or assembly facilities;
- 6) the Work is defective, requiring correction or replacement;
- 7) PWC has been required to correct defective Work or has accepted defective Work in accordance with the Contract Documents:
- 8) the Contract Price has been reduced by Change Orders;
- 9) an event that would constitute a default by Contractor and therefore justify a termination for cause has occurred;
- 10) liquidated damages have accrued as a result of Contractor's failure to achieve Milestones, Substantial Completion, or Completion of the Project; or
- 11) there are other items entitling PWC to a set off against the amount recommended.
- (ii) If PWC imposes any set-off against payment, whether based on its own knowledge or on the written recommendations of Project Engineer, PWC will give Contractor immediate written notice stating the reasons for such action and the specific amount of the reduction, and promptly pay Contractor any amount remaining after deduction of the amount so withheld. PWC shall promptly pay Contractor the amount so withheld, or any adjustment agreed to by PWC and Contractor if Contractor remedies the reasons for

- such action. The reduction imposed shall be binding on Contractor unless it duly submits a Change Proposal contesting the reduction.
- (iii) Upon a subsequent determination that PWC's refusal of payment was not justified, the amount wrongfully withheld shall be treated as an amount due and subject to interest as provided in the Contract Documents.

Section 12.02 Substantial Completion

- (a) When Contractor considers the entire Work ready for its intended use Contractor shall notify PWC and Design Engineer in writing that the entire Work is substantially complete and request that PWC acknowledge in writing that Contractor has met Substantial Completion.
- (b) Promptly after Contractor's notification, PWC, Contractor, and Design Engineer shall make an inspection of the Work to determine the status of completion. If PWC does not consider the Work substantially complete, PWC will notify Contractor in writing giving the reasons therefor. PWC shall thereafter submit to Contractor an initial draft of punch list items to be completed or corrected before final payment.
- (c) If Design Engineer considers the Work substantially complete, Design Engineer will deliver to PWC a preliminary certificate of Substantial Completion which shall fix the date of Substantial Completion. Design Engineer shall attach to the certificate a punch list of items to be completed or corrected before final payment. PWC shall have seven (7) Business Days after receipt of the preliminary certificate to make written objection to Design Engineer as to any provisions of the certificate or attached punch list. If, after considering the objections to the provisions of the preliminary certificate, PWC concludes that the Work is not substantially complete, PWC will, within fourteen (14) calendar days after submission of the preliminary certificate to PWC, notify Contractor in writing that the Work is not substantially complete, stating the reasons therefor.
- (d) At the time of receipt of the preliminary certificate of Substantial Completion, PWC and Contractor will confer regarding PWC's use or occupancy of the Work following Substantial Completion, review the builder's risk insurance policy with respect to the end of the builder's risk coverage, and confirm the transition to coverage of the Work under a permanent property insurance policy held by PWC. Unless PWC and Contractor agree otherwise in writing, PWC shall bear responsibility for security, operation, protection of the Work, property insurance, maintenance, heat, and utilities upon PWC use or occupancy of the Work.
- (e) After Substantial Completion the Contractor shall promptly begin work on the punch list of items to be completed or corrected prior to final payment and shall complete such items within the time specified by PWC. In appropriate cases Contractor may submit monthly Applications for Payment for completed punch list items, following the progress payment procedures set forth above.
- (f) PWC shall have the right to exclude Contractor from the Site after the date of Substantial Completion subject to allowing Contractor reasonable access to remove its property and complete or correct items on the punch list.

Section 12.03 Partial Use or Occupancy

- (a) Prior to Substantial Completion of all the Work, PWC may use or occupy any substantially completed part of the Work which has specifically been identified in the Contract Documents, or which PWC, Design Engineer, and Contractor agree constitutes a separately functioning and usable part of the Work that can be used by PWC for its intended purpose without significant interference with Contractor's performance of the remainder of the Work, subject to the following conditions:
 - (i) At any time PWC may request in writing that Contractor permit PWC to use or occupy any such part of the Work that PWC believes to be substantially complete.
 - (ii) At any time Contractor may notify PWC and Design Engineer in writing that Contractor considers any such part of the Work substantially complete and request Design Engineer to issue a certificate of Substantial Completion for that part of the Work.
 - (iii) Within a reasonable time after either such request, PWC, Contractor, and Design Engineer shall make an inspection of that part of the Work to determine its status of completion. If Design Engineer does not consider that part of the Work to be substantially complete, Design Engineer will notify PWC and Contractor in writing giving the reasons therefor.
- (iv) No use or occupancy or separate operation of part of the Work may occur prior to compliance with the requirements regarding builder's risk or other property insurance.

Section 12.04 Final Inspection

(a) Upon written notice from Contractor that Completion of the Project has been achieved or an agreed portion thereof is complete, PWC will promptly make a final inspection with Project Engineer, Design Engineer, and Contractor and will notify Contractor in writing of all particulars in which this inspection reveals that the Work, or agreed portion thereof, is incomplete or defective. Contractor shall immediately take such measures as are necessary to complete such Work or remedy such deficiencies.

Section 12.05 Final Payment

- (a) Application for Payment:
 - (i) After Contractor has, in the opinion of PWC, satisfactorily completed all corrections identified during the final inspection and has delivered, in accordance with the Contract Documents, all maintenance and operating instructions, schedules, guarantees, bonds, certificates or other evidence of insurance, certificates of inspection, annotated record documents, and other documents, Contractor may make application for final payment.
 - (ii) The final Application for Payment shall be accompanied (except as previously delivered) by:
 - 1) all documentation called for in the Contract Documents;
 - 2) consent of the surety, if any, to final payment;
 - 3) satisfactory evidence that all title issues have been resolved such that title to all Work, materials, and equipment has passed to PWC free and clear or will so pass upon final payment:
 - 4) a list of all disputes that Contractor believes are unsettled; anD
 - 5) complete and legally effective releases or waivers (satisfactory to PWC) required by the Contract Documents.

- (iii) If Design Engineer is satisfied that the Work has been completed and Contractor's other obligations under the Contract have been fulfilled, Design Engineer will, within ten (10) Business Days after receipt of the final Application for Payment, indicate in writing Design Engineer's recommendation of final payment and present the Application for Payment to PWC for payment. Such recommendation shall account for any set-offs against payment that are necessary in Design Engineer's opinion to protect PWC from loss for the reasons stated above with respect to progress payments. At the same time Design Engineer will also give written notice to PWC and Contractor that the Work is acceptable and that Completion of the Project has been achieved. Otherwise, Design Engineer will return the Application for Payment to Contractor, indicating in writing the reasons for refusing to recommend final payment, in which case Contractor shall make the necessary corrections and resubmit the Application for Payment.
- (iv) Within thirty (30) calendar days after the presentation to PWC of the final Application for Payment and accompanying documentation, the amount recommended by Design Engineer (less any further sum PWC is entitled to set off against Design Engineer's recommendation, including but not limited to set-offs for liquidated damages and set-offs allowed under the provisions above with respect to progress payments) will become due and shall be paid by PWC to Contractor.

Section 12.06 Waiver of Claims

- (a) The making of final payment will not constitute a waiver by PWC of claims or rights against Contractor. PWC expressly reserves claims and rights arising from defective Work appearing after final inspection, from Contractor's failure to comply with the Contract Documents or the terms of any special guarantees specified therein, from Contractor's indemnification obligations, or from Contractor's continuing obligations under the Contract Documents.
- (b) The acceptance of final payment by Contractor will constitute a waiver by Contractor of all claims and rights against PWC other than those pending matters that have been duly submitted or appealed under the provisions of the Contract Documents.

Section 12.07 <u>Correction Period</u>

- (a) If within one (1) year after the date of Substantial Completion (or such longer period of time as may be prescribed by the terms of any applicable special guarantee required by the Contract Documents, or by any specific provision of the Contract Documents), any Work is found to be defective, or if the repair of any damages to the Site, adjacent areas that Contractor has arranged to use through construction easements or otherwise, and other adjacent areas used by Contractor as permitted by Laws and Regulations, is found to be defective, then Contractor shall promptly, without cost to PWC and in accordance with PWC's written instructions:
 - (i) correct the defective repairs to the Site or such other adjacent areas;
 - (ii) correct such defective Work;
 - (iii) if the defective Work has been rejected by PWC, remove it from the Project and replace it with Work that is not defective, and
 - (iv) satisfactorily correct or repair or remove and replace any damage to other Work, to the work of others, or to other land or areas resulting therefrom.
- (b) If Contractor does not promptly comply with the terms of PWC's written instructions, or in an emergency where delay would cause serious risk of loss or damage, PWC may have

the defective Work corrected or repaired or may have the rejected Work removed and replaced. Contractor shall pay all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such correction or repair or such removal and replacement (including but not limited to all costs of repair or replacement of work of others).

- (c) In special circumstances where a particular item of equipment is placed in continuous service before Substantial Completion of all the Work, the correction period for that item may start to run from an earlier date only as provided in the Contract Documents.
- (d) Where defective Work (and damage to other Work resulting therefrom) has been corrected or removed and replaced under this Article XII, the correction period hereunder with respect to such Work will be extended for an additional period of one year after such correction or removal and replacement has been satisfactorily completed.
- (e) Contractor's obligations under this Article XII are in addition to all other obligations and warranties. The provisions of this Article XII shall not be construed as a substitute for, or a waiver of, the provisions of any applicable statute of limitation or repose.

Article XIII. Suspension of Work and Termination

Section 13.01 PWC May Suspend Work

(a) At any time and without cause, PWC may suspend the Work or any portion thereof for a period of not more than 90 consecutive calendar days by written notice to Contractor and Design Engineer. Such notice will fix the date on which Work will be resumed. Contractor shall resume the Work on the date so fixed. Contractor shall be entitled to an adjustment in the Contract Price or an extension of the Contract Times, or both, directly attributable to any such suspension. Any Change Proposal seeking such adjustments shall be submitted no later than thirty (30) calendar days after the date fixed for resumption of Work.

Section 13.02 <u>PWC May Terminate for Cause</u>

- (a) The occurrence of any one or more of the following events will constitute a default by Contractor and justify termination for cause:
 - (i) Contractor's continued failure to perform the Work in accordance with the Contract Documents (including, but not limited to, failure to supply sufficient skilled workers or suitable materials or equipment or failure to adhere to the Progress Schedule);
 - (ii) Failure of Contractor to perform or otherwise to comply with a material term of the Contract Documents;
 - (iii) Contractor's disregard of Laws or Regulations of any public body having jurisdiction; or
 - (iv) Contractor's repeated disregard of the authority of PWC, Project Engineer, or Design Engineer.
- (b) If one or more of the events identified in Paragraph 13.02(a) occurs, then after giving Contractor (and any surety) ten (10) calendar days written notice that PWC is considering a declaration that Contractor is in default and termination of the Agreement, PWC may proceed to:
 - (i) declare Contractor to be in default, and give Contractor (and any surety) notice that the

General Conditions (Rev 7/2023)

- Contract is terminated; and
- (ii) enforce the rights available to PWC under any applicable performance bond.
- (c) Subject to the terms and operation of any applicable performance bond, if PWC has terminated the Contract for cause, PWC may exclude Contractor from the Site, take possession of the Work, incorporate in the Work all materials and equipment stored at the Site or for which PWC has paid Contractor but which are stored elsewhere, and complete the Work as PWC may deem expedient.
- (d) PWC may not proceed with termination of the Contract under Paragraph 13.02(b) if Contractor within seven (7) calendar days of receipt of notice of intent to terminate begins to correct its failure to perform and proceeds diligently to cure such failure and such efforts are agreed to by PWC.
- (e) If PWC proceeds as provided in Paragraph 13.02(b), Contractor shall not be entitled to receive any further payment until the Work is completed. If the unpaid balance of the Contract Price exceeds the cost to complete the Work, including all related claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals) sustained by PWC, such excess will be paid to Contractor. If the cost to complete the Work including such related claims, costs, losses, and damages exceeds such unpaid balance, Contractor shall pay the difference to PWC. Such claims, costs, losses, and damages incurred by PWC will be reviewed by PWC as to their reasonableness and, when so approved by PWC, incorporated in a Change Order.
- (f) Where Contractor's services have been so terminated by PWC, the termination will not affect any rights or remedies of PWC against Contractor then existing or which may thereafter accrue, or any rights or remedies of PWC against Contractor or any surety under any payment bond or performance bond. Any retention or payment of money due Contractor by PWC will not release Contractor from liability.
- (g) The provisions of any applicable payment or performance bond shall govern over any inconsistent provisions of this Section.

Section 13.03 PWC May Terminate For Convenience

- (a) Upon seven (7) calendar days written notice to Contractor, PWC may, without cause and without prejudice to any other right or remedy of PWC, terminate the Contract. In such case, Contractor shall be paid for (without duplication of any items):
 - (i) completed and acceptable Work executed in accordance with the Contract Documents prior to the effective date of termination, including fair and reasonable sums for overhead and profit on such Work;
 - (ii) expenses sustained prior to the effective date of termination in performing services and furnishing labor, materials, or equipment as required by the Contract Documents in connection with uncompleted Work, plus fair and reasonable sums for overhead and profit on such expenses; and
 - (iii) other reasonable expenses directly attributable to termination, including costs incurred to prepare a termination for convenience cost proposal.
- (b) Contractor shall not be paid on account of loss of anticipated overhead, profits, or revenue, or other economic loss arising out of or resulting from such termination.

Section 13.04 Contractor May Stop Work or Terminate

- (a) If, through no act or fault of Contractor, (1) the Work is suspended for more than ninety (90) consecutive calendar days by PWC or under an order of court or other public authority or (2) PWC fails for sixty (60) calendar days to pay Contractor any sum finally determined to be due, then Contractor may, upon seven (7) calendar days written notice to PWC, and provided PWC does not remedy such suspension or failure within that time, terminate the Contract and recover from PWC payment on the same terms as provided in this Article.
- (b) In lieu of terminating the Contract and without prejudice to any other right or remedy, if PWC has failed for thirty (30) calendar days to pay Contractor any sum finally determined to be due, Contractor may, seven (7) calendar days after written notice to PWC, stop the Work until payment is made of all such amounts due Contractor, including interest thereon. The provisions of this paragraph are not intended to preclude Contractor from submitting a Change Proposal for an adjustment in Contract Price or Contract Times or otherwise for expenses or damage directly attributable to Contractor's stopping the Work as permitted by this paragraph.

Section 13.05 Morality

(a) If, in the sole opinion of PWC, at any time Contractor or any of its owner(s) or employee(s) or agent(s) (each party, owner, employee, and agent is an "Actor") engages in any one or more actions that bring disrepute, contempt, scandal, or public ridicule to the Actor or subject the Actor to prosecution or offend the community or public morals or decency or denigrate individuals or groups in the community served by PWC or are scandalous or inconsistent with community standards or good citizenship or may adversely affect PWC's finances, public standing, image, or reputation or are embarrassing or offensive to PWC or may reflect unfavorably on PWC or are derogatory or offensive to one or more employee(s) or customer(s) of PWC, PWC may immediately upon written notice to Contractor terminate the Agreement, in addition to any other rights and remedies that PWC may have pursuant to the Contract Documents or at law or in equity.

Article XIV. Miscellaneous

Section 14.01 <u>Additional General Terms and Conditions</u>

(a) Contractor shall be subject to any additional terms and conditions for this Project as set forth in the applicable Appendices as specific in the Agreement, which is incorporated by reference as if set forth word-for-word herein.

Section 14.02 Giving Notice

- (a) Whenever any provision of the Contract Documents requires the giving of written notice, it will be deemed to have been validly given if:
 - (i) delivered in person, by a commercial courier service or otherwise, to the individual or to a member of the firm or to an officer of the corporation for which it is intended;
 - (ii) delivered at or sent by registered or certified mail, postage prepaid, to the last business address known to the sender of the notice; or
 - (iii) sent to PWC or Contractor's designee(s) via email, with a confirmation of receipt.

Section 14.03 <u>Computation of Times</u>

(a) When any period of time is referred to in the Contract by days, it will be computed to exclude the first and include the last day of such period. If the last day of any such period falls on a Saturday or Sunday or on a day made a legal holiday by the law of the applicable jurisdiction, such day will be omitted from the computation.

Section 14.04 <u>Cumulative Remedies</u>

(a) The duties and obligations imposed by these General Conditions and the rights and remedies available hereunder to the parties are in addition to, and are not to be construed in any way as a limitation of, any rights and remedies available to any or all of them which are otherwise imposed or available by Laws or Regulations, by special warranty or guarantee, or by other provisions of the Contract Documents. The provisions of this paragraph will be as effective as if repeated specifically in the Contract Documents in connection with each particular duty, obligation, right, and remedy to which they apply.

Section 14.05 Limitation of Damages

(a) With respect to any and all Change Proposals, Claims, disputes subject to final resolution, and other matters at issue, neither PWC nor Design Engineer, nor any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, shall be liable to Contractor for any claims, costs, losses, or damages sustained by Contractor on or in connection with any other project or anticipated project.

Section 14.06 No Waiver

(a) A party's non-enforcement of any provision shall not constitute a waiver of that provision, nor shall it affect the enforceability of that provision or any other provision of the Contract Documents.

Section 14.07 Survival of Obligations

(a) All representations, indemnifications, warranties, and guarantees made in, required by, or given in accordance with the Contract Documents, as well as all continuing obligations indicated in the Contract Documents, will survive final payment, completion, and acceptance of the Work or termination or completion of the Agreement or termination of the services of Contractor.

Section 14.08 Controlling Law

(a) The Agreement shall be governed by the law of the State of North Carolina.

Section 14.09 Headings

(a) Article and paragraph headings, numbers, and letters are inserted for convenience only and do not constitute parts of these General Conditions.

01000 - SUPPLEMENTARY CONDITIONS

PAYMENTS AND FINAL COMPLETION

A. STORED MATERIALS

The option to incorporate stored materials shall be addressed prior to the first pay estimate. The Contractor will not be permitted to request payment for stored materials on future pay applications once the first application has been signed by the Contractor and submitted to the Owner. If considered for payment, stored materials shall be delivered and stored to the satisfaction of the Project Coordinator. Stored material estimates must be submitted in a form acceptable to the Project Engineer. All invoices shall accompany the pay estimates and be separated by the associated project "Part" (i.e. Part A, Part B, etc.). Stored materials shall be paid for according to eighty-five percent (85%) of the actual invoice value including sales tax.

B. PAY ESTIMATES/PAY APPLICATIONS

All pay estimates will be generated by the Owner. The Contractor and the Project Coordinator will review quantities and mutually agree on the monthly quantities for payment. The monthly progress status report shall be signed by the Contractor and the Project Coordinator. Payment shall be based on those quantities installed and accepted as of the last Friday of the month. The Project Engineer will generate the pay application based on the quantities submitted and forward electronically the pay application to the Contractor to be returned with original signatures. The Contractor shall return all two (2) pay applications with sales tax certification and invoices, stored material documentation, certified payrolls for the period and Affidavit E. Pay requests will not be processed if any of the required documents have not been submitted.

C. PAYMENTS WITHHELD

The Project Engineer may refuse to approve the whole or any part of any payment. The Project Engineer may refuse to approve payment if evidence is discovered, or the results of subsequent inspection or tests, nullify any such payment previously approved. The Project Engineer reserves the right to withhold payment or any portion of a payment throughout the course of the project in the event the following, including but not limited to, occurs:

- 1. Slippage in the schedule in excess of two (2) or more weeks.
- 2. Liens or claims filed against the Contractor.
- 3. Persistent failure to carry out the work in accordance with the Contract Documents.
- 4. Claims from residents or businesses not addressed or resolved within thirty (30) days.
- 5. Defective work not corrected, tested, or completed following damage, correction or replacement.
- 6. Reasonable evidence that the Work cannot be completed for the unpaid balance of the Contract.
- 7. Reasonable evidence that the Work will not be completed within the Contract time and that the unpaid balance would not be adequate to cover actual or liquidated damages for the anticipated delay.
- 8. Damage to the Owner's property, Property Owner, or another Contractor.
- 9. The Contract price has been reduced because of modifications.
- 10. Any required documentation has not been submitted as requested.

The amounts withheld will be at the sole discretion of the Project Engineer. When the grounds for withholding payments have been removed, payment will be released. The Project Engineer is not liable and will not accept claims from the Contractor resulting from payments being withheld.

D. CHANGE ORDERS

The Owner may authorize changes to the Work. These changes shall not invalidate, relieve, or release the Contractor from any guarantee given by him pertinent to the Contract provisions. These changes shall not affect the validity of the Payment Bond and Performance Bond nor relieve the Surety or Sureties of said Bonds. The Contractor shall notify their Bonding Company of all changes to the Contract. All changes to the Work shall be performed under the terms of the original Contract, unless otherwise specified in the approved Change Order.

Except in an emergency endangering life or property, no changes shall be made to the Contract without written notice from the Project Engineer authorizing such change. No claim for adjustments of the contract price shall be valid without such written authorization.

E. EXTENSION OF CONTRACT TIME

The Contract Time may be extended by change order for causes beyond the Contractor's control or for delays which the Project Engineer determines to be justified. Extensions to the Contract time shall be granted solely in calendar days. If, at the end of the Contract, the final completion date falls on a non-work day, the Project Engineer may, at their sole discretion grant additional calendar days so that the final completion date is the following work day.

Request for time extensions shall be made in writing within thirty (30) calendar days following the cause of delay. In cases of continuing cause for delay, only one claim is necessary. Failure to make written requests within the allowed time frame shall waive the Contractor's ability to make future claims for that specific instance.

Time can only be extended for the following:

- Change in Work Delays

Additional calendar days may be granted by the Project Engineer, for work assigned to the Contractor; through a change order, provided that the Contractors critical path is impacted by the change in work. The additional time shall be based on the actual number of calendar days that the critical path (i.e. controlling operation) is delayed. The Project Engineer may extend the contract duration based on estimated calendar days to complete the additional work that does not impact the critical path.

Weather Delays

The initial contract duration does not include weather days. Weather delays are defined as any event that affects the standard daily production for 50% or more of the Contractor's scheduled work day. Weather days shall be based on the actual precipitation received (i.e., inches of rain), the time the precipitation occurred, and the Project Coordinator's observations. Weather days shall not be granted for weather that occurs during non-working hours, including weekends and/or holidays, unless it affects the Contractor's standard daily production for 50% or more of the following working days. If it is confirmed that the weather has affected production on the project, the Project Engineer will issue a

modification of the contract time in full calendar days. Weather days shall be approved or disapproved by the Project Engineer based upon review of the project daily records.

Throughout the Contract, the Contractor shall record the occurrence of weather and the resulting impact to the scheduled work. It is the Contractor's responsibility to request additional time for weather delays in accordance with these Contract Documents. Requests for time extensions for weather delays do not entitle the Contractor to extend overhead.

PERFORMANCE BOND

| Date of Execution: | |
|--|---|
| Name of Principal: (Contractor) | |
| Name of Surety: | |
| Name of Contracting Body: | Fayetteville Public Works Commission, Fayetteville, N.C. |
| Amount of Bond: | |
| PROJECT: FAYET AREA 27 – CLIFFDA | TEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION LE FOREST |
| held and firmly bound Contracting Body, in t and truly to be made, | THESE PRESENTS, That We, the Principal and Surety above named, are unto the above named Contracting Body, hereinafter called the he penal sum of the amount stated above the payment of which sum well we bind ourselves, our heirs, executors, administrators, and successors, irmly by these present. |
| | THIS OBLIGATION IS SUCH that whereas the Principal entered into a he Contracting Body, identified as shown above and hereto attached. |
| covenants, terms, cor Contract and any exter without notice to the Stand shall also well and conditions, and agree may hereafter be made | if the Principal shall well and truly perform and fulfill all the undertakings, additions, and agreements of said Contract during the original term of said ensions there of that may be granted by the Contracting Body, with or Surety, and during the life of any Guaranty required under the Contract, d truly perform and fulfill all the undertakings, covenants, terms, ments of any and all duly authorized modifications of said Contract that le, notice of which modifications to the Surety being hereby waived, then, bid; otherwise to remain in full force and virtue. |
| several seals on the d | EOF, the above bounded parties have executed this instrument under the late indicated above, the name and corporate seal of each corporate party and these presents duly signed by its undersigned representative, of its governing body. |
| Executed in | counterparts. |

| Witness: | CONTRACTOR: |
|--|--|
| (Proprietorship of Partnership) | (Trade or Corporate Name) |
| By: | By: |
| Title: | Title: |
| (Corporate Secretary or Assistant Secretary, Only) | (Owner, Partner, Corporate President or Vice-President, Only) (CORPORATE SEAL) |
| Witness: | SURETY COMPANY: |
| | (Surety Company Name) |
| | Ву: |
| Countersigned: | Title: |
| (N.C. Licensed Resident Agent) | (Attorney in Fact) (SURETY CORPORATE SEAL) |

PAYMENT BOND

| Date of Execution: | |
|---------------------|--|
| Name of Principal: | |
| (Contractor) | |
| Name of Surety: | |
| Name of Contracting | |
| Body: | Fayetteville Public Works Commission, Fayetteville, N.C. |
| | |
| Amount of Bond: | |

PROJECT: FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

KNOW ALL MEN BY THESE PRESENTS, that We, the PRINCIPAL and Surety above named, are held and firmly bound unto the above named Contracting Body, hereinafter called the Contracting Body, in the penal sum of the amount stated above the payment of which sum well and truly to be made, we bind ourselves, our heirs, executors, administrators, and successors, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION IS SUCH that whereas the Principal entered into a certain Contract with the Contracting Body, identified as shown above and hereto attached.

NOW THEREFORE, if the Principal shall promptly make payment to all persons supplying labor and material in the prosecution of the work provided for in said contract, and any and all duly authorized modifications of said contract that may hereafter be made, notice of which modifications to the Surety being hereby waived, then, this obligation to be void; otherwise to remain in full force and virtue.

IN WITNESS WHEREOF, the above bounded parties have executed this instrument under the several seals on the date indicated above, the name and corporate seal of each corporate party being hereto affixed, and these presents duly signed by its undersigned representative, pursuant to authority of its governing body.

| Executed in | counterparts. |
|---|--|
| Witness: | CONTRACTOR: |
| (Proprietorship of Partnership) | (Trade or Corporate Name) |
| Ву: | Ву: |
| Title: | Title: |
| (Corporate Secretary or Assistant Secretary, Only) | (Owner, Partner, Corporate President or Vice-President, Only) (CORPORATE SEAL) |
| Witness: | SURETY COMPANY: |
| | (Surety Company Name) |
| | Ву: |
| Countersigned: | Title: |
| (N.C. Licensed Resident Agent) | (Attorney in Fact) (SURETY CORPORATE SEAL) |


POWER OF ATTORNEY (ATTACH)


CERTIFICATE(S) OF INSURANCE (Attach)

NOTICE TO PROCEED

| TO: | Date: |
|--|--|
| PROJECT: FAYETTEVILLE ANNEXATION AREA 27 – CLIFFDALE FOREST | PHASE V, PROJECT XII, CONSTRUCTION |
| You are hereby notified to commence work in ac | ecordance with the Contract dated |
| , 20 <u>24,</u> on or befor | e, 20 <u>24,</u> and you are to |
| complete the WORK within the contract period | thereafter. The date of final completion |
| therefore is | |
| | |
| FA | YETTEVILLE PUBLIC WORKS COMMISSION |
| BY: | <u> </u> |
| | Victoria McAllister |
| | Procurement Manager |
| ACCEPTANCE OF NOTICE | |
| Receipt of the above NOTICE TO PROCEED | |
| is hereby acknowledged this theday | of, 20 <u>24</u> . |
| | |
| (CONTRACTOR) | |
| | |
| BY: | |
| TITLE: | |
| END OF | SECTION - |

FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 – CLIFFDALE FOREST

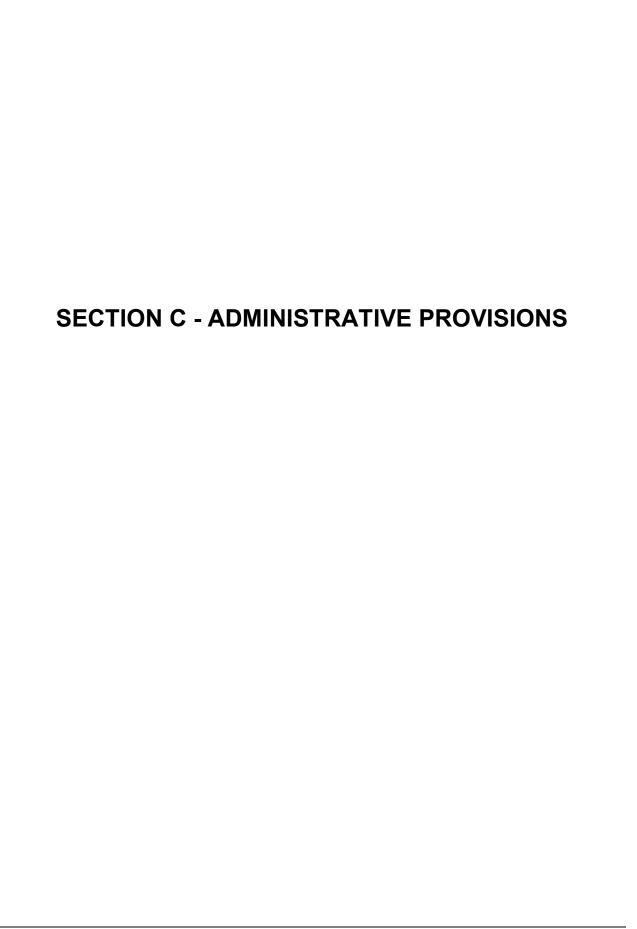

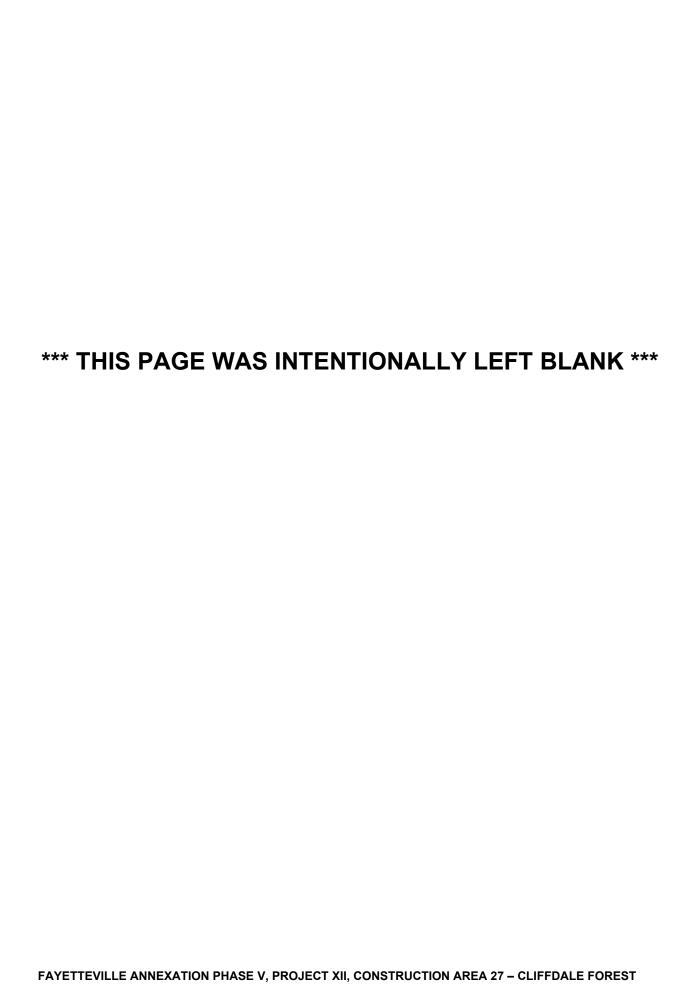

DIVISION I 01025 MEASUREMENT AND PAYMENT

GENERAL

- A. The purpose of this Section is to define the methods of measurement and payment for each of the unit prices and/or lump sum prices listed in the Bid Form, which are required to construct the Work.
- B. The unit price and/or lump sum price bid shall be full compensation for the work required under each bid item, which shall include all incidental costs relative thereto. Certain items of work are specified and/or shown as a detail in the Contract Documents and drawings; bid prices shall include all items of work required to furnish and/or install each in accordance with the Project requirements, whether specifically stated or itemized in the Measure and Payment description.
- C. Certain items of work listed hereinafter may not be required on this project, and shall be denoted as not applicable.
- D. Certain bid items have been designated to conform to maximum payment widths and/or lengths and no additional payment therefore will be allowed unless otherwise approved by the Owner. These designated items will be as identified in the Bid Form, Technical Specifications and as may be indicated on the Contract Drawings. The designation of these items of work shall be noted as "No Overage Allowed" or "NOA". Prospective bidders shall be responsible for verifying that the actual quantities of work are listed in the Bid Form prior to submitting bids, and include all costs (regardless whether the Bid quantities are over or under the quantities indicated on the plans) in the unit price bid.

THE FOLLOWING PAYMENT ITEMS ARE APPLICABLE IN ALL PARTS A, C, & D

G-1 MOBILIZATION AND DEMOBILIZATION

- A. The lump sum prices shown under each PART of the Bid Form are based on a percentage of the Design Engineer's estimate of probable cost. Payment under this item shall include all costs of mobilization, demobilization, bonds and insurance and other related costs.
- B. Fifty percent (50%) of the mobilization items will be paid under the first payment application submitted and the balance under the second payment application submitted.

G-2 TRAFFIC CONTROL & TRAFFIC PLAN

A. The lump sum prices bid under each PART in the Bid Form shall include all costs for the preparation and implementation of required traffic management plans, furnishing, installing and maintaining traffic control signage and devices, relocating or removing signs or other traffic control devices, replacement of street signs, replacement of traffic signal loops, and all other incidental work throughout the project site, throughout the project duration. The Contractor shall coordinate his activities so as to minimize disruption of traffic and inconvenience to residents and the general public. All such traffic control devices, signage, traffic patterns and road closures shall be approved by the City of Fayetteville and/or NCDOT.

- B. Payment under the lump sum prices bid for each part shall be made on a monthly basis based on actual estimated percentage of work completed and maintained as determined by the Project Coordinator or Project Engineer. In no case shall the monthly payment exceed ten (10) percent of the lump sum prices bid without approval by the Project Engineer.
- C. Prospective bidders are advised that failure to provide and maintain adequate traffic control devices and/or signage may result in the Project Engineer's refusal to make payment until corrective measures are in place.
- D. Improper signage and/or traffic control devices will not be allowed. The City of Fayetteville, NCDOT, and/or Fayetteville Public Works Commission reserves the right relocate and/or remove such non-conforming signs and devices, setup proper signage to ensure public safety and deduct all costs for these items which may be incurred by the Owner. The Contractor shall make no claim for such work performed.

G-3 EROSION AND SEDIMENTATION CONTROL

- A. The lump sum prices bid under the applicable PARTs in the Bid Form bid for erosion and sedimentation control shall include all costs for furnishing, erecting, maintaining and removing silt fence, temporary sedimentation control devices, rip-rap, rock check dams, temporary seeding, gravel construction entrances, filter fabric, integral straw, culled wood matting, inlet protection and any other erosion control devices shown or as may be required by the appropriate regulatory agencies throughout the project site, throughout the project duration. No additional payment will be made for removal of soil and debris from drainage structures, features, or reconditioning grading that is part of the normal maintenance activities associated with the approved erosion control plan. No additional payment shall be made for any other work due to inadequate or improperly maintained measures.
- B. Prospective bidders are advised, that erosion and sedimentation control will be strictly enforced, and any failure to conform to required standards is considered a right precedent to the Owner to deny payment. Additional measures required by the North Carolina Department of Environmental and Natural Resources (NCDENR) shall not be cause for change in the lump sum price bid. Bidders shall make themselves aware of all NCDENR regulations and requirements. The Contractor shall be responsible for all fines levied due to improper erosion and sediment control measures to include all costs incurred by City of Fayetteville and/or Fayetteville Public Works Commission necessary to bring a non-conforming site into compliance.
- C. The lump sum price bid shall include all costs necessary for the Contractor to comply with the requirements of the NPDES permit that is associated with the approved erosion control permit. Such activities include, but are not limited to: installation and maintenance of rain gauges, completing the required inspection reports, posting the permit and reports on the project, and furnishing copies of the inspections reports to the Owner.
- D. Payment under the lump sum prices bid for each PART shall be made on a monthly basis as indicated in the Contractor's schedule for the substantial completion of all work under this Contract. In no case, shall the monthly payment exceed ten (10) percent of the lump sum prices bid without the approval of the Owner.

G-4 BORROW EXCAVATION (SELECT BACKFILL)

- A. Borrow excavation (select backfill) shall be paid for at the unit price bid per cubic yard, as contained in the Bid Form. Payment shall constitute full compensation for all material, equipment, labor and all else required for acquisition, placement and compaction of select backfill material from borrow. Borrow excavation material shall be supplied by the Contractor from approved borrow areas located off-site. Materials utilized "on-site" within the Project limits or as defined, as the "free haul limit" will not be considered for payment as borrow excavation.
- B. The cubic yards of select backfill to be paid for shall be 75% of the volume indicated on the submitted truck tickets. Disposal of unsuitable and/or suitable excavated material will not be paid for as a separate bid item. The Owner reserves the right to verify the actual amount of material in place.
- C. Payment under this item shall include all costs necessary to furnish and install select material necessary to provide proper suitable backfill material compacted and in place as measured. Work shall include all costs to acquire, place, and compact select backfill material, removal and proper disposal of unusable material, and all labor, materials, equipment, and incidentals necessary to complete the work. The PWC Project Coordinator shall approve the use of select material within the limits of this project.

G-5 CLEARING AND GRUBBING, PERMANENT EASEMENTS

A. The unit price bid per acre shall include the costs for felling trees, stump removal and disposal off-site, cutting trees in pulpwood length and stacking on or off easement areas if required, disposing of all trimmings, removing and disposing off-site all logs, branches, trunks, root mats, brush, vegetation, debris from clearing and grubbing operations and all other incidental materials not to be re-used in the work. Areas containing and requiring cutting and removal of weeds, grass, grain annual or perennial plants, or saplings less than one inch in diameter shall not be measured and paid for as clearing and grubbing. Payment shall be based on the horizontal area cleared and grubbed as designated on the plans or as directed by the Owner. Measurement will be made to the nearest one hundredth of an acre.

G-6 CLEARING AND GRUBBING, TEMPORARY EASEMENTS

- A. The unit price bid per acre shall include the costs for felling trees, stump removal and disposal off-site, cutting trees in pulpwood length and stacking on or off easement areas if required, disposing of all trimmings, removing and disposing off-site all logs, branches, trunks, root mats, brush, vegetation, debris from clearing and grubbing operations and all other incidental materials not to be re-used in the work. Areas containing and requiring cutting and removal of weeds, grass, grain annual or perennial plants, or saplings less than one inch in diameter shall not be measured and paid for as clearing and grubbing. Payment shall be based on the horizontal area cleared and grubbed as designated on the plans or as directed by the Owner. Measurement will be made to the nearest one hundredth of an acre.
- B. The unit price bid per acre shall also include all work as noted for permanent easements and shall also include protection of all trees, floral bushes or plants not to be removed or disturbed.

G-7 SOD (NO OVERAGE ALLOWED)

- A. Payment for placing sod as indicated on the drawings or as directed by the Project Coordinator or Project Engineer shall be made at the unit price bid per square yard listed in the Bid Form. Payment shall include grading, fine raking, sod bed preparation, pest and disease control, soil amendments, placing sod, anchoring, fertilizing, maintaining, protection of turf areas, removal and replacement of dying sod and watering to ensure growth. No payment will be made for sodding areas outside of easements or rights-of-way disturbed or otherwise damaged by the Contractor. The Proposal quantity reflects the total quantity of sod the Owner will pay for. In general, the maximum pay widths are shown below.
- B. In some cases, specific quantities of sod in individual easement areas are identified on the Drawings and no overage will be allowed or paid for in these specific locations.
- C. Stripping of topsoil will not be measured and paid for as a separate bid item. All work shall be included for payment under the applicable items listed in the Bid Form. Work shall include stripping, stockpiling, spreading, leveling, supplemental topsoil, filling, grading and compaction of suitable topsoil along right-of-way and easements.

Maximum Pay Widths for Sod

| Permanent Easements | 20' (or as indicated on the plans) |
|-------------------------|------------------------------------|
| Temporary Easements | 20' (or as indicated on the plans) |
| Storm Drainage | 15' |
| Water Mains | 12' |
| Sanitary Sewer Laterals | 6' |
| Water Laterals | 4' |

G-8 SEEDING (NO OVERAGE ALLOWED)

- A. Seeding of wetlands areas, easements and along right-of-way will be paid for at the unit price bid listed in the Bid Form and shall include all costs for soil preparation, pest control, disease control, anchoring, placing soil amendments, topsoil, grading, raking, seeding, fertilizing, mulching, crimping, watering, protection of turf areas, maintenance, reseeding if required, tack, and other work incidental thereto. Area to be paid for shall be measured horizontally and payment for this work will be made to the nearest one tenth (1/10) of an acre. No payment will be made for areas outside of permanent and temporary easements and along rights-of-way disturbed by the Contractor's operations.
- B. Stripping of topsoil will not be measured and paid for as a separate bid item. All work shall be included for payment under the applicable items listed in the Bid Form. Work shall include stripping, stockpiling, spreading, leveling, supplemental topsoil, filling, grading and compaction of suitable topsoil along right-of-way and easements.

G-9 FRENCH DRAINS

A. Payment for constructing french drains shall be made at the unit price bid per linear foot as listed in the Bid Form and shown on the detail. Payment shall include all labor, equipment and materials including but not limited to excavation, backfilling, compaction, filter fabric, slotted pipe, socks, graded stone, and all else necessary to complete the work.

| The location and length of french drains shall be as shown on the plans or as determine in the field by the Project Coordinator. | ∍d |
|--|----|
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |
| | |

PART "A", STREET CONSTRUCTION

A-1 PERMANENT PAVEMENT PATCH (NO OVERAGE ALLOWED)

Payment for placing a minimum of two (2) inches of Asphalt Pavement Surface Course (SF9.5A) and eight (8) inches of Aggregate Base Course (ABC), shall be made at the unit price bid per square yard completed and accepted as listed in the Bid Form. Installation of the permanent pavement patch shall be completed in accordance with these Contract Documents. Measurement shall be based on the number of square yards. The square yards will be calculated using the maximum trench widths.

Maximum payment widths for trenches have been established as indicated below. Payment widths shown include a minimum cutback of six (6) inches on each side of the trench prior to placing pavement patch. Any pavement removed or damaged beyond the limits specified, shall be replaced by the Contractor at his own cost unless directed otherwise by the Project Engineer. No payment for overage beyond the quantity shown in the Bid Form will be made.

Maximum Pay Widths for Permanent Pavement Patch

| Storm Drainage | 6' | (for pipe 24" in diameter and less) |
|-------------------|-----|--|
| Storm Drainage | 8' | (for pipe 30" up to 42" in diameter) |
| Storm Drainage | 10' | (for pipe 48" up to 54" in diameter) |
| Storm Drainage | 12' | (for pipe greater than 54") |
| Sanitary Sewer | 10' | (0' to 10' depth, measured to invert of pipe) |
| Sanitary Sewer | 12' | (greater than 10' depth, measured to invert of pipe) |
| Sewer Laterals | 6' | |
| Water Main | 4' | |
| Water Services | 4' | |

Payment for furnishing and placing permanent asphalt pavement patch shall include recutting pavement to straight uniform widths parallel and perpendicular to the road with no jagged edges, removal and disposal of asphalt offsite, re-compaction of pavement subgrade, placement and compaction of ten (10) inches of ABC, maintaining ABC stone at pavement grade until removal of upper two (2) inches for paving, installation and maintenance of transitions to accommodate road travel, adjusting structures as required, tack coat, placing and compacting of asphalt material, cleanup, and all costs for labor, materials, tools, equipment, and incidentals necessary to complete the work.

A-2 TEMPORARY ASPHALT PAVEMENT PATCH (NO OVERAGE ALLOWED)

Payment for the placement of Asphalt Pavement Intermediate Course (I19.0) shall be

made at the unit price bid per square yard completed and accepted with a minimum compacted thickness of three (3) inches as listed in the Bid Form. Installation of the temporary asphalt pavement patch shall be completed in accordance with these Contract Documents. Measurement shall be based on the number of square yards. The square yards will be calculated using the maximum trench widths.

Maximum payment widths for trenches have been established as indicated below. Payment widths shown include a minimum cutback of six (6) inches each side of the trench prior to placing pavement trench patch. Any pavement removed or damaged beyond the limits specified shall be replaced by the Contractor at his own cost unless directed otherwise by the Project Engineer. No payment for overage beyond the quantity shown in the Bid Form will be made.

Maximum Pay Widths for Temporary Pavement Patch

| Storm Drainage | 6' | (for pipe 24" in diameter and less) |
|-------------------|-----|--|
| Storm Drainage | 8' | (for pipe 30" up to 42" in diameter) |
| Storm Drainage | 10' | (for pipe 48" up to 54" in diameter) |
| Storm Drainage | 12' | (for pipe greater than 54") |
| Sanitary Sewer | 10' | (0' to 10' depth, measured to invert of pipe) |
| Sanitary Sewer | 12' | (greater than 10' depth, measured to invert of pipe) |
| Sewer Laterals | 6' | |
| Water Main | 4' | |
| Water Services | 4' | |

Payment for furnishing and placing temporary asphalt pavement patch shall include recutting pavement to straight uniform widths parallel and perpendicular to the road with no jagged edges, removal and disposal of asphalt off-site, re-compaction of pavement subgrade, installation and maintenance of transitions to accommodate road travel, adjusting structures as required, tack coat, placing and compacting of asphalt material, cleanup, and all costs for labor, materials, tools, equipment, and incidentals necessary to complete the Work.

This Measurement and Payment description only applies if the City of Fayetteville elects to proceed with an overlay as part of this Project. This line item is to be bid as an alternate, and if not incorporated into the Contract, shall not apply.

A-3 ASPHALT SURFACE COURSE PAVEMENT (OVERLAY)

Payment for placement of asphalt surface course (SF-9.5A) shall be made at the unit price bid per square yard completed and accepted with a minimum compacted thickness of one (1) inch. Installation of the Asphalt Surface Course shall be completed in accordance with these Contract Documents. Measurement shall be based on the number of square yards

in place and accepted.

The payment shall be full compensation for all work including preparation of existing surfaces, asphalt, cement, tack coat, and all incidentals necessary to complete the work to include maintenance and repair until final project acceptance.

Payment shall also include the adjustments of structures to finish grade of the overlay that may be necessary project wide.

This Measurement and Payment description only applies if the City of Fayetteville elects to proceed with an overlay as part of this Project. This line item is to be bid as an alternate, and if not incorporated into the Contract, shall not apply.

A-4 PERMANENT PAVEMENT PATCH FAILED AREAS (NO OVERAGE ALLOWED)

Failed areas are those areas outside the specified trench limits that have been identified by the City of Fayetteville or the Project Engineer as needing to be replaced. Payment shall be made for removing the failed areas as identified, milling and replacing with two (2) inches of Asphalt Pavement Surface Course and eight (8) inches of Aggregate Base Course (ABC). Payment shall be made at the unit price bid per square yard completed and accepted as listed in the Bid Form. Installation of the permanent pavement patch in these areas shall be completed in accordance with these Contract Documents. Any pavement removed or damaged beyond the specified area of failed pavement shall be replaced by the Contractor at his own cost unless directed otherwise by the Project Engineer. No payment for overage beyond the quantity shown in the Bid Form will be made.

Payment for furnishing and placing permanent asphalt pavement patch in failed areas shall include re-cutting pavement to straight uniform widths parallel and perpendicular to the road with no jagged edges, removal and disposal of asphalt offsite, re-compaction of pavement subgrade, placement and compaction of ten (10) inches of ABC, maintaining ABC stone at pavement grade until removal of upper two (2) inches for paving, installation and maintenance of transitions to accommodate road travel, adjusting structures as required, tack coat, placing and compacting of asphalt material, cleanup, and all costs for labor, materials, tools, equipment, and incidentals necessary to complete the work.

A-5 TEMPORARY PAVEMENT PATCH FAILED AREAS (NO OVERAGE ALLOWED)

Failed areas are those areas outside the specified trench limits that have been identified by the City of Fayetteville or the Project Engineer as needing to be replaced. Payment shall be made for removing the failed areas as identified, milling and replacing with three (3) inches of Asphalt Pavement Intermediate Course (I19.0). Payment shall be made at the unit price bid per square yard completed and accepted as listed in the Bid Form. Installation of the temporary pavement patch in these areas shall be completed in accordance with these Contract Documents. Any pavement removed or damaged beyond the specified area of failed pavement shall be replaced by the Contractor at his own cost unless directed otherwise by the Project Engineer. No payment for overage beyond the quantity shown in the Bid Form will be made.

Payment for furnishing and placing temporary asphalt pavement patch in failed areas shall include re-cutting pavement to straight uniform widths parallel and perpendicular to the road with no jagged edges, removal and disposal of asphalt offsite, re-compaction of

pavement subgrade, installation and maintenance of transitions to accommodate road travel, adjusting structures as required, tack coat, placing and compacting of asphalt material, cleanup, and all costs for labor, materials, tools, equipment, and incidentals necessary to complete the work.

This Measurement and Payment description only applies if the City of Fayetteville elects to proceed with an overlay as part of this Project. This line item is to be bid as an alternate, and if not incorporated into the Contract, shall not apply.

A-6 UNDERCUT EXCAVATION IN ASPHALT SUBGRADE

Undercut excavation shall be measured by the volume in cubic yards of unsuitable material excavated, as authorized by the Project Engineer. Excavation to greater depths and/or widths shall be backfilled and compacted with ABC stone at no additional cost to the Owner. Payment shall constitute full compensation for removal and disposal of unsuitable material off site, furnishing, placing, grading, and compaction of ABC stone and all incidentals necessary to complete the work. No payment for this item shall be made unless specifically authorized by the PWC Project Coordinator.

A-7 INCIDENTAL STONE (ABC)

Payment for incidental Aggregate Base Course (ABC) authorized by the Project Coordinator to be placed for the maintenance of driveways and street intersections shall be made at the unit price bid per ton. Contractor shall submit tickets to the Project Coordinator in accordance with these Contract Documents. Payment for incidental stone will not be made without copies of the accompanying tickets.

Payment shall include all costs for labor, tools, materials, equipment, furnishing, placing, supplementing stone required for maintenance, grading stone, wetting, compaction, removing and disposal of incidental stone immediately prior to asphalt pavement patch in each area. Incidental stone that is stockpiled or not placed will not be considered for payment.

Contractor shall remove a minimum two (2) inches of soil or ABC stone, place, and compact stone in order to be considered for payment.

No separate payment shall be made for incidental ABC stone placed in mainline or service lateral trenches unless authorized by the PWC Project Coordinator.

A-8 REMOVE AND REPLACE CONCRETE CURB AND GUTTER

Removal and replacement of concrete curb and gutter will be paid for at the unit price bid per linear foot. Measurement of the curb and gutter shall be along the bottom of the gutter near the face of the curb excluding catch basin openings. Payment shall be full compensation for removal and disposal of existing concrete curb and gutter, grading, form work, backfilling behind curb with topsoil, and all equipment, materials, tools, labor, and incidentals necessary to complete the work.

A-9 REMOVE AND REPLACE CONCRETE DRIVEWAYS (NO OVERAGE ALLOWED)

Removal and replacement of concrete driveways shall be paid for at the unit price bid per

FAYETTEVILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27 - CLIFFDALE FOREST

square yard. Concrete drives shall be installed in accordance with the Owner's requirements. Measurement shall be made to the nearest one-tenth square yard. Payment shall be full compensation for saw cutting and removal of the existing driveway, removing and disposing of excess or unsuitable materials off-site, grading, compaction, expansion joint materials, backfilling with topsoil, curing compound, form work, and all equipment, tools, labor, and incidentals necessary to complete the work.

A-10 REMOVE AND REPLACE ASPHALT DRIVEWAYS (NO OVERAGE ALLOWED)

Removal and replacement of asphalt driveways shall be paid for at the unit price bid per square yard. Asphalt drives shall be installed in accordance with the Owner's requirements. Measurement shall be made to the nearest one-tenth square yard. Payment shall be full compensation for saw cutting and removal of the existing driveway, removing and disposing of excess or unsuitable materials off-site, grading, compaction, backfilling behind with topsoil, all equipment, tools, labor, and incidentals necessary to complete the work.

A-11 REPLACE GRAVEL/SOIL DRIVEWAYS WITH AGGREGATE BASE COURSE (NO OVERAGE ALLOWED)

Removal and replacement of gravel/soil driveways shall be paid for at the unit price bid per square yard. Gravel/soil drives shall be installed in accordance with the Owner's requirements. Measurement shall be made to the nearest one-tenth square yard. Payment shall be full compensation for removal of the existing driveway, removing and disposing of excess or unsuitable materials off-site, grading, compaction, and all equipment, tools, labor, and incidentals necessary to complete the work.

A-12 REMOVE AND REPLACE CONCRETE SIDEWALK

Removal and replacement of concrete sidewalk shall be paid for at the unit price bid per linear foot. The concrete sidewalk shall be constructed in accordance with the Owner's requirements. Payment shall be full compensation for saw cutting and removal of the existing sidewalk, removing and disposing of excess or unsuitable materials off-site, grading, compaction, expansion joint material, form work, backfilling behind curb with topsoil, curing compounds and all equipment, tools, labor, and incidentals necessary to complete the work

A-13 MAINTENANCE STONE (NO OVERAGE ALLOWED)

Payment for maintenance stone (#57) authorized by the Project Coordinator shall be made at the unit price bid per square yard. Payment shall include all costs for labor, tools, materials, equipment, compaction, maintenance, and the removal and disposal of maintenance stone in each area.

To be considered for payment, maintenance stone shall be at a minimum depth of four (4) inches and a minimum length of fifty (50) feet. Payment shall be made based upon actual width in place not to exceed ten (10) feet.

A-14 TEMPORARY DRIVEWAY

Payment under this item shall include all costs necessary to install, maintain and remove a temporary driveway as specified on the plans. The driveway shall be installed utilizing

six (6) inches of Aggregate Base Course (ABC) compacted in place. Payment shall be by lump sum. Fifty Percent (50%) of the item will be paid upon installation of the temporary driveway. The balance will be paid once the temporary driveway has been removed and the property has been restored to existing or better condition. The Contractor shall be responsible for obtaining a signed release from the property owner(s), stating the property has been properly restored.

A-15 SHOULDER RECONSTRUCTION

Payment for shoulder reconstruction shall be made at the unit price per square yard. Shoulders shall be reconstructed 3-foot wide each side of the resurfaced roadway. This work shall include building and maintaining the roadway shoulders following the resurfacing of the roadway, reconstructing and restoring the roadway shoulder areas with top soil and sod, labor, materials, equipment and all other incidentals necessary to complete the work.

This Measurement and Payment description only applies if the City of Fayetteville elects to proceed with an overlay as part of this Project. This line item is to be bid as an alternate, and if not incorporated into the Contract, shall not apply.

A-16 ASPHALT LEVELING COURSE

Payment for leveling course shall be made at the unit price per ton. Contractor shall submit asphalt tickets to the Project Coordinator in accordance with these Contract Documents. Payment for leveling course will not be made without copies of the accompanying tickets. The installation of the leveling course shall be completed in accordance with these Contract Documents.

Payment for the leveling course shall include preparation of existing surfaces, crack filling, tack coat and all labor, materials, tools, equipment, and incidentals necessary to complete the work.

This Measurement and Payment description only applies if the City of Fayetteville elects to proceed with an overlay as part of this Project. This line item is to be bid as an alternate, and if not incorporated into the Contract, shall not apply.

PART "C", WATER UTILITIES

C-1 PVC WATER MAINS

A. Installation of the PVC water main shall be accomplished in accordance with PWC Standard Specifications 02660 Water Distribution. Payment under this item shall include all costs necessary to install the specified water main in accordance with PWC standards. Work shall include all costs for excavation, backfill, thrust blocking as required, compaction, fittings, tracing wire, cutting and removal of pavement, removal and disposal of excess unsuitable material off site, installation of the pipe at the specified line and grade, bedding material, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, all required compaction testing, proper alignment of the installed main, and all other items related to proper installation. No payment for installation of water main shall be made until all required compaction testing has been satisfactorily completed.

C-2 DUCTILE IRON WATER MAIN

A. Installation of the ductile iron water main shall be accomplished in accordance with PWC Standard Specifications 02660 Water Distribution. Payment under this item shall include all costs necessary to install the specified water main in accordance with PWC standards. Work shall include all costs for excavation, backfill, thrust blocking as required, compaction, fittings, cutting and removal of pavement, installation of the pipe at the specified line and grade, bedding material, removal and disposal of excess unsuitable material off site, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, all required compaction testing, proper alignment of the installed main, and all other items related to proper installation. No payment for installation of water main shall be made until all required compaction testing has been satisfactorily completed.

C-3 RESTRAINED JOINT DUCTILE IRON WATER MAIN

A. Installation of the restrained joint ductile iron water main shall be accomplished in accordance with PWC Standard Specifications 02660 Water Distribution. Payment under this item shall include all costs necessary to install the water main in accordance with PWC standards. Work shall include all costs for excavation, backfill, compaction, fittings, cutting and removal of pavement, installation of restrained joint pipe as specified in the drawings or as required by PWC standards, bedding material, removal and disposal of excess unsuitable material off site, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, all required testing, proper alignment of the installed main, and all other items related to proper installation. No payment for installation of the water main shall be made until all required compaction tests are satisfactorily completed.

C-4 TWO (2) INCH PVC WATER MAIN

A. Installation of the two (2) inch PVC water main shall be accomplished in accordance with PWC Standard Specifications 02660 Water Distribution. Payment under this item shall include all costs necessary to install the specified water main in accordance with PWC standards. Work shall include all costs for excavation, backfill, thrust blocking as required, compaction, fittings, cutting and removal of pavement, installation of the pipe at the specified line and grade, tracing wire, bedding material, removal and disposal of excess unsuitable material off site, and all labor, materials, equipment, and incidentals

necessary to complete the work. The Contractor shall be responsible for completing the installation, all required compaction testing, proper alignment of the installed main, and all other items related to proper installation. No payment for installation of water main shall be made until all required compaction testing has been satisfactorily completed.

C-5 UNDERCUT EXCAVATION

- A. Undercut excavation shall be measured and paid for by the volume in cubic yards of unsuitable material excavated below the bedding limit line of four (4) inches below the pipe as authorized by the Project Coordinator. Payment shall be based on the width of two (2) feet plus the internal diameter of the pipe and to the authorized additional depth required for proper support of the pipeline. Payment for structures shall be based on the width of two (2) feet plus the external diameter/dimension to the authorized depth required for proper support of the structure.
- B. Payment shall include the costs for all labor, tools, materials and equipment including but not limited to the removal and disposal of unsuitable soil, approved bedding material and all other incidentals necessary to complete the work. No payment for undercut will be made for over excavation by error or where proper dewatering methods are not in place for trench and or excavation stabilization.

C-6 GATE VALVES

A. Gate valves shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to install the specified gate valve and valve box, as indicated on the plans. All gate valves shall be installed in accordance with PWC standard details. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, installation, valve boxes, concrete protection rings, concrete collars, tracing wire, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-7 GATE VALVES ON EXISTING MAINS

A. Installation of gate valves on existing mains shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to install the specified gate valve and valve box on the existing water main, as indicated on the plans. All gate valves shall be installed in accordance with PWC standard details. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, installation, cutting and disposal of the existing water main, valve boxes, fittings, concrete protection rings, concrete collars, tracing wire, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-8 TAPPING SLEEVE AND VALVE

A. Installation of tapping sleeves and valves shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to install the specified tapping sleeve and valve on the existing water mains. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, determining the proper size sleeve, installation, testing

of the sleeve, thrust blocking, concrete protection rings, concrete collars, valve boxes, tracing wire, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-9 TAPPING SADDLE AND VALVE

A. Installation of tapping saddles and valves shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to install the specified tapping saddle and two (2) inch ball valve on the existing or proposed water mains. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, determining the proper size saddle, installation, valve boxes, tracing wire, concrete protection rings, concrete collars, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-10 FIRE HYDRANTS ON EXISTING WATER MAINS

A. Fire hydrants will be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid for fire hydrants as listed in the Bid Form. Payment will be full compensation for furnishing and installing hydrants and hydrant branches in accordance with PWC standards, painting, stone drainage wells, anchorage, testing, excavation, backfill and compaction, saw-cutting, removal, and disposal of pavement, sod all disturbed areas, gate valves and boxes, pipe, fittings, concrete protector rings, concrete collars, removal and disposal of excess unsuitable material off site, tapping sleeve and valve, hydrant barrel adjustments to finish grade, and painting.

C-11 FIRE HYDRANT INSTALLATION

A. Fire hydrants will be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to install a new fire hydrant to the proposed location as shown on the plans, in accordance with PWC standards. Work shall include cutting and removal of pavement, concrete collars, gate valves, boxes, concrete protection ring, painting, barrel depth verification, hydrant barrel depth adjustments to finished grade, excavation, backfill, compaction, pipe, fittings, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-12 REMOVE EXISTING FIRE HYDRANT

A. Payment under this item shall include all costs necessary to remove the existing fire hydrant. Work shall include cutting and removal of pavement, excavation, backfill, compaction, removal of pipe, valve, and fittings, capping of the existing hydrant branch, returning the fire hydrant to PWC, removal and disposal of excess unsuitable material off site, sod all disturbed areas, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-13 INSTALLATION OF NEW WATER SERVICE

A. Installation of a new water service shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall install water services, utilizing copper tubing, as indicated on the plans. Installation of the services shall be in accordance with PWC standard detail W.24.

The meter boxes shall be located 18-inches inside the right-of-way, in accordance with PWC standards. Payment under this item shall include all costs necessary to install the new copper service, as indicated on the plans. Work shall include cutting and removal of pavement, proper disposal of waste, excavation, backfill, removal and disposal of excess unsuitable material off site, compaction, installation, if necessary boring the lateral under the road, furnishing and installing new meter boxes, corporations, saddles, lock valves, fittings, tapping the new or existing water main, and all equipment, tools, labor, and incidentals necessary to complete the work. No payment for installation of water services shall be made until all required compaction testing has been satisfactorily completed.

C-14 REPLACEMENT OF EXISTING 1-INCH WATER SERVICE

A. Replacement of existing water services shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall replace the existing water services, utilizing copper tubing, as indicated on the plans. Installation of the services shall be in accordance with PWC standard detail W.24. The meter boxes shall be located 18-inches inside the right-of-way, in accordance with PWC standards. All connections to the customer side of the meter shall be completed by the Contractor. Payment under this item shall include all costs necessary to install the new copper service, as indicated on the plans. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, installation, if necessary boring the lateral under the road, furnishing and installing new meter boxes, corporations, saddles, lock valves, tailpiece, fittings, tapping the new or existing water main, connecting the new service to the Customer's side utilizing brass fittings, and all equipment, tools, labor, and incidentals necessary to complete the work. No payment for installation of water services shall be made until all required compaction testing has been satisfactorily completed.

C-15 1-INCH WATER SERVICE RELOCATION

A. Relocation of water services shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall relocate and replace the existing water service utilizing copper tubing, as indicated on the plans. Installation of the service shall be in accordance with PWC standard detail W.24. The meter box shall be located 18-inches inside the right-of-way. in accordance with PWC standards. The location of the new meter box is as indicated on the plans. All connections to the customer side of the meter shall be completed by the Contractor utilizing brass fittings. Payment under this item shall include all costs necessary to install the new copper service, as indicated on the plans. Work shall include cutting and removal of pavement, removal and disposal of excess unsuitable material off site, excavation, backfill, compaction, installation, if necessary boring the lateral under the road, removal of the existing meter box, removal and reinstallation of existing meter to new location, furnishing and installing new meter boxes, corporations, saddles, lock valves, tailpiece, fittings, tapping the new or existing water main, and all equipment, tools, labor, and incidentals necessary to complete the work. No payment for relocation of the existing water service shall be made until all required compaction testing has been satisfactorily completed.

C-16 ADJUSTING EXISTING VALVE BOXES

A. Adjustment of existing valve boxes indicated as a separate item of work shall be measured by actual count, complete, in place, and payment will be made at the applicable

unit price bid as listed in the Bid Form. Payment will be full compensation for excavation, removal and disposal of excess unsuitable material off site, concrete valve protection rings, furnishing and placement of concrete collars in paved areas, re-adjustments, backfill, compaction, and all other essentials necessary for the complete adjustment in accordance with PWC requirements. Replacement of valve boxes if necessary will be as directed by the PWC Project Coordinator.

C-17 ABANDONMENT OF WATER SERVICES

A. Abandonment of existing water services shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall furnish all materials necessary to "kill-out" the existing water services. The Contractor will excavate the tap on the existing main, turn off the corporation, plug the corporation, then plug the service, as indicated on the plans. All work shall be in accordance with PWC standards. Work shall include all costs for excavation, cutting and removal of pavement, removal of meter boxes, removal and disposal of excess unsuitable material off site, backfill, compaction, all necessary fittings, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-18 TWO (2) INCH BLOW OFF

A. Installation of two (2) inch blow-offs shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all necessary costs to install a two (2) inch blow-off at the end of water mains, in accordance with PWC standards. The Contractor shall furnish and install a blow-off assembly at the end of the water mains, as indicated on the drawings. Work shall include all costs for excavation, valves, valve boxes, meter boxes, tracing wire, backfill, compaction, fittings, thrust blocks, saddles, concrete protector rings, concrete collar, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-19 CONNECT TO EXISTING WATER MAIN

A. Connections to existing water mains shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all necessary costs to connect to the existing water main. Work shall include all costs for excavation, backfill, compaction, removal of the existing blow-off, tracing wire, removal and disposal of excess unsuitable material off site, necessary fittings to connect to the new water main, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-20 ABANDON EXISTING VALVES

A. Abandonment of existing valves shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all necessary costs to properly abandon the existing valves, as specified on the plans. Work shall include all costs for excavation, cutting and removal of pavement, removal and disposal of excess unsuitable material off site, backfill, compaction, fittings, turning off existing valve, plugging existing valve and all necessary fittings, removal of valve boxes as required, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-21 ABANDON & GROUT FILL EXISTING WATER MAIN

A. Payment under this item shall include all necessary costs to grout fill the existing water main to be abandoned. All work shall be in accordance with PWC standard detail W.22, and as approved by PWC. Work shall include all costs to plug the water main, hoses, pumps, fittings, grout, and all labor, materials, equipment, and incidentals necessary to complete the work. Grouting of the water main shall occur after PWC has accepted the new water main and laterals.

C-22 ABANDON EXISTING WATER MAIN

A. Abandonment of the existing water main shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall furnish all materials necessary to "kill-out" the existing water mains, as indicated on the plans. All work shall be in accordance with PWC standard detail W.22, and as approved by PWC. Work shall include all costs for excavation, cutting and removal of pavement, removal and disposal of unsuitable material off site, backfill, compaction, concrete, all necessary fittings, and all equipment, tools, labor, and incidentals necessary to complete the work.

C-23 BORE AND JACK

A. Payment under this item shall include all necessary costs to install the casing and carrier pipe in accordance with the project requirements. Work shall include all costs for excavation, shoring, removal and disposal of excess unsuitable material off site, bedding material, horizontal and vertical controls, bore steering mechanisms, steel casing, casing spacers, concrete grouting and closures, installation of the restrained joint ductile iron carrier pipe, backfill, compaction, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall comply with all requirements for construction within the right-of-ways of the applicable permitting authority.

C-24 STERILIZATION AND TESTING

- A. Payment under this line item shall include all costs necessary to perform the required testing on the water mains, laterals and appurtenances. Work shall include all costs for furnishing test equipment, installation of temporary taps for testing and/or disinfection, coordination with the Project Coordinator, and all labor, materials, equipment, and incidentals necessary to complete the testing in accordance with PWC standards. All laterals shall be tested. The Contractor shall pressure test and disinfect the new water main, laterals and appurtenances in accordance with PWC standards, prior to placing it into service.
- B. The Contractor shall be responsible for furnishing all necessary equipment to complete the testing and sterilization, coordination with the Project Coordinator, and removal of all unnecessary taps and fittings upon completion of the work. Payment under this line item will not be made until all required tests are successful.

C-25 REPLACEMENT OF ASBESTOS-CEMENT WATER MAINS

A. Payment under this line item shall include all costs necessary to remove the existing asbestos-cement (AC) water mains and install new ductile iron water mains. Replacement of the water main shall be in accordance with PWC standards. Work shall include all costs

for excavation, backfill, thrust blocking as required, compaction, fittings, all necessary connections, cutting and removal of pavement, installation of the pipe at the specified line and grade, bedding material, removal and disposal of excess unsuitable material off site, removal and proper disposal of the AC water main, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, all required compaction testing, proper alignment of the installed main, and all other items related to proper installation. The replacement of the existing AC water main shall be paid for by the actual count per linear feet installed at each proposed crossing.

B. The Contractor shall also replace all of the existing water services from the main to the meter box connected to the section of the AC pipe to be replaced. The water services and meter boxes shall be replaced in accordance with the utility owner's standards. The replacement of the connected water services shall be paid for by the actual count of each and payment made under the applicable unit price per each contained in the Bid Form.

C-26 RELOCATION OF EXISTING WATER MAINS

- A. Payment under this line item shall include all costs necessary to relocate existing water mains due to conflict with existing or proposed utility work. Relocation of the water main shall be in accordance with PWC standards. Work shall include all costs for excavation, backfill, , compaction, fittings, installation of restrained joint pipe as specified in the drawings or as required by PWC standards, all necessary connections, cutting and removal of pavement, installation of the pipe at the specified line and grade, bedding material, removal and disposal of excess unsuitable material off site, removal and proper disposal of the existing water main, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, all required compaction testing, proper alignment of the installed main, and all other items related to proper installation. The relocation of the existing water main shall be paid for by the actual count per linear feet installed.
- B. The Contractor shall also replace all of the existing water services from the main to the meter box connected to the section of the pipe to be relocated. The water services and meter boxes shall be replaced in accordance with the utility owner's standards. The replacement of the connected water services shall be paid for by the actual count of each and payment made under the applicable unit price per each contained in the Bid Form.

C-27 INSTALLATION OF NEW 2" WATER SERVICE

A. Installation of a new 2 inch water service shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. The Contractor shall install water services, utilizing SDR-21, as indicated on the plans. Installation of the services shall be in accordance with PWC standard details W.5 and W.15. The meter boxes shall be located 18-inches inside the right-of-way, in accordance with PWC standards. Payment under this item shall include all costs necessary to install the new 2" SDR-21 water service, as indicated on the plans. Work shall include cutting and removal of pavement, proper disposal of waste, excavation, backfill, removal and disposal of excess unsuitable material off site, compaction, installation, if necessary boring the lateral under the road, furnishing and installing new meter boxes, 2" ball valve, 2" tapping saddles, corporations, saddles, lock valves, fittings,

tapping the new or existing water main, and all equipment, tools, labor, materials, and incidentals necessary to complete the work. No payment for installation of water services shall be made until all required compaction testing has been satisfactorily completed.

C-28 WELL ABANDONMENT

A. Seal abandoned wells at locations shown in the contract or as directed. Perform all work I accordance with NCDEQ requirements.

Construction Methods

- A. Contractor shall utilize a Well Contractor that is certified by the State of North Carolina to perform abandonment. Prior to commencing clearing and grubbing in the easement, the Contractor shall inspect the area to determine if there are any wells within the clearing limits. The well shall be inspected from land surface to the entire depth of the well before it is sealed to ensure freedom from obstructions that may interfere with sealing operations. Before sealing, place chlorine in the well in sufficient quantities to produce a chlorine residual of at least 100 milligrams per liter in the well. All casing and screen materials may be salvaged except casing that is cemented in place. In the case of gravel-packed wells in which the casing and screens have not been removed, perforate the casing opposite the gravel pack at intervals not exceeding 10 feet. Completely fill bored wells with cement grout or dry clay compacted in place. Completely fill wells constructed in unconsolidated formations with cement grout by introducing it through a pipe extending to the bottom and raising it as the well is filled. Fill wells constructed in consolidated rock formations or that penetrate zones of consolidated rock to at least 5 feet below the top of the consolidated rock with sand, gravel, or grout opposite the zones of consolidated rock. Fill the remainder of the well with cement grout. Complete a certified well abandonment record (Form GW-30) and submit to the Owner and to NCDEQ.
- B. The contractor shall remove and dispose of the well house/pumphouse, remove all piping at the wellhouse/pumphouse, return the pump to the property owner, disconnect any electrical components from the power source (at the electrical panel) to the well pump, and disconnect and plug the existing plumbing back to the structure. The contractor shall restore the property with sod upon completion.
- C. If the property owner is not served by public water, the contractor shall connect the owner to public water as indicated in the Contract Documents. Payment for connecting the property owner to public water shall be made under a separate line item. If the property owner utilizes the well for irrigation purposes, the contractor shall connect the existing irrigation to public water as indicated in the Contract Documents. Payment for connecting the property owner's irrigation to public water shall be made under a separate line item.

Measurement and Payment

A. Payment under this item shall include all costs to abandon existing wells in accordance with NCDEQ requirements. Work shall include, but not limited to, chlorinating the well before sealing, perforating the well casing, filling the well with cement, grout, dry clay, and or gravel, furnishing all necessary records to NCDEQ, furnishing all records and confirmations of receipt of records by NCDEQ to the Owner (PWC), removal and disposal of the existing well house/pumphouse, removal and disposal of piping, removing the pump and providing it to the property owner, disconnecting any electrical components from the power source to the well pump, disconnecting and plugging existing plumbing, restoration of the property with sod,

| and any other incidentals necessary to complete the work. |
|---|
| |
| |
| |
| |
| |
| |
| |
| |
| |
| |
| |
| |
| |

PART "D", SANITARY SEWER UTILITIES

D-1 PVC SANITARY SEWER MAINS

A. Installation of the PVC sewer main shall be accomplished in accordance with PWC Standard Specifications 02730 Sanitary Sewer Systems. Payment per linear foot of sanitary sewer shall be made at the applicable unit prices for each size and pay depth as indicated on the Bid Form. Payment under this item shall include all costs necessary to install the specified sewer main in accordance with PWC standards. Work shall include all costs for excavation, backfill, compaction, dewatering, cutting and removal of pavement, proper disposal of waste materials, installation of the pipe at the specified line and grade, stone bedding, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, proper alignment and grade of the installed main, and all other items related to proper installation. All pipe segments installed must have passed the detailed compaction requirements in order to be considered for payment.

D-2 DUCTILE IRON SEWER MAIN

A. Installation of the ductile iron sewer main shall be accomplished in accordance with PWC Standard Specifications 02730 Sanitary Sewer Systems. Payment per linear foot of sanitary sewer shall be made at the applicable unit prices for each size and pay depth as indicated on the Bid Form. Payment under this item shall include all costs necessary to install the specified sewer main in accordance with PWC standards. Work shall include all costs for excavation, backfill, compaction, dewatering, cutting and removal of pavement, proper disposal of waste materials, installation of the pipe at the specified line and grade, stone bedding, linings, coatings and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall be responsible for completing the installation, proper alignment and grade of the installed main, and all other items related to proper installation. All pipe segments installed must have passed the detailed compaction requirements in order to be considered for payment.

D-3 LOW PRESSURE FORCE MAIN

A. Measurement for the installation of a low pressure sewer system force main shall be made at the unit price bid per linear foot contained in the Bid Form. Payment shall include excavation, saw cutting, removal and disposal of pavement, all necessary fittings, installation of the blow-off assembly, tracing wire, backfill, passing compaction for each segment, and all other labor, materials and equipment necessary to install a complete low pressure force main as specified herein and as shown on the Contract Drawings. Pipe segments installed must have passed the detailed compaction requirements in order to be considered for payment.

D-4 HORIZONTAL DIRECTION DRILLING – DUCTILE IRON PIPE

A. The quantity of the directionally controlled horizontal drilling to be paid for shall be the number of linear feet, complete, in place, as determined by the horizontal length labeled as beginning and ending stations, as shown on the plans. Payment shall be made at the applicable indicated unit price bid, as contained in the Bid Form. Payment will include all work of every description including excavation, grading, trenching, backfilling, dewatering, compaction, drilling, drilling mud, (i.e. lubricants), fittings, connection to the manhole or pipe, CCTV inspection of all pipe installed and all other incidentals necessary for the

complete pipe installation.

D-5 FURNISH AND INSTALL MANHOLE

A. Payment under this item shall include all costs necessary to furnish and install various diameter manholes as specified on the plans. Payment per each manhole shall be made at the applicable unit prices for each size and pay depth as indicated on the Bid Form. Work shall include all costs for excavation, backfill, removal and disposal of unsuitable material off-site, linings, inverts, pipe slides, dewatering, compaction, cutting and removal of pavement, proper disposal of waste, stone bedding, installation of the manhole in accordance with PWC standards, installation of the specified frame and cover, concrete collar, and all labor, materials, equipment, and incidentals necessary to complete the work.

D-6 FURNISH AND INSTALL DOGHOUSE MANHOLE

A. Payment under this item shall include all costs necessary to furnish and install various diameter doghouse manholes as specified on the plans. Payment per each doghouse manhole shall be made at the applicable unit prices for each size and pay depth as indicated on the Bid Form. Work shall include all costs for excavation, backfill, compaction, cutting and removal of pavement, proper disposal of waste, linings, inverts, pipe slides, installation of the doghouse manhole in accordance with PWC standards, installation of the specified frame and cover, stone bedding, removal and disposal of unsuitable material off-site, dewatering, removal of the existing pipe, concrete collar, and all labor, materials, equipment, and incidentals necessary to complete the work. Vacuum testing of the doghouse manhole is not required.

D-7 FURNISH AND INSTALL INSIDE DROP STRUCTURE

A. Payment shall be measured by actual count, complete, in place and accepted at the unit price bid as listed on the Bid Form. Payment shall include all costs necessary to install the specified inside drop connection in accordance with PWC standards. Work shall include installation of the inside drop structure in accordance with PWC standard detail S.5. Work shall include all costs for pipe, fittings, stainless steel straps, anchors, and all labor, materials, equipment, and incidentals necessary to complete the work.

D-8 PVC SEWER LATERAL INSTALLATION

A. Installation of PVC sewer laterals shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to furnish and install a PVC sanitary sewer lateral in accordance with PWC standards. Work shall include all costs for excavation, backfill, compaction, cutting of pavement, removal and disposal of excess unsuitable material off-site, proper disposal of waste, dewatering, marking the location of the lateral on the curb or edge of pavement, installation of a cleanout, all necessary fittings, stone bedding, installation of the lateral at the specified line and grade, and all labor, materials, equipment, and incidentals necessary to complete the work. All laterals installed must have passed the detailed compaction requirements in order to be considered for payment.

D-9 DUCTILE IRON SEWER LATERAL INSTALLATION

A. Installation of ductile iron sewer laterals shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs necessary to furnish and install a ductile iron sanitary sewer lateral in accordance with PWC standards. Work shall include all costs for excavation, backfill, compaction, cutting of pavement, removal and disposal of excess unsuitable material off-site, proper disposal of waste, dewatering, marking the location of the lateral on the curb or edge of pavement, installation of a cleanout, coatings, linings, all necessary fittings, stone bedding, installation of the lateral at the specified line and grade, and all labor, materials, equipment, and incidentals necessary to complete the work. All laterals installed must have passed the detailed compaction requirements in order to be considered for payment.

D-10 ABANDON EXISTING SEWER LATERAL

A. Abandonment of existing sewer laterals shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all necessary costs to abandon existing sewer laterals as indicated on the plans. Work shall include all costs for excavation, dewatering, backfill, removal of the existing lateral at the main, installing a plug at the main to lateral connection, compaction, removal of the existing combination and cleanout stack, installing a plug on that end of the lateral, and all labor, materials, equipment, and incidentals necessary to complete the work.

D-11 RECONNECT SEWER LATERAL TO EXISTING PLUMBING

A. Re-connecting a sewer lateral to existing plumbing shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs to connect from the PWC lateral to the customer's existing sewer service as indicated on the plans. Work shall be in accordance with the Plumbing code and City of Fayetteville requirements. Work shall include all costs to install cleanouts, permits, coordination with the property owner, excavation, dewatering, backfill, compaction, connection to the existing lateral, and all labor, materials, equipment and incidentals necessary to complete the work.

D-12 LOW PRESSURE SERVICE LATERAL

A. Measurement for the installation of a low pressure sewer lateral to serve an individual building shall be made at the unit price bid per each as contained in the Bid Form. Payment shall include all necessary excavation, removal and disposal of excess unsuitable materials off site, saw-cutting and removal of pavement, all necessary fittings, connection to the low pressure force main, tracing wire, installation of the connection assembly at the property line, dewatering, compaction, backfill, and all other labor, materials, and equipment necessary to furnish and install a complete low pressure service lateral assembly as specified herein and as shown on the Contract Drawings. Laterals installed must have passed the detailed compaction requirements in order to be considered for payment.

D-13 CONNECTIONS TO EXISTING STRUCTURES

A. Connections to existing manholes will be paid for at the unit price bid per each as listed in the Bid Form completed and accepted and shall include all costs of equipment, labor, tools, materials and all incidental work. Connections shall consist of coring the manhole,

installing flexible boots, re-building inverts, and sealing penetrations as required.

D-14 ANTI-SEEP COLLARS

A. Payment for installing anti-seep collars shall be made at the unit price bid per each as listed on the Bid Form. Collars shall be constructed at the locations indicated on the Contract Drawings and as shown in the PWC Standard Details.

D-15 CONCRETE ANCHOR BLOCKS

A. Concrete anchor blocks will be measured and paid for by actual count, complete, in place. Payment shall be based upon the unit price bid as contained in the Bid Form. Payment shall include all work of every description necessary for complete installation, including concrete construction, stainless steel saddle, fittings, stone bedding as required, anchoring materials and all other labor, materials and equipment to construct and install concrete anchor blocks in accordance with PWC requirements.

D-16 UNDERCUT EXCAVATION

- A. Undercut excavation shall be measured and paid for by the volume in cubic yards of unsuitable material excavated below the bedding limit line of four (4) inches below the pipe as authorized by the Project Coordinator. Payment shall be based on the width of two (2) feet plus the internal diameter of the pipe and to the authorized additional depth required for proper support of the pipeline. Payment for structures shall be based on the width of two (2) feet plus the external diameter to the authorized depth required for proper support of the structure.
- B. Payment shall include the costs for all labor, tools, materials and equipment including but not limited to the removal and disposal of unsuitable soil, furnishing and placing stone bedding material and all other incidentals necessary to complete the work. No payment for undercut will be made for over excavation by error or where proper dewatering methods are not in place for trench and or excavation stabilization.

D-17 TESTING

- A. Payment under this item shall include all costs necessary to perform the required testing on the sewer mains, laterals, and manholes. Work shall include all costs for furnishing test equipment, blow offs coordination with the PWC Project Coordinator, and all labor, materials, equipment, and incidentals necessary to complete the testing in accordance with PWC standards. Payment under this line item shall not be made until all performed tests are successful. No extra payment will be made for laterals connecting directly to manholes.
- B. The Contractor shall be responsible for furnishing all necessary equipment to complete the testing, coordination with the Project Coordinator, and removal of all unnecessary taps and fittings upon completion of the work. Payment under this line item will not be made until all required tests are successful.

D-18 LIFT STATION WATER SERVICE

A. Water services shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Installation of one-inch (1") copper water service for a lift station will be measured by actual count in place and accepted. Payment shall be made under the applicable unit price bid per each as

contained in the Bid Form. Payment shall include saw cutting, removing and disposal of pavement, excavation, tapping and connecting to water mains, fittings, service pipe, corporations, installation of a reduced pressure backflow device in an insulated above ground enclosure, yard hydrant, standard meter box, all associated fittings, backfill, compaction, and all other incidental work necessary to furnish a complete installation as specified herein and shown on the Contract Drawings. Metering for the service will be installed by the utility provider once work has been completed and accepted.

D-19 SELF-PRIMING LIFT STATION

A. Payment for the self-priming lift station as described herein shall be made at the lump sum price bid contained in the Bid Form. Payment shall include all necessary piping, fittings, wet well installation (including excavation, backfill, stone bedding, compaction), all necessary work to grade, clear, and prepare the site in accordance with the detailed site plan, fencing and gates, construction of the access road, pumps, bypass assembly, electrical work, control panels, site lighting, coordination as required for the installation and delivery of pumps, materials, electrical and mechanical equipment, coordination as necessary with the electrical service provider to provide the required electrical service to the lift station site, installation of piping and equipment, labor, materials, equipment, and all other necessary work required to furnish a complete installation as specified herein and shown on the Contract Drawings.

D-20 SUBMERSIBLE LIFT STATION

A. Payment for the submersible lift station as described herein shall be made at the lump sum unit price contained in the Bid Form. Payment shall include all necessary piping, fittings, wet well installation (including excavation, backfill, stone bedding, compaction), all necessary work to grade, clear, and prepare the site in accordance with the detailed site plan, fencing and gates, construction of the access road, pumps, bypass assembly, electrical work, control panels, site lighting, coordination as required for the installation and delivery of pumps, materials, electrical and mechanical equipment, coordination as necessary with the electrical service provider to provide the required electrical service to the lift station site, hoist assembly and wiring, valve vault, installation of piping and equipment, labor, materials, equipment, and all other necessary work required to furnish a complete installation as specified herein and shown on the Contract Drawings.

D-21 LIFT STATION ENCLOSURE

A. Payment for furnishing and installing the enclosure for the specified lift station shall be made at the lump sum unit price contained in the Bid Form. All items necessary to provide a complete enclosure, including but not limited to electrical work, fans, vents, lighting, attachment to the slab, and all labor, equipment, materials, and all other necessary work required to furnish a complete installation as specified herein and shown on the Contract Drawings shall be included in the unit price bid.

D-22 REMOTE TELEMETRY SYSTEM

A. Payment for furnishing and installing the remote telemetry (SCADA) system for the specified lift station shall be made at the lump sum price contained in the Bid Form. Payment shall include all necessary electrical work, necessary coordination with the PWC Lift Station Department, programming, testing, installation of the antennae, concrete foundation for the antennae, and necessary control panel, and all other labor, materials, and equipment as specified within these Contract Documents and as required by PWC to

provide a working remote telemetry system capable of interacting with the existing PWC lift station remote telemetry system.

D-23 <u>LIFT STATION STANDBY POWER</u>

A. Payment for furnishing and installing the emergency generator for the specified lift station shall be made at the lump sum unit price contained in the Bid Form. Payment shall include the emergency generator as specified within these Contract Documents, all necessary electrical, mechanical, and site work, installation of conduit, concrete foundation, necessary coordination with the remote telemetry installer, and all other labor, materials, and equipment necessary to furnish a working standby power system as specified within these Contract Documents.

D-24 ABANDON AERIAL SEWER CROSSING

A. Abandonment of existing aerial sewer crossings shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all costs to remove and properly dispose of the existing aerial crossing. Work shall include cutting and plugging the existing aerial sewer main at the existing manhole and bridge abutment, removal of the existing pipe, removal of the existing hangars, pilings, proper disposal of the materials, all necessary coordination with PWC, and all necessary materials, labor, equipment, and incidentals to complete the work.

D-25 ABANDON & GROUT FILL EXISTING SEWER

A. Payment under this item shall include all necessary costs to grout fill the existing sewer mains to be abandoned. Work shall include all costs to plug the sewer mains at the manholes, hoses, pumps, fittings, grout, and all labor, materials, equipment, and incidentals necessary to complete the work. Grouting of the sewer mains shall occur after PWC has accepted the new sewer main and laterals.

D-26 ABANDON EXISTING MANHOLE

A. Abandonment of existing manholes shall be measured by actual count, complete, in place, and payment will be made at the applicable unit price bid as listed in the Bid Form. Payment under this item shall include all necessary costs to abandon existing manholes as indicated on the plans. Work shall include all costs to remove the manhole cone, excavation, backfill of the manhole with select material or flowable fill, dewatering, removal and disposal of unsuitable material off site, proper disposal of the abandoned manhole, compaction, and all labor, materials, equipment, and incidentals necessary to complete the work. Abandonment of the existing manholes shall be completed after the sewer mains have been grout filled.

D-27 BORE AND JACK SEWER MAIN

A. Payment under this item shall include all necessary costs to install the casing and carrier pipe in accordance with the project requirements. Work shall include all costs for excavation, shoring, removal and disposal of excess unsuitable material off site, bedding material, horizontal and vertical controls, bore steering mechanisms, steel casing, casing spacers, concrete grouting and closures, installation of the restrained joint ductile iron carrier pipe, backfill, compaction, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall comply with all requirements for

construction within the right-of-ways of the applicable permitting authority.

D-28 BORE AND JACK SEWER LATERALS

A. Payment under this item shall include all necessary costs to install the casing and carrier pipe in accordance with the project requirements measured by actual count, complete, in place and payment will be made at the applicable unit price bid as listed on the bid form. Work shall include all costs for excavation, shoring, removal and disposal of excess unsuitable material off site, bedding material, horizontal and vertical controls, bore steering mechanisms, steel casing, casing spacers, concrete grouting and closures, installation of the restrained joint ductile iron carrier pipe, backfill, compaction, and all labor, materials, equipment, installation of the lateral at the specified line and grade, and incidentals necessary to complete the work. Laterals will not be considered for payment until they are installed per PWC Standards.

D-29 FURNISH AND INSTALL CAM-LOCK RING & COVER

A. Payment under this item shall include all costs necessary to furnish and install camlock ring and cover on an existing manhole. Measurement shall be based on the actual number installed. Payment shall be made at the contract unit price per each. The unit price shall include removal and disposal of the existing ring and cover, any existing grade rings or masonry adjustment, any necessary excavation to remove and/or install the ring and cover or any manhole sections, preparation of the concrete surface as required, installation of the ring and cover shall be in accordance with PWC standard details, clean-up and proper disposal of all debris and excess material and all labor, materials, tools, and equipment necessary to complete the work.

D-30 RESTRAINED JOINT DUCTILE IRON SEWER MAIN IN CASING (OPEN CUT)

A. Payment under this item shall include all necessary costs to install the specified casing and carrier pipe using open cut method in accordance with the project requirements. Payment per linear foot shall be made at the applicable unit price as indicated on the Bid Form. Work shall include all costs for excavation, shoring, sawcutting and removal of pavement, removal and disposal of excess unsuitable material off site, bedding material, steel casing, casing spacers, concrete grouting and closures, installation of the restrained joint ductile iron carrier pipe, backfill, compaction, and all labor, materials, equipment, and incidentals necessary to complete the work. The Contractor shall comply with all requirements for construction within the right-of-ways of the applicable permitting authority.

D-31 FURNISH AND INSTALL TEMPORARY MANHOLE

A. Payment under this item shall include all costs necessary to furnish and install any temporary manholes as specified on the plans. Payment shall be made at the applicable unit prices for each size and pay depth as indicated on the Bid Form. Work shall include all costs for excavation, backfill, removal and disposal of unsuitable material off-site, linings, inverts, pipe slides, dewatering, compaction, cutting and removal of pavement, proper disposal of waste, stone bedding, installation of the manhole in accordance with PWC standards, installation of the specified frame and cover, concrete collar, and all labor, materials, equipment and incidentals necessary to complete the work. Work shall also include all costs necessary to maintain sanitary sewer service during construction to include, but not limited to, maintenance of the manhole and laterals, pumping, hauling and

proper disposal of waste for the duration of use of the temporary manhole.

D-32 HYDROSTATIC TESTING (SANITARY SEWER)

A. This item shall be measured by the linear feet of gravity sanitary sewer main, force main, and/or low pressure systems, that are required to be hydrostatically pressure tested in accordance with the State of North Carolina and PWC standards. Testing of sanitary sewer laterals connected to mains or directly to manholes are considered incidental and will not be measured and paid separately. Work shall include all costs associated with the testing to include furnishing test equipment, installation and removal of blow offs, and all labor, materials, equipment, and any other incidentals necessary to complete the testing. Payment under this line item shall not be made until all required tests are successfully completed. The contractor shall schedule testing and fully cooperate with the PWC Project Coordinator and/or other PWC representative as required by the contract specifications.

D-33 <u>FURNISH AND INSTALL AERIAL CLASS 53 RJDIP SANITARY SEWER CROSSING (INCLUDING PIERS)</u>

A. This item shall be measured by actual linear feet of unburied gravity sanitary sewer installed, complete, in place, measured horizontally along the centerline of the top of the pipe. Payment shall be made at the applicable unit price for each pipe diameter as listed in the Bid Form. Payment under this item shall include all work and costs necessary to furnish and install the gravity sanitary sewer pipe as indicated on the plans, H-piles driven to refusal or to design depths, drilled concrete piers to design depth, reinforced concrete bents, the bent plate, structural anchors, and anchor blocks, fittings, coatings, encasement pipe ports, spacers, end seals, concrete supports, piers, cradles, restraints, polyethylene casing where shown on the plans, carrier pipe at the specified line and grade, dewatering, testing, inspection in accordance with the design specifications and PWC standards. Work shall also include removal and disposal of excess material off site, and all labor, materials, equipment, and incidentals necessary to complete the work.

D-34 FURNISH AND INSTALL STANDARD MANHOLE VENTS

A. This item shall be measured by actual count, complete and in place. Payment will be made at the applicable unit price as listed in the Bid Form. Payment under this item shall include all costs necessary to install the specified manhole vents as indicated on the plans and in accordance with PWC Standards. Work shall include materials, fabricating, and all equipment, tools, labor, and incidentals necessary to complete the work. Installation shall be accomplished in accordance with PWC Standard Detail S.17 and with PWC Standard Specifications 02730 Sanitary Sewer Systems.

D-35 INSTALL X FOOT TALL XX FOOT WIDE DOUBLE GATE

A. Measured and paid in units of each for the number of gates erected on the project. Double gates will be measured as one gate. The Contractor shall furnish and install double gates as indicated on the plans and in accordance with PWC Standards. The Contractor shall match existing fence material or install the material indicated on the plans or in the special conditions. Work shall include all materials, equipment, tools, labor, and incidentals necessary to complete the work. Posts, braces, concrete, gates, fittings, and any other materials necessary to complete the work. Installation shall be in accordance with PWC Standard Detail M.17 and should match the existing fence material or material indicated in the plans.

01300 - SUBMITTALS

GENERAL

This section specifies the means of all submittals. All submittals shall be submitted to Fayetteville Public Works Commission. A general summary of the types of submittals and the number of copies required is as follows:

| Copies to PWC | Type of Submittal |
|---------------|----------------------------|
| 5 | Administrative Submittals |
| 3 | Construction schedule |
| 5 | Shop drawings |
| 5 | Product samples |
| 1 | Preconstruction Video |
| 5 | Project Sign Sketch |
| 5 | Certificates of compliance |
| 5 | Warranties |

SUBMITTAL PROCEDURES

Transmit each submittal with a form acceptable to Fayetteville Public Works Commission, clearly identifying the project, the Contractor, the enclosed material and other pertinent information specified in other parts of this section. The Contractor shall specifically identify variations from the Contract Documents and/or any Product or system limitations which may be detrimental to successful performance of the completed Work.

The Contractor shall revise and resubmit submittals as required, identify all changes made since previous submittals. Re-submittals shall be noted as such and shall direct attention to the revisions made. Re-submittals shall be handled in the same manner as the first submittal.

The Contractor shall distribute copies of reviewed submittals to concerned parties, with instructions to the party to promptly report any inability to comply with provisions.

ADMINISTRATIVE SUBMITTALS

All administrative submittals shall be prepared and submitted in accordance with the Submittal Checklist provided in these Contract Documents. All Preconstruction Administrative submittals must be submitted and approved prior to the release of Contractor's first Application for Payment. Construction Administrative Submittals must be submitted and approved prior to the release of monthly pay applications. Post Construction Administrative Submittals must be submitted and approved prior to the release of the Contractor's Final Application for Payment.

CONSTRUCTION SCHEDULE

The construction schedule shall be prepared and submitted in accordance with Specification Section 01310. Three (3) copies of the schedule showing the first forty-five (45) calendar days of the work shall be submitted within 10 calendar days after the date of the Notice to Proceed. Three (3) copies of the proposed construction schedule for the entire Contract duration shall be submitted within thirty (30) calendar days after the date of the Notice to Proceed.

The construction schedule shall be revised to reflect comments by Fayetteville Public Works Commission and updated monthly, depicting progress to the last day of the month. Two (2) copies shall be submitted to the Project Engineer no later than the Monday prior to each Monthly Progress Meeting.

Changes to the schedule shall be accompanied by a letter of explanation with appropriate reference and revision date on the schedule.

SHOP DRAWINGS

The Contractor shall submit for review shop drawings for concrete reinforcement, structural details, materials fabricated especially for this Contract, and/or materials for which such Drawings are specified or specifically requested by Fayetteville Public Works Commission.

Shop drawings shall show the principal dimensions, weight, structural and operating features, type and/or brand of finish or shop coat, grease fittings, etc., depending on the subject of the Drawings.

When so specified, or if considered by Fayetteville Public Works Commission to be acceptable, the manufacturer's specifications, catalog data, descriptive matter, illustrations, etc. may be submitted for review in place of shop drawings. In such case, the requirements shall be as specified for shop drawings, insofar as applicable.

The Contractor shall be responsible for the prompt submittal of all shop drawings so that there shall be no delay to the Work due to the absence of such Drawings. Fayetteville Public Works Commission will review and return the shop drawings within thirty (30) calendar days of receipt of such Drawings. Two (2) sets of the reviewed shop drawings will be returned to the Contractor by regular mail.

Project delays caused by failure to submit, or rejection of submittals shall not be cause for additional compensation or Contract time extensions.

All shop drawings shall be submitted to Fayetteville Public Works Commission through the Contractor. The Contractor is responsible for obtaining shop drawings from his subcontractors and returning reviewed Drawings to them. All shop drawings shall be prepared on standard size, 24-inch by 36-inch sheets, or smaller. All Drawings shall be clearly marked with the name of the project, Fayetteville Public Works Commission, Contractor, and pay item to which the drawing applies. Drawings shall be suitably numbered and stamped by the Contractor. Each shipment of Drawings shall be accompanied by a letter of transmittal giving a list of the drawing numbers and the names mentioned above.

PRODUCT DATA

Where manufacturer's publications in the form of catalogs, brochures, illustrations, or other data sheets are submitted in lieu of prepared shop drawings, such submission shall specifically indicate the particular item offered. Identification of such items and relative pertinent information shall be made with indelible ink. Submissions showing only general information will not be accepted.

Product data shall include materials of construction, dimensions, performance characteristics and capacities, etc.

SAMPLE WARRANTIES

When warranties are called for, a sample of the warranty shall be submitted with the shop drawings. The sample warranty shall be the same form that will be used for the actual warranty.

WORK PRIOR TO REVIEW

No material or equipment shall be purchased, fabricated especially for this Contract, or delivered to the project site until the required shop drawings have been submitted, processed and marked either "APPROVED" or "APPROVED AS NOTED". All materials and Work involved in the construction shall be as represented by said Drawings.

The Contractor shall not proceed with any portion of the Work for which the design and details are dependent upon the design and details of equipment for which submittal review has not been completed.

Only submittals which have been checked and corrected should be submitted to the Contractor by his subcontractors and vendors. Prior to submitting shop drawings to Fayetteville Public Works Commission, the Contractor shall check thoroughly all such Drawings to verify that the subject matter conforms to the Contract Documents in all respects. Drawings which are correct shall be signed and dated by the Contractor's representative checking the submittal and shall include the following statement: "This shop drawing has been reviewed and approved with respect to means, methods, techniques, sequences and operations of construction, safety precautions and programs incidental thereto. The Contractor also warrants that this shop drawing complies with the Contract Documents and comprises no variation thereto." Once correct, they shall be submitted to the Project Engineer for Review. Drawings submitted without this statement shall be returned to the Contractor un-reviewed.

The review of shop drawings will be general and shall not relieve the Contractor of the responsibility for details of design, dimensions, etc., necessary for proper fitting and construction of the Work required by the Contract Documents and for achieving the specified performance.

For submissions containing departures from the Contract Documents, the Contractor shall include proper explanation in his letter of transmittal. Should the Contractor submit for review equipment that requires modifications to the structures, piping, layout, etc. detailed on the Drawings, he shall also submit for review details of the proposed modifications. If such equipment and modifications are accepted, the Contractor, at no additional cost to Fayetteville Public Works Commission, shall do all Work necessary to make such modifications.

SUBSTITUTIONS

Whenever a particular brand or make of material, equipment, or other item is specified, or is indicated in these Contract Documents, it is for the purpose of establishing a standard of quality, design, and type desired and to supplement the detailed specifications. Any other brand or make which, in the opinion of Fayetteville Public Works Commission, is equivalent to that specified or indicated may be offered as a substitute subject to the following provisions:

- a. Contractor shall submit for each proposed substitution sufficient details, complete descriptive literature, and performance data together with samples of the materials, where feasible, to enable Fayetteville Public Works Commission to determine if the proposed substitution is equal.
- b. Contractor shall submit certified tests, where applicable, by an independent laboratory attesting that the proposed substitution is equal.
- c. A list of installations, to include the owner's name and phone number, where the proposed substitution is equal.
- d. Where the acceptance of a substitution requires revision or redesign of any part of the Work, all such revision and redesign, and all new Drawings and details required therefore, shall be provided by the Contractor at his own cost and expense, and shall be subject to review of Fayetteville Public Works Commission.
- e. In all cases Fayetteville Public Works Commission shall be the sole judge as to whether a proposed substitution is to be accepted. The Contractor shall abide by Fayetteville Public Works Commission's decision when proposed substitute items are judged to be unacceptable and shall in such instances furnish the item, or substitute, as specified. No substitute items shall be used in the Work without written acceptance of Fayetteville Public Works Commission. Fayetteville Public Works Commission reserves the right to reject any proposed changes and/or substitutions at their sole discretion and is under no obligation to justify the decision.
- f. Acceptance of any proposed substitution shall in no way release the Contractor from any of the provisions of the Contract Documents.

Each submittal shall be complete in all aspects incorporating all information and data required to evaluate the products' compliance with the Contract Documents. Partial or incomplete submissions shall be returned to the Contractor without review.

Shop Drawing Distribution: The Contractor shall submit a minimum of five (5) copies of all shop drawings to Fayetteville Public Works Commission for review. Shop drawings will be reviewed, stamped and distributed with the appropriate box checked either "APPROVED", "APPROVED AS NOTED", "NOT APPROVED" or "REVISE AND RESUBMIT". Fayetteville Public Works Commission shall return three (3) copies to the Contractor and retain two (2) copies.

If the Contractor requires additional copies of returned shop drawings, he shall include extra Drawings in his original submittal. Fayetteville Public Works Commission will process the Drawings and return them to the Contractor.

PRODUCT SAMPLES

Contractor shall furnish for review all product samples as required by the Contract Documents or requested by Fayetteville Public Works Commission to determine compliance with the specifications.

Samples shall be of sufficient size or quantity to clearly illustrate the quality, type, range of color, finish or texture and shall be properly labeled to show complete project identification, the nature of the material, trade name of manufacturer and location of the Work where the material represented by the sample will be used.

Samples shall be checked by the Contractor for conformance to the Contract Documents before being submitted to Fayetteville Public Works Commission and shall bear the Contractor's stamp certifying that they have been so checked. Transportation charges on samples submitted to Fayetteville Public Works Commission shall be prepaid by the Contractor.

Fayetteville Public Works Commission's review will be for compliance with the Contract Documents, and comments will be transmitted to the Contractor with reasonable promptness.

Acceptable samples will establish the standards by which the completed Work will be judged.

PRECONSTRUCTION VIDEO

The Contractor shall document pre-existing conditions on the project site in accordance with these Contract Documents. This shall be done prior to Work beginning in the area. **The video shall** be submitted to the Project Engineer before the first payment application can be released.

PROJECT SIGN SKETCH

Prior to first application for payment, Contractor shall erect the specified number of project signs consisting of 4 feet -0 inch by 8 feet -0 inch by $\frac{3}{4}$ inch exterior grade plywood and hardwood edging on all four edges. The signs shall be mounted on two 4 inch by 4-inch wood posts. Posts shall be 6 feet -0 inch on centers, and the center of the sign shall be located midway between posts. Top of sign shall be 6 feet -0 inch above ground, and posts shall extend 2 feet -0 inch below ground level (or deeper if required to ensure stability). The plywood shall be painted white, front and back. Hardwood edging and posts shall be painted black. All lettering shall be black and wording on the signs shall be as follows:

FAYETTEVILLE PUBLIC WORKS COMMISSION PROJECT # FAYETTEVEILLE ANNEXATION PHASE V, PROJECT XII, CONSTRUCTION AREA 27- CLIFFDALE FOREST

PROJECT NAME

ENGINEERING FIRM (or)
NAME OF FIRM
(Depending on the firm)

NAME OF GENERAL CONTRACTOR GENERAL CONTRACTOR

ANNEXATION INFORMATION HOTLINE 910-483-1382

FAYETTEVILLE PUBLIC WORKS COMMISSION PROJECT ENGINEER

- The project sign(s) shall meet requirements of all local codes and ordinances.
- The Contractor shall submit a simple sketch to the Project Engineer for approval prior to ordering or erecting the sign. The submitted sketch shall show heights and spacing of lettering.

RECORD DRAWINGS

Upon completion of the Work, the Contractor shall provide two complete sets of drawings recording all changes to the work to indicate actual installation. Changes shall be noted in legible red letters. These changes shall include but are not limited to the following:

- 1) Change in lateral location
- 2) Change in pipe material
- 3) Change in manhole location
- 4) Location of ductile iron installed on existing AC water mains
- 5) Size, depth, and installed elevations of mains, laterals, force mains, and manholes
- 6) Location of valves, blow-offs, and other appurtenances

Completion of the Contractor's record drawings is a specific contract requirement, and final payment will not be made until these drawings and project manual (as required) have been submitted to and approved by the Project Engineer.

CERTIFICATES OF COMPLIANCE

Copies of certificates of compliance and test reports shall be submitted for requested items to Fayetteville Public Works Commission prior to request for payment.

WARRANTIES

Original warranties, called for in the Contract Documents, shall be submitted to Fayetteville Public Works Commission. When warranties are required for an item, warranty shall be submitted prior to request for payment of that item.

When warranties are requested, a sample of the warranty to be provided shall be submitted with, and considered part of, the shop drawings.

The Contractor shall warrant to Fayetteville Public Works Commission that all material and labor used in the construction are covered by his warrantee for a minimum of a one (1) year period (unless otherwise noted in these Contract Documents) upon approval and acceptance by Fayetteville Public Works Commission. The Contractor shall replace or repair defects at no cost to Fayetteville Public Works Commission during the warrantee period. No visible or potential leakage shall be allowed during the warrantee period.

END OF SECTION

DIVISION 1 01310 - CONSTRUCTION SCHEDULE

PART 1 GENERAL

1.01 WORK INCLUDED:

A. This section specifies requirements and procedures in preparing and updating construction schedules and reports for planning, coordinating, executing and monitoring the progress of the work. The construction work shall be scheduled to be completed within the specified duration of the Contract.

1.02 RELATED WORK SPECIFIED ELSEWHERE

- A. Special Provisions
- B. General Conditions
- C. Submittals

1.03 SCHEDULING RESPONSIBILITIES

- A. The construction schedule will be used to monitor job progress. The Contractor will be responsible for providing all information concerning the sequencing, logic and durations of planned activities. The Contractor will be responsible for providing monthly update information on logic changes, percent complete, actual start and finish dates and duration changes. The Contractor will be required to produce the monthly, computerized printout of the schedule updates.
- B. Assembling the initial schedule in hand drawn or computer-generated (preferred) form is the responsibility of the Contractor.
- C. It should be clearly understood that the initial schedule and all update information must be provided by the Contractor and that this information is a representation of the best efforts of the Contractor and his subcontractors as to how they envision the work to be accomplished. Similarly, all progress information to be provided by and through the Contractor must be an accurate representation of his or his subcontractors' or suppliers' actual performance. The schedule shall at all times remain an accurate reflection of the Contractor's actual or projected sequencing of the work. Once accepted, adherence to the schedule shall be obligatory upon the Contractor and his subcontractor for the work under this Contract. Owner may require the Contractor to revise the schedule if, in the Project Engineer's judgment, the schedule does not accurately reflect the actual extension of the work, or is in violation of any provision of the Contract Documents. The Contractor shall provide the necessary information required to revise the schedule as often as is necessary during the course of performance of the work without additional cost to the Owner.

1.04 PROGRESS OF WORK

A. The work shall be started on the date indicated in the Notice to Proceed and shall be executed with such progress as may be required to prevent delay to other

contractors or to the general completion of this project. The Contractor shall at all times, schedule and direct his work so that it provides an orderly progression of the work to completion within the specified Contract Time. The Contractor shall account for traffic control requirements, access of citizens within the work area and the requirements for timely restoration.

- B. The Contractor agrees that, whenever it becomes apparent from the current monthly schedule update that delays to the planned progress of work have resulted and these delays are through no fault of the Owner and hence, the Contract completion date will not be met, or when so directed by the Project Engineer, he will prepare a recovery schedule outlining steps to recover time and to complete the project on schedule.
- C. The Contractor shall submit for review a written statement of the steps he intends to take, to remove or arrest the delay to the schedule. The Contractor shall promptly provide such level of effort at no additional cost to the Owner. In addition, should schedule delays persist; the Contractor's surety will be asked to attend a schedule update meeting.
- D. Failure of the Contractor to comply with the requirements of this provision shall subject him to, at the Owner's sole discretion, withholding, in partial or in total, payments otherwise due the Contractor for work due under this Contract. The Contractor agrees that any withholding of monies is not a penalty for noncompliance, but is an assurance for the Owner that funds will be available to implement these requirements should the Contractor fail to do so, since failure of the Contractor to comply with these requirements shall mean that the Contractor failed to execute the work with such diligence as to ensure its completion within the time for completion.

PART 2 CONSTRUCTION SCHEDULE

2.01 SCHEDULE REQUIREMENTS

- A. The schedule shall show the order and interdependence of activities and the sequence in which the work is to be accomplished as planned by the Contractor. The schedule shall show how the start date of a given activity is dependent on the completion date of preceding activities how its completion restricts the start of succeeding activities. A time scaled precedence format will be followed. The schedule shall indicate the start date, completion date, and duration (in days), of each activity.
- B. The Schedule Activities shall be developed into two major groups:
 - 1. Construction Activities Construction activities will be physical work activities that describe how the job will be constructed. Work shall include planned restoration and paving.
 - 2. Post Construction Testing, Start-up, Training and Close-out Activities for this group shall include all work required satisfying appropriate specification requirements sections and meeting the requirements of final completion. There are at least three (3) mandatory activities: Punch list, Final Walkthrough and Project Complete.
- C. The Contractor shall break the work into activity durations of one to twenty (1 to 20) working days each, except for non-construction activities (such as procurement of materials and delivery of equipment) and other activities that may require longer durations. To the extent feasible, activities related to a specific physical or geographic area of the project should be grouped on the schedule for ease of understanding and simplification. The selection and number of activities shall be subject to the review of the Project Engineer.
- D. Each activity on the schedule shall have indicated for it the following:
 - 1. Construction activities will be divided by easily recognizable division points such as stationing or street names, area of work, etc.
 - 2. A brief description of the activity will be included. If this description is not definitive, a separate listing of each activity and a descriptive narrative may be required.
 - 3. Where the contractor intends to perform work concurrently, a resource or crew identifier will be assigned to the activity to indicate parallel paths.
 - 4. Established PWC holidays and other non-work days will be excluded from the schedule.

- E. Failure to include on the schedule any element of work required for the performance of this Contract shall not excuse the Contractor from completing all work required within the applicable Contract Time.
- F. A schedule which shows a completion of any portion of the construction work prior to the Contract Time dates may be accepted but in no event shall be acceptable as a basis for a claim for any delay against the Owner by the Contractor.

PART 3 SCHEDULE OF SUBMITTALS

3.01 SCHEDULE IMPLEMENTATION

- A. Within ten (10) calendar days after the Notice to Proceed, the Contractor shall submit up to three (3) prints of a schedule showing the first forty-five (45) calendar days of the work. The Contractor will revise and resubmit the forty-five (45) day schedule until it is acceptable.
- B. Within (30) calendar days after the Notice to Proceed, the Contractor shall submit three (3) copies of their proposed construction schedule for the entire Contract duration.
- C. The Contractor may submit a schedule on disk in a format wholly compatible with Microsoft Project. Submission of an electronic schedule does not preclude any other of the aforementioned individual activity requirements.
- D. If a review of the submitted schedule indicates a work plan that will not complete the work within the Contract time, it shall be the responsibility of the Contractor to revise the schedule as required and resubmit it until it is acceptable. Failure by the Contractor to submit an acceptable schedule may, at the Owner's sole discretion, be cause for the withholding of any partial payment(s) otherwise due under the Contract.
- E. Acceptance of the schedule shall not constitute a representation by the Owner that the work can be completed as shown on the schedule.

3.02 SCHEDULE UPDATES

A. The Contractor shall submit a Schedule Update on the Monday prior to the monthly progress meeting, (or as directed by the Project Engineer), to allow the Project Engineer to review the schedule. The schedule shall be up-to-date as of the previous Friday or as directed by the Project Engineer. Actual progress of the previous month shall be recorded and future activities will be reviewed. The duration of activities and their logical connections may be revised as needed. Decisions made at these meetings and agreed to by all parties are binding with the exception that no contractual completion dates will be modified without formal

written requests and acceptance as specified in the Contract Documents. The Contractor must provide the following information for each update at a minimum:

- 1. Actual start and finish dates for all completed activities.
- 2. Actual start dates for all started but incomplete activities including remaining durations and/or percent completes.
- 3. Revisions in the logic, critical path or resource assigned to an activity that would affect the anticipated early start of all activities not yet started.
- 4. Any approved extension of Contract time shall be included in the next monthly updating of the schedule.
- B. Provide a Monthly Progress Status Report that provides the following items:
 - 1. Summarized revisions made to the Construction Schedule since the previous submittal.
 - 2. Work anticipated to be started during the next period, including those activities already in progress.
 - 3. Problem areas, anticipated delays, and the impact on the schedule.
 - 4. Corrective action.
 - 5. The effect of changes on schedules of other prime Contractors in adjacent work areas.
- C. Failure to provide update information listed above, or failure to attend progress meetings may result in the Owner withholding partial payments.

END OF SECTION

DIVISION 1 01400 - QUALITY CONTROL

QUALITY ASSURANCE

Quality: All materials shall be new and correctly designed, and shall conform to the requirements outlined in these Contract Documents. They shall be standard first-grade quality produced by expert workmen and be intended for the use for which they are offered. Materials which, in the opinion of Fayetteville Public Works Commission, are inferior or of a lower grade than indicated, specified, or required will not be acceptable.

Source Limitations: To the greatest extent possible for each unit of Work, the Contractor shall provide products, materials, or equipment from a single manufacturer.

Compatibility of Options: If the Contractor cannot obtain all necessary products, materials, and/or equipment from a single manufacturer, the Contractor shall submit compatible products, materials, and/or equipment to Fayetteville Public Works Commission for review and approval. Once Fayetteville Public Works Commission has issued approval of the proposed products, materials, and/or equipment, the Contractor shall only utilize that manufacturer's products, materials, and/or equipment, unless otherwise approved in writing by Fayetteville Public Works Commission.

QUALITY CONTROL

Quality control is the sole responsibility of the Contractor and shall include the activities of his Subcontractors and all suppliers as required.

TESTING SERVICES

The Contractor shall cooperate with Fayetteville Public Works Commission's Consultant performing required testing and provide equipment, access, or other means required at no additional expense to Fayetteville Public Works Commission. The Contractor shall be responsible for coordinating testing with the PWC Project Coordinator. The Contractor shall be responsible for all costs incurred by Fayetteville Public Works Commission's Consultant when scheduled testing cannot be performed.

Fayetteville Public Works Commission shall employ and pay for the services of an independent laboratory for specified testing as outlined in these Contract Documents, with the following exceptions:

- If Laws and Regulations of any public body having jurisdiction specifically require any part of the Work to be tested, inspected, or approved by an employee or other representative of that public body, the Contractor shall be responsible for arranging and obtaining such inspections and/or approvals. The Contractor shall bear all costs associated with the required testing, inspections, and/or approvals, and shall furnish Fayetteville Public Works Commission all required documentation that the required testing, inspection, and/or approvals have been obtained.
- If any part of the Work is found to be defective and not in compliance with the Contract Documents, the Contractor shall be responsible for all subsequent testing necessary to

prove that the Work has been brought into compliance. Any necessary testing to ensure compliance shall be directed by the PWC Project Coordinator and/or PWC Project Engineer.

- When scheduled testing by Fayetteville Public Works Commission's Consultant cannot be performed.
- Arranging and obtaining any required inspections, testing, or approvals required in connection with Fayetteville Public Works Commission's acceptance of a material supplier, or equipment proposed to be incorporated into the Work, or materials, mix designs, etc. submitted for approval prior to purchase for incorporation into the Work. All inspections, tests, and approvals shall be performed by organizations acceptable to Fayetteville Public Works Commission.

PRODUCT EVALUATION

Testing shall be accomplished as deemed necessary by Fayetteville Public Works Commission to ensure that the products conform to the requirements of the Contract Documents.

The work or actions of the testing laboratory shall in no way relieve the Contractor of his obligations under the Contract. The laboratory testing work will include such inspections and testing required by the Contract Documents, existing laws, codes, ordinances, etc. The testing laboratory will have no authority to change the requirements of the Contract Documents, nor perform, accept or approve any of the Contractor's Work.

The Contractor shall allow Fayetteville Public Works Commission ample time and opportunity for evaluation and testing materials to be used in the Work. The Contractor shall advise Fayetteville Public Works Commission promptly upon placing orders for materials so that arrangements may be made, if desired, for evaluation before shipment from the place of manufacture. The Contractor shall at all times furnish Fayetteville Public Works Commission and its representatives, facilities including labor, and allow proper time for evaluation and testing materials, and workmanship. The Contractor must anticipate that possible delays may occur due to the necessity of materials being inspected and accepted for use. The Contractor shall furnish, at his own expense, all samples of materials required by Fayetteville Public Works Commission for testing, and shall make his own arrangements for providing water, electric power, or fuel for the various evaluation and tests of structures and materials.

Fayetteville Public Works Commission will bear the cost of all tests, evaluation, or investigations undertaken by the order of the PWC Project Engineer for the purpose of determining conformance with the Contract Documents if such tests, evaluation, or investigations are not specifically required by the Contract Documents, and if conformance is ascertained thereby. Whenever nonconformance is determined by Fayetteville Public Works Commission as a result of such tests, evaluation, or investigations, the Contractor shall bear the full cost of any additional tests, evaluations and investigations, which are ordered by Fayetteville Public Works Commission to ascertain subsequent conformance with the Contract Documents.

EVALUATION AT PLACE OF MANUFACTURE

Unless otherwise specified, all products and materials shall be subject to evaluation by Fayetteville Public Works Commission at the place of manufacture.

The presence of Fayetteville Public Works Commission at the place of manufacture however, shall not relieve the Contractor of the responsibility for furnishing products, materials, and equipment which comply with all requirements of the Contract Documents. Compliance is a duty of the Contractor, and said duty shall not be avoided by any act or omission on the part of Fayetteville Public Works Commission.

SAMPLING AND TESTING

Unless otherwise specified, all sampling and testing shall be in accordance with the methods prescribed in the current standards of the ASTM, as applicable to the class and nature of the 5 c or materials considered. However, Fayetteville Public Works Commission reserves the right to use any generally-accepted system of sampling and testing which will ensure that the quality of the workmanship is in full accord with the Contract Documents.

Any waiver by Fayetteville Public Works Commission of any specific testing or other quality assurance measures shall not be construed as a waiver of any requirements of the Contract Documents. Fayetteville Public Works Commission may require a guarantee of substantial performance and/or a performance bond to ensure any necessary corrective or remedial Work, should a waiver be granted.

Fayetteville Public Works Commission reserves the right to make independent investigations and tests. Failure of any portion of the Work to meet any of the requirements of the Contract Documents, shall be reasonable cause for Fayetteville Public Works Commission to require the removal or correction and reconstruction of any such work in accordance with the Contract Documents. In addition to any other evaluation, observation or quality assurance provisions that may be specified, Fayetteville Public Works Commission shall have the right to independently select, test, and analyze, at their expense, additional test specimens or any or all of the materials to be used. Results of such tests and analyses shall be considered along with the tests or analyses made by the Contractor to determine compliance with the applicable specifications for the materials so tested or analyzed. The Contractor shall be responsible for all costs of removal, correction, and reconstruction or repair of any such Work that fails to meet the requirements of the Contract Documents.

SITE INVESTIGATION AND CONTROL

The Contractor shall verify all dimensions in the field and shall check field conditions continuously during construction. The Contractor shall be solely responsible for any inaccuracies built into the Work due to their failure to comply with this requirement.

The Contractor shall inspect related and appurtenant Work and shall report in writing to Fayetteville Public Works Commission any conditions which will prevent proper completion of the Work. Failure to report any such conditions shall constitute acceptance of all site conditions, and any required removal, repair, or replacement caused by unsuitable conditions shall be performed by the Contractor at their sole cost and expense.

RIGHT OF REJECTION

Fayetteville Public Works Commission shall have the right, at all times, to reject any articles or materials to be furnished hereunder which, in any respect, fail to meet the requirements of the Contract Documents, regardless of whether the defects in such articles or materials are detected at the point of manufacture or after completion of the Work. If Fayetteville Public Works Commission, through an oversight or otherwise, has accepted materials or Work which is defective or which is contrary to the Contract Documents, such materials, no matter in what stage or condition of manufacture, delivery, or erection, may be subsequently rejected by Fayetteville Public Works Commission.

The Contractor shall promptly remove rejected articles or materials from the Work after notification of rejection. All costs of removal and replacement of rejected articles or materials as specified herein shall be borne by the Contractor.

WATERTIGHTNESS OF STRUCTURES

It is the intent of these Contract Documents that all Work shall be performed as required by quality construction to ensure proper sealing so that groundwater and/or rainwater will not leak into any repaired collection line, service lateral, or manhole.

The Contractor shall provide at its own expense all labor, material, temporary bulkheads, pumps, water, measuring devices, etc., necessary to perform the required tests.

HYDRAULIC UPLIFT ON STRUCTURES

The Contractor shall be completely responsible for any pipelines or manholes that may become buoyant before the Work is completed and accepted. The Contractor shall take all necessary steps to prevent any structures from becoming buoyant. Damage to any structures due to floating or flooding shall be repaired or replaced at the Contractor's expense.

TIME OF OBSERVATION AND TESTS

Samples and test specimens required under these Contract Documents shall be furnished and prepared for testing in ample time for the completion of the necessary tests and analyses before said articles or materials are to be used. The Contractor shall furnish and prepare all required test specimens within the scope of the Contract. Except as otherwise provided in the Contract Documents, the performance and cost of the required tests will be the responsibility of Fayetteville Public Works Commission. However, the costs of any test which shows unsatisfactory results shall be borne by the Contractor. Whenever the Contractor is ready to backfill, bury, cast in concrete, or otherwise cover any Work under the Contract, Fayetteville Public Works Commission shall be notified not less than twenty-four hours in advance to request inspection before beginning any such Work of covering. Failure of the Contractor to notify Fayetteville Public Works Commission a minimum of twenty-four hours in advance of any such inspections shall be cause for Fayetteville Public Works Commission to order a delay in the Contractor's schedule to allow time for inspections. Any remedial or corrective Work required, and all costs of such delays, including its effect upon other portions of the Work, shall be borne by the Contractor.

*** END OF SECTION ***

DIVISION 1 01700 - PROJECT CLOSEOUT

GENERAL

The Contractor shall promptly remove from the vicinity of the completed Work, all rubbish, unused materials, concrete forms, construction equipment, temporary structures and facilities, construction signs, tools, scaffolding, materials, supplies and equipment which may have been used in the performance of the work. The Contractor shall broom clean paved surfaces and rake clean other surfaces of grounds. Final acceptance of the Work by Fayetteville Public Works Commission will be withheld until the Contractor has satisfactorily complied with the foregoing requirements for final cleanup of the project site.

The Contractor shall thoroughly clean all materials, equipment and structures; all marred surfaces shall be touched up to match adjacent surfaces.

The Contractor shall remove spatter, grease, stains, fingerprints, dirt, dust, labels, tags, packing materials and other foreign items or substances from interior and exterior surfaces, equipment, signs and lettering.

The Contractor shall remove paint, clean and restore all equipment and material nameplates, labels and other identification markings.

The Contractor shall maintain cleaning until project, or portion thereof, is accepted by the Public Works Commission.

The Contractor shall:

- A. Use only cleaning materials recommended by manufacturer of surface to be cleaned.
- B. Use each type of cleaning material on only those surfaces recommended by the cleaning material manufacturer.
- C. Use only materials which will not create hazards to health or property.

CLOSEOUT TIMETABLE

The Contractor shall establish dates for testing, acceptance periods, and on-site instructional periods (as required under this Contract). Such dates shall be established not less than one week (seven (7) calendar days) prior to beginning any of the foregoing items, to allow Fayetteville Public Works Commission and their authorized representative's sufficient time to schedule attendance at such activities.

FINAL SUBMITTALS

Before the final acceptance of the project, the Contractor shall submit to Fayetteville Public Works Commission certain records, certifications, etc., which are specified elsewhere in these Contract Documents. Missing, incomplete or unacceptable items, as determined by Fayetteville Public Works Commission, shall constitute grounds for withholding final payment to the Contractor. A partial list of such items appears below, but is shall be the Contractor's responsibility to submit any other items which are required in these Contract Documents:

- A. Written Test results of project components.
- B. Written guarantees, where required.
- C. Certificates of inspection and acceptance by local governing agencies having jurisdiction.
- D. Pre-construction photos (5" x 7").
- E. Releases from all parties who are entitled to claims against the subject project, property, or improvement pursuant to the provisions of law.

PUNCH LISTS

Final cleaning shall be scheduled upon completion of the project.

Fayetteville Public Works Commission will make their final inspection whenever the Project Coordinator has determined that the work is ready for the inspection. Any work not found acceptable and requiring cleaning, repair and/or replacement will be noted on the "Punch" list. Work that has been inspected and accepted by Fayetteville Public Works Commission shall be maintained by the Contractor, until final acceptance of the entire project.

Whenever the Contractor has completed the items on the punch list, he shall coordinate an inspection with the PWC Project Coordinator to verify that the punch list items have been satisfactorily completed. This procedure will continue until the entire project is accepted by Fayetteville Public Works Commission. The "Final Payment" will not be processed until the entire project has been accepted by Fayetteville Public Works Commission and all of the requirements in this Specification Section have been satisfied and any additional requirements as outlined in Section 01000 – Special Conditions of these Contract Documents.

TOUCH-UP AND REPAIR

The Contractor shall touch-up and repair damage to all existing facilities and surfaces. If in the opinion of Fayetteville Public Works Commission the touch-up work is not satisfactory, the Contractor shall repeat the item.

MAINTENANCE AND GUARANTEE

The Contractor shall comply with all maintenance and guarantee requirements of these Contract Documents.

Replacement of earth fill or backfill, where it has settled below the required finish elevations, shall be considered as a part of such required repair work, and any repair or resurfacing constructed by the Contractor which becomes necessary by reason of such settlement shall likewise be considered as a part of such required repair work unless the Contractor shall have obtained a statement in writing from the affected private owner or public agency releasing Fayetteville Public Works Commission from further responsibility in connection with such repair or resurfacing.

END OF SECTION
